



NCC

SWSM PROJECTS – UP – GORAKHPUR

Project Name : Survey, Design, Preparation of DPR, Construction, Commissioning and O&M for 10 years of Various Rural Water Supply Project in the State of Uttar Pradesh– Gorakhpur District
Client : SWSM/DWSM-UP-GKP
Consultant : Medhaj Techno Concept Pvt. Ltd.
Contractor : NCC Limited

Request For Inspection

RFI No:	SWSM-UP-GKP/N/S/Tw/125	Date And Time - 17/05/2022	9:40pm
Description:	Lowering of pipe with Assembly and filling gravel		
Location:	Block - Barhalganj GP - Sukul puri		
Preceding RFI No.	V.A		
Commencement of work:	18/05/2022		
Submitted By:	Ankit Salunkhe		
Signature:			
Designation:	J.E civil		
Concessionaire:	Proceed	Hold	
Name:			
Designation:			
Comments:	<p>① Fact delivery fact report not provide for MSERL.</p> <p>② H-frame. not available at site.</p> <p>③ pea gravel fact report not provided.</p>		


Signature
Contractor Representative



Signature
Consultant Representative


Signature
Client Representative

NCC SWSM PROJECTS – UP – GORAKHPUR

Project Name : Survey, Design, Preparation of DPR, Construction, Commissioning and O&M for 10 years of Various Rural Water Supply Project in the State of Uttar Pradesh– Gorakhpur District
Client : SWSM/DWSM-UP-GKP
Consultant : Medhaj Techno Concept Pvt. Ltd.
Contractor : NCC Limited

Request For Inspection


RFI No:	SWSM-UP-GKP/IS/TW/125/R ₁	Date And Time	10/05/2022
Description:	Rectification of Compliance.		
Location:	Block Banhalganj, C.P. Shukulpur		
Preceding RFI No.	SWSM-UP-C/125/TW/125		
Commencement of work:	10/05/2022		
Submitted By:	Anant Sahu		
Signature:			
Designation:	JB (Civil)		
Concessionaire:	Proceed	Hold	
Name:			
Designation:			
Comments:	<p>① Post delivery testing of MSEGW is under process. ② H-frame is fabricated. ③ Pea-gravel test report is attached.</p>		


Signature
Contractor Representative


Signature
Consultant Representative

Signature
Client Representative

Shuklpuri

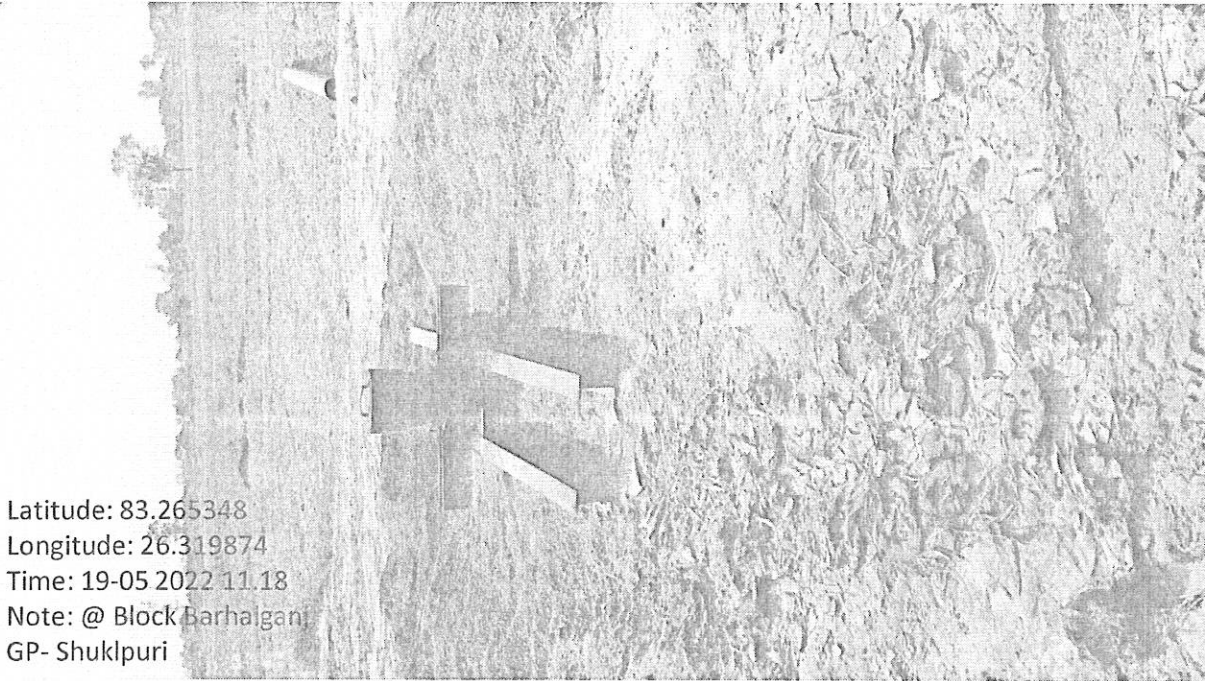

Latitude: 83.265348

Longitude: 26.319874

Time: 19-05-2022 11.18

Note: @ Block Barhaiganj

GP- Shuklpuri

NCC
NCC Limited

NCC LTD.

STATE WATER AND SANITATION MISSION

CLIENT: JJM / SWSM / DWSM

GORAKHPUR-UP



SPECIFIC GRAVITY OF PEA GRAVELS (SIZE- 1.6 mm to 4.8 mm)
As per IS : 2386 (Part-3)

Date of Testing-

15/05/2022

Test report no :

NCC/GKP-5/SC/131

SL NO.

DESCRIPTION

OBSERVATIONS

1

Source of material :

Lakvon, Nainital, Uttarakhand

2

Location :

NAME OF THE BLOCK - BARNDEGANJ

NAME OF THE GRAM PANCHAYAT - SHUKULPURI

3

Date of sampling :

14/05/2022

4

Lab. Test no :

131

5

Sample no :

131

SPECIFIC GRAVITY TEST AT ROOM TEMPERATURE

6

Weight of the Jar, W1 (gm)=

246 gm

7

Weight of Jar + Gravel, W2 (gm)=

455 gm

8

Weight of Jar + Gravel + Water, W3 (gm)=

854 gm

9

Weight of the Jar + Water, W4 (gm)=

718 gm

10

Specific Gravity
=

W2 - W1

(W2 - W1) - (W3 - W4)

= $\frac{212}{212 - 136}$

= 2.78

Note : The Specific Gravity should not be less than 2.5

NCC LTD.

PMC/TPIA

CLIENT



NCC LTD.

STATE WATER AND SANITATION MISSION

CLIENT: JJM / SWSM / DWSM



GORAKHPUR-UP

SIEVE ANALYSIS OF PEA GRAVELS (SIZE-1.6 mm to 4.8 mm)

(As per IS : 460 and IS: 4097)

Date of Testing :

15/05/2022

Test report no :

NCC/WRP-S/Ocd/131

SL NO.	DESCRIPTION	OBSERVATIONS
1	Source of material :	Lalkoon, Nainital, Uttarakhand
2	Location :	Block Name- BARMALGANJ G.P Name- SHUKULPURI
3	Date of sampling :	14/05/2022
4	Lab. Test no :	131
5	Sample no. :	131
6	Total wt. of sample (gm) :	1000gm


SIEVE ANALYSIS

IS Sieve Size	retained	Cumulative wt. Retained (gm)	Cumulative % wt. Retained	% passing	Acceptable / Not Acceptable
6.3 mm	09	09	0.9	99.1	OK
4.75 mm	116	125	12.5	87.5	OK
2.36 mm	726	851	85.1	14.9	OK
1.18 mm	148	999	99.9	0.1	OK
Pan	01				
Total(gm)=					

The Hardness of Material is=

Note:- The Hardness value should not be less than 5 in Moh's scale.

NCC LTD.
PMC/TPIA
CLIENT



Aqua Xplore

(Groundwater Assessment & Allied Services)

243/5, New Colony Jiyamau, Hazratganj, Lucknow – 226001
Mob. 9918202546 / 9889323322, Email-aquaxploreelko@gmail.com

Advisor- Dr. R. A. Yadav, ex- Manager (Groundwater), U. P. Jal Nigam

Ref 513 - S / AX - 2022

Date 13.05.2022

Geophysical Borehole Logging Report

Name of the site : Shukulpuri, Block- Barhalganj

District : Gorakhpur

Date : 13.05.2022

Depth logged : 160.0 mbgl

Depth drilled : 167.0 mbgl

Loggee used : Robertson make UPTRON

Presence : Representative of M/S NCC Limited, Gorakhpur - South

Based on the interpretation of geophysical logs, following information may be deciphered, particularly with respect to salinity of the formation water;

Sl.No.	Depth range(mbgl)	Thickness(m)	Remarks
1	25.0---37.0	12.0	Good all
2	75.0---82.0	7.0	
3	85.0---100.0	15.0	
4	105.0---112.0	7.0	
5	125.0---130.0	5.0	
6	135.0---152.0	17.0	


Note, All zones are intermixed with fine bands of kankar.

Verified as per
logs provided:
G.S.
14/5/22

for Aqua Xplore

CC;

1. Executive Engineer, C.D. (Rural), U.P.Jal Nigam, Gorakhpur.
2. M/S NCC Limited, Gorakhpur –South, SWSM.



TECHPRO ENGINEERS PVT. LTD.

(Laboratory Division)

Lab Add. 131, Ram Ganga Housing Society, Naramau, Kanpur-209217,

Tel.: 0512-2525759, 09793209918, Web site: www.techproindia.com

e-mail: tepllab@gmail.com, info@techproindia.com,

Doc No.: TEQR-36C, Issue No.: 02, Issue Date: 18/08/20, Rev. No. : 01, Rev. Date: 10/12/2020

TEPL/MT/2022/136/R1

Dated: 05-03-2022

TEST REPORT

Name of Customer	:	Jal Nigam, Gorakhpur
Project	:	SWSM-JJM Project (Har Ghar Jal Mission) at Gorakhpur U.P.
Reference No.	:	SWSM-UP/GKP/QC/77
Sample supplied to Lab by	:	Customer representative
Name of Contractor/ Agency	:	NCC Ltd.
Sample Particulars	:	Pea-Gravel

Sample Receipt Date	:	03/03/2022	Job No.	:	MT136
Condition of sample	:	Satisfactory	SRF No.	:	2022/29
Type of Sample	:	Pea-Gravel	ULR No.	:	NA
Source of sample	:	Lalkuan (Uttarakhand)	Period of Testing	:	03/03/2022 to 05/03/2022



Terms & Conditions:

1	Results relate only to the test sample provided by customer.
2	This report is under copyright of Techpro Engineers Pvt. Ltd. (Laboratory Division) and is not to be reproduced, copied, handed over third party or used for any purpose other than for which it has been loaned.
3	The tested samples are retained for three months after issue of test report (if not collected by customer).
4	The unique identification of sample is as Job No. / Chainage No. /BH. No./SI. No. But only SI. No is mentioned in results.

Checked By:

Alok Chauhan

Alok Kumar Chauhan
(Technical Manager)



Approved By:

Arvind Kumar Garg

Arvind Kumar Garg
(Quality Manager)



TECHPRO ENGINEERS PVT. LTD.

(Laboratory Division)

Lab Add: 131, Ram Ganga Housing Society, Naramau, Kanpur-209217,

Tel.: 0512-2525759, 09793209918, Web site: www.techproindia.com


e-mail: tepplab@gmail.com, info@techproindia.com,

Doc No.: TEQR-36C, Issue No.: 02, Issue Date: 18/08/20, Rev. No. : 01, Rev. Date: 10/12/2020

1. PHYSICAL TEST RESULT OF PEA GRAVEL

Sample Unique ID: MT136/TEPL/02


Sl. No.	Particular of Test	Test Passing %	Specification As Per IS (383 & 4097)	Test Method	Remarks	
1.0	Sieve Analysis (% by weight)	12.5 mm	100	-	IS 2386 (Part-1) 1963, RA-2016	-
		8.0 mm	100			
		6.30mm	100			
		4.75 mm	80.90			
		3.35 mm	14.40			
		2.00 mm	8.60			
2.0	Combined Flakiness & Elongation Index (% by weight)	0.0	40 Max	IS 2386 (Part-1)-1963, RA-2016	Partical Size >6.3	
3.0	Water Absorption (% by weight)	0.90	5 Max	IS 2386 (Part-3)-1963 RA-2016	-	
4.0	Specific Gravity	2.66	2.1 - 3.2	IS 2386 (Part-3)-1963 RA-2016	-	
5.0	Hardness Test (Number)	7.3	5 Min	IS 13630 (Part-13)-2006	-	
6.0	Bulk Density , Kg/litre			IS 2386 (Part-3)-1963 RA-2016	-	
	a) Compacted	1.59	NA			
	b) Loose	1.49	NA			



Checked By:

Alok Chauhan


Alok Kumar Chauhan
(Technical Manager)



Approved By:

Arvind Kumar Garg

Arvind Kumar Garg
(Quality Manager)



TECHPRO ENGINEERS PVT. LTD.

(Laboratory Division)



Lab Add. 131, Ram Ganga Housing Society, Naramau, Kanpur- 209217,

Tel.: 0512-2525759, 09793209918, Web site: www.techproindia.com

e-mail: tepllab@gmail.com, info@techproindia.com,

Doc No.: TEQR-36C, Issue No.: 02, Issue Date: 18/08/20, Rev. No. : 01, Rev. Date: 10/12/2020

PHOTOGRAPHS

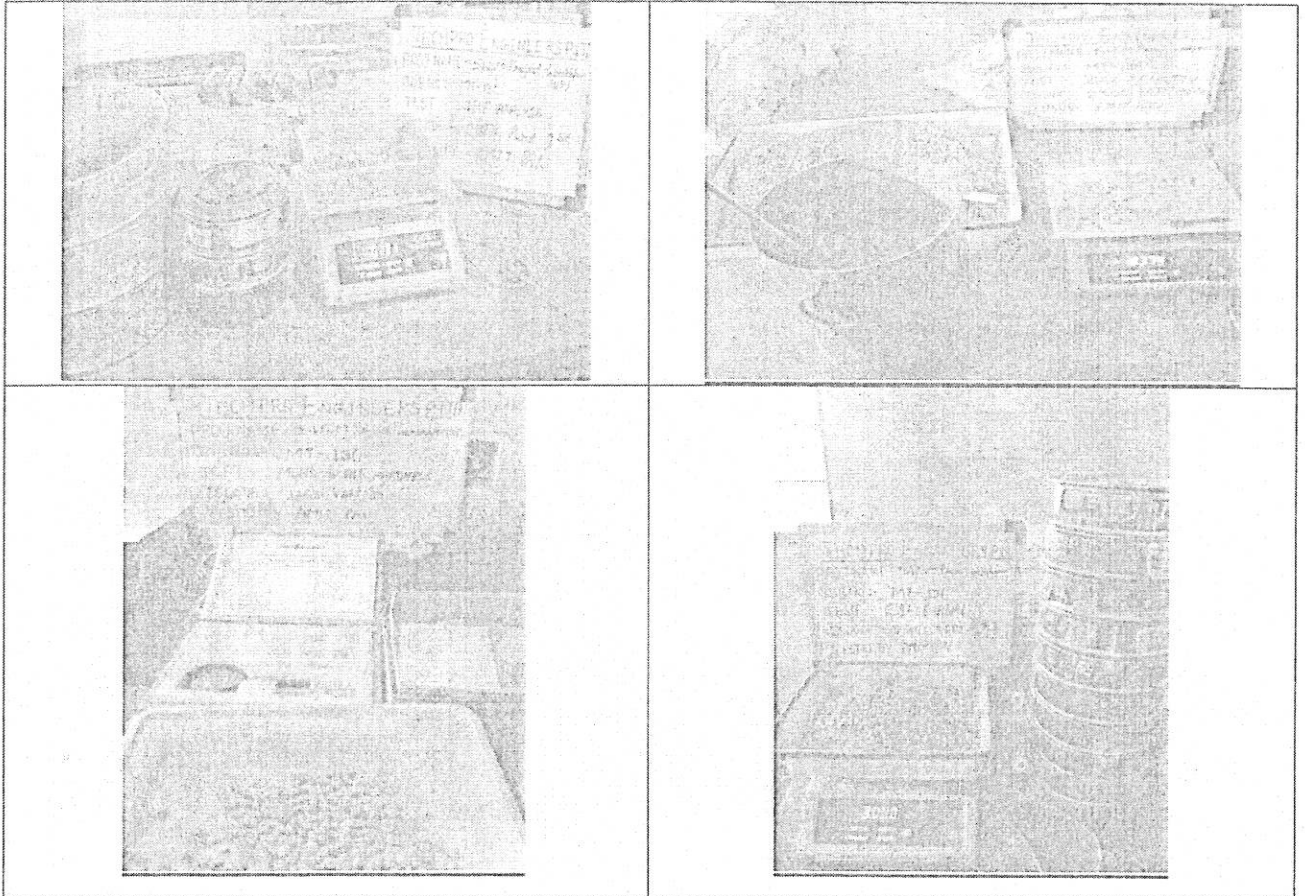

END OF REPORT



प्रोजेक्ट्स एण्ड डेवलपमेंट इण्डिया लिमिटेड
PROJECTS & DEVELOPMENT INDIA LIMITED

Inspection Report/Certificate

Certificate/Report No. 1500-005000049311-C
Dated 14.02.2022


Client /Purchaser	M/S SWSM UP/ M/S NCC LIMITED	Inspection office	INSP NOIDA
P.O. No. & Date	NCC/SWSM-GORAKHPUR-SOUTH/215721-22 03.02.2021	Start Date of Inspection	12.02.2022
Supplier /Manufacturer	M/S DADU PIPES (P) LTD.	End Date of Inspection	12.02.2022
Sub Supplier	NA	PDIL Job no	4004006945
Sub supplier P.O.No & date	NA	PDIL Sales Order No.	
Project Name		Total P.O. value	LS
Client Reference		Total inspected item value	LS
P.O.Status	COMPLETE	Inspection Status	FINAL

IC/IR Status APPROVED

Sl No.	P.O/BOM /Item No.	Description (Nomenclature, Size, Final Specification)	Unit	Ordered Qty	Offered Qty	Inspected Qty	Status	Accepted Qty	Cummulative Qty	Document Ref.	Heat no./batch No./Earlier certificate NO./material identification etc.
01	01	150MM DIA 5.4 MM THK (THE SLOT SIZE SHALL BE 75MM*1.20MM AND IT SHOULD BE ZIG-ZAG PATTERN AS PER IS8110)	MTR	738	738	738	A	738	738	AS PER PO	BATCH NO.: 22B05
02	02	200MM DIA 7.1 MM THK (THE SLOT SIZE SHALL BE 75MM*1.20MM AND IT SHOULD BE ZIG-ZAG PATTERN AS PER IS8110)	MTR	108	108	108	A	108	108	AS PER PO	BATCH NO.: 22B01
03	03	150MM DIA 5MM THK MS ERW PIPE AS PER IS 4270	MTR	1458	1470	1470	A	1458	1458	AS PER PO	BATCH NO.: 22B04
04	04	300MM DIA 7.1MM THK	MTR	468	480	480	A	468	468	AS PER PO	BATCH NO.: 22A29

Status Code (for details refer remarks): A- Accepted, B- Customer Clearance Required, D-Deviated, P- Partial Accepted, R- Rejected, S- Stage, W- Rework, X-Refer Remarks	
Signature	
Name	SANDEEP SINGH BHATI
Company/Organization	PDIL (Inspection & NDT)
Client/Purchaser	
Supplier/Manufacturer	
Sub Supplier	

* This Inspection Certificate is issued without prejudice of contractual obligation of the supplier and does not relieve him from the guarantees and obligations set forth in purchase order and attachment.



प्रोजेक्ट्स एण्ड डेवलपमेंट इण्डिया लिमिटेड
PROJECTS & DEVELOPMENT INDIA LIMITED

Inspection Report/Certificate

Certificate/Report No. 1500-005000049311-C
Dated 14.02.2022

Client /Purchaser	M/S SWSM UP/ M/S NCC LIMITED	Inspection office	INSP NOIDA
P.O. No. & Date	NCC/SWSM-GORAKHPUR-SOUTH/215721-22 03.02.2021	Start Date of Inspection	12.02.2022
Supplier /Manufacturer	M/S DADU PIPES (P) LTD.	End Date of Inspection	12.02.2022
Sub Supplier	NA	PDIL Job no	4004006945
Sub supplier P.O.No & date	NA	PDIL Sales Order No.	
Project Name		Total P.O. value	LS
Client Reference		Total inspected item value	LS
P.O.Status	COMPLETE	Inspection Status	FINAL

SI No.	P.O./BOM /Item No.	Description (Nomenclature, Size, Final Specification)	Unit	ICIR Status			Status	Accepted Qty	Cumulative Qty	Document Ref.	Heat no./batch No./Earlier certificate NO./material identification etc.
				Ordered Qty	Offered Qty	Inspected Qty					
		MS ERW PIPE AS PER IS4270									

Inspection/Test:

INSPECTION CARRIED OUT AS PER APPROVED QAP & IS4270

- 1) VISUAL & PHYSICAL INSPECTION FOR QUANTITY, MARKING, FINISHING AND FOUND OK.
- 2) DIMENSION CHECKED AND FOUND WITHIN TOLERANCE LIMITS.
- 3) TENSILE TEST, ELONGATION, FLATTENING & HYDRO TEST WITNESSED OF RANDOMLY SELECTED SAMPLES AND RESULTS FOUND SATISFACTORY.
- 4) INTERNAL REPORT, MTC AND CALIBRATION CERTIFICATES REVIEWED AND FOUND IN ORDER.
- 5) FOR IDENTIFICATION MATERIAL STAMPED AS "P&d/117".

Enclosure:

1) MATERIAL TEST CERTIFICATE (2) CALIBRATION CERTIFICATE (3) INSPECTION VISIT REPORT

Remarks:

MATERIAL RELEASED FOR DISPATCH AS PER TERMS & CONDITIONS OF PURCHASE ORDER.

Status Code (for details refer remarks): A- Accepted, C- Customer Clearance Required, D-Deviated, P- Partial Accepted, R- Rejected, S- Stage, W- Rework, X-Refer Remarks	
Signature	
Name	SANDEEP SINGH BHATT
Company/organization	PDIL (Inspection & NDT) Noida
Client/Purchaser	
Supplier/Manufacturer	
Sub Supplier	

* This Inspection Certificate is issued without prejudice of contractual obligation of the supplier and does not relieve him from the guarantees and obligations set forth in purchase order and attachment.

Estimate for Shukal puri Gram Panchayat
Water Supply Scheme
Under - SWSM
Block- Barhalganj District- Gorakhpur

BOQ Item No.	Description	Unit	Qty	Rate	Amount
	Survey, Design & Preparation of DPR				
1.01	All the works including Hydrological survey, topographical survey, Design charges including preparation and approval of DPR	LS	1.00	230888.00	230888
2.00	Drilling of Borchole for Tubewell construction by DC/RC/DTH Rig Machine including transportaion, erection, dismantling of Rig and assosiated T&P complete in all respect including required all material labour etc.				
	RIG Transportation for Tube Well Construction				
2.01	Transportation, Installation Dismantling of Rig machine and logging of bore hole	Job	1.00	159478.88	159479
	Tube Well Construction- Drilling of Borchole				
2.03	DC/RC Drilling up to 100Mtr.				
2.04	400 MMØ	Mtr.		1638.27	
2.05	450 MMØ	Mtr.		1834.20	
2.06	500 MMØ	Mtr.	100.00	2013.00	201300
2.07	600 MMØ	Mtr.		2422.00	
2.08	DC/RC Drilling from 101 Mtr. To 200 Mtr.Deep				
2.09	450 MMØ	Mtr.		1960.88	
2.10	500 MMØ	Mtr.	67.00	2144.00	143648
2.11	600 MMØ	Mtr.		2510.25	
2.12	DC/RC Drilling from 201 Mtr. To 300 Mtr.Deep				
2.13	450 MMØ	Mtr.		2831.63	
2.14	500 MMØ	Mtr.		3014.75	
2.15	600 MMØ	Mtr.		3381.00	
2.16	DC/RC Drilling from 301 Mtr. To 400 Mtr.Deep & above				
2.17	450 MMØ	Mtr.		3319.35	
2.18	500 MMØ	Mtr.		3502.48	
2.19	600 MMØ	Mtr.		3868.72	
2.20	DTH Drilling upto 200.0 Mtr.Deep				
2.21	200/165 MMØ (in over burden/Hard Rock)	Mtr.		1250.00	
2.22	Development / Flushing of tubewell	Hr.		2900.00	
	Tubwell Assembly (Supply + Fittings & Specials)				
3.01	MSERW plain pipe,As per IS 4270				
3.02	100 MMØ	Mtr.		927.50	
3.03	150 MMØ	Mtr.	96.00	1900.00	182400
3.04	200 MMØ	Mtr.	36.00	2550.00	91800
3.05	300 MMØ	Mtr.		3800.00	
3.06	MSERW Pipe slotted pipe as per IS 8110				
3.07	100 MMØ	Mtr.		1366.85	
3.08	150 MMØ	Mtr.	18.00	2800.00	50400
3.09	200 MMØ	Mtr.		3833.80	
3.10	300 MMØ	Mtr.		5188.59	
3.11	MS fittings such as clamp, bail plug, reducer, well cap, girder & support structure	LS	1.00	32295.00	32295
3.12	MS fittings such as ring & centre guide	RM	150.00	471.68	70752
	Tubwell Assembly Lowering Works				
	Lowering of above assembly with welding of parts complete in all respect with all required material, T&P, labour, etc.				
4.01	Lowering up to 100 Mtr. Deep				
4.02	100 MMØ MSERW Plane/Slotted Pipe	Mtr.		129.45	
4.03	150 MMØ MSERW Plane/Slotted Pipe	Mtr.	64.00	281.00	17984
4.04	200 MMØ MSERW Plane/Slotted Pipe	Mtr.	36.00	376.50	13554
4.05	300 MMØ MSERW Plain/Slotted Pipe	Mtr.		472.00	
4.06	Lowering from 101 Mtr. To 200 Mtr. Deep				
4.07	150 MMØ MSERW Plane/Slotted Pipe	Mtr.	50.00	376.00	18800
4.08	200 MMØ MSERW Plane/Slotted Pipe	Mtr.		499.19	

BOQ Item No.	Description	Unit	Qty	Rate	Amount
4.09	300 MMØ MSERW Plane/Slotted Pipe	Mtr.		745.58	
4.10	Lowering from 201 Mtr. To 300 Mtr. Deep				
4.11	150 MMØ MSERW Plane/Slotted Pipe	Mtr.		385.19	
4.12	200 MMØ MSERW Plane/Slotted Pipe	Mtr.		459.00	
4.13	300 MMØ MSERW Plane/Slotted Pipe	Mtr.		606.62	
4.14	Lowering from 301 Mtr. To 400 Mtr. Deep & above				
4.15	150 MMØ MSERW Plane/Slotted Pipe	Mtr.		426.53	
4.16	200 MMØ MSERW Plane/Slotted Pipe	Mtr.		499.00	
4.17	300 MMØ MSERW Plane/Slotted Pipe	Mtr.		643.94	
	Supply and Packing of Gravel Works				
5.00	Supply and unconsolidated packing of gravel with suitable size	Cum	44.00	7500.00	330000
	Development of Tube well				
6.01	Tranportation, Installation Dismantling of 150 PSI Compressor	Job		42120.00	
6.02	Charges for Development by 150 PSI Compressor per hour	Hr.		2544.52	
6.03	Tranportation, Installation Dismantling of 250/400/600 PSI Compressor	Job	1.00	42120.00	42120
6.04	Charges for Development by 250 PSI Compressor per hour	Hr.	60.00	3027.00	181620
6.05	Charges for Development by 400 PSI Compressor per hour	Hr.		3154.10	
6.06	Charges for Development by 600 PSI Compressor per hour	Hr.		4062.20	
6.07	Tranportation, Installation Dismantling of 0.5 Cusec OP Unit and Yield test, water test	Job		22321.28	
6.08	Charges for Development of TW by 0.5 Cusec OP Unit	Hr.		785.42	
6.09	Tranportation, Installation Dismantling of 1 Cusec to 3 Cusec OP Unit and Yield test, water test	Job	1.00	67225.00	67225
6.10	Charges for Development of TW by 1 cusec OP Unit	Hr.	100.00	959.00	95900
6.11	Charges for Development of TW by 3 cusec OP Unit	Hr.		1196.00	
6.12	Tranportation, Installation Dismantling of 2 Cusec OP Unit and Yield test, water test	Job		89317.00	
6.13	Charges for Development of TW by 2 cusec OP Unit	Hr.		1119.00	
	Pumping Plant:-				
7.00	SITC of Pumping plant including pumps with motors starter, pannel, cable, complete in all respect with all required material T&P labour etc.				
7.01	1 HP	Nos		32518.98	
7.02	2 HP	Nos		35843.14	
7.03	3 HP	Nos		46249.21	
7.04	5 HP	Nos		65037.95	
7.05	7.5HP	Nos		228500	
7.06	10 HP	Nos		230200	
7.07	12.5 HP	Nos	1.00	238800	238800
7.08	15 HP	Nos		252100	
7.09	17.5 HP	Nos		276504.56	
7.10	20 HP	Nos		295500	
7.11	25 HP	Nos		334043.48	
7.12	30 HP	Nos		366163.04	
7.13	35 HP	Nos		393723.7	
7.14	40 HP	Nos		426547.83	
7.15	Variation in HP due to change of site locations increased/decreased in per HP of the proposed pumping plants.	Rate/HP		30467	
8.00	Pressure Transmitter	Nos	1.00	43120	43120
A.I - 13	Electrically operated Sluice Valve:-				
A.I - 13.01	Electrically operated Sluice Valve PN 1.0 dia 80 mm	Nos	2.00	125000	250000
A.I - 13.02	Electrically operated Sluice Valve PN 1.0 dia 125 mm	Nos		125000	
9.00	Electrically operated Sluice Valve PN 1.0 dia 100 mm	Nos	1.00	125000	125000
9.01	Electrically operated Sluice Valve PN 1.0 dia 150 mm	Nos		125000	
9.02	Electrically operated Sluice Valve PN 1.0 dia 200 mm	Nos		150000	
A.I - 14	Check Valve:-				
A.I - 14.01	Check Valve PN 1.0 DPCV dia 80 mm	Nos	1.00	27519.8	27520
9.03	Check Valve PN 1.0 DPCV dia 100 mm	Nos		27519.8	
9.04	Check Valve PN 1.0 DPCV dia 150 mm	Nos		51145.45	
9.05	Check Valve PN 1.0 DPCV dia 200 mm	Nos		73485.9	
A.I - 15	Dismantling Joint :-				



Particulars	Details of actual measurement				Contents or area/Vol.
	No.	L.	B.	H.	
3.11 No fitting such as clamp, bail plug reduces, well cap, girder & support structure	1X	32295	00		= 32,295.00
3.12 Ms Fittings such as ring & Centre Guide	1X	136.27	X 471.68		= 64275.83
4.00 lowering of above assembly with welding of parts complete in all respect with all required material, TLP, labour etc					
4.01 lowering up to 100 Mts Deep					
4.03 150 mm φ MS ERW plain/slotted pipe	1X	63.70	X 281.00		= 17899.70
4.05 300 mm φ MS ERW plain/slotted pipe	1X	36.00	X 472.00		= 16992.00
4.06 Lowering from 101 Mts to 200 Mts deep					
4.07 150 mm φ MS ERW plain/slotted pipe	1X	36.27	X 376.00		= 13637.52
5.00 Supplying & Consolidated packing of Gravel with suitable size	1X	45.51	X 7500		= 341325.00
				Amount =	13,25,136.03
				Discount (0.14%)	(₹) 1855.19
				Net Amount =	13,23,280.84
				SGST @ 9%	1,19,095.28
				CST @ 9%	1,19,095.28
				Total Amount =	15,61,471.39
<i>Passed & charged to "Dadaosa" W.D.S of Dist - Gaoathpur.</i>					
Abstract of RA bill of NCC limited GKP dt NO:- 216/EP/2021-22 dt 15/12/21, Toipartire agreement NCC/327 for Construction of tubewell of Gaoathpur Dist. G.P. Shuklapur water supply scheme.				against Coas agreement NO:- JH/UP/Phase 2/Gaoathpur	
2.01 Transportation, installation, dismantling of Rig machine & logging of bore hole	1X	159478.88			= 159478.88
2.03 DC/RC drilling up to 100 Mts.					
2.06 500 mm φ	1X	60.00	X 2013.00		= 120780.00
2.07 500mm φ	1X	40.00	X 2013.00		= 80520.00
2.08 DC/RC drilling from 104 Mts 200 Mts deep					

[Handwritten signature]



Particulars	Details of actual measurement				Contents or area/Vol.
	No.	L.	B.	H.	
2.10 500 mm ϕ	1x	67	21	14.00	= 143648.00
3.00 Tubewell assembly.					
3.01 MSERW plain pipe, as per IS 4270					
3.03 150 mm ϕ					@ Rs. 1900.00
On supply & delivery	70%	of 81.19	x	1330.00	= 107982.70
On Completion erection, fixing, laying, jointing	20%	of 81.19	x	380.00	= 30852.20
3.04 200 mm ϕ					@ Rs. 2550.00
On supply & delivery	70%	36.00	x	1785.00	= 64260.00
On Completion erection, fixing, laying, jointing	20%	of 36.00	x	510.00	= 18360.00
3.06 MSERW plain slotted pipe as per IS 8110					
3.08 150 mm ϕ					@ Rs. 2800.00
On supply & delivery	70%	of 18.00	x	1960.00	= 35280.00
On Completion erection, fixing, laying, jointing	20%	of 18.00	x	560.00	= 10080.00
3.11 No Fitting Such as clamp, bail plug, reducers, well cap, girders & support structure	1x				32295.00 = 32295.00
3.12 No Fitting Such as rings & Centre Guide	1x	135.88	x	471.68	= 64091.88.
4.00 Lowering of above assembly with welding of parts complete in all respect with all required materials T&P, labour etc					
4.01 Lowering up to 100 Mts Deep					
4.03 150 mm ϕ MSERW plain/slotted pipe	1x	63.55	x	281.00	= 17857.55
4.05 200 mm ϕ MSERW plain/slotted pipe	1x	36.00	x	376.50	= 13554.00
4.06 Lowering from 101 Mts to 200 Mts deep					
4.07 150 mm ϕ MSERW plain/slotted pipe	1x	35.88	x	376.00	= 13490.88.
5.00 Supplying & unconsolidated packing of gravel with suitable size	1x	42.62	x	7500	= 319650.00
					(Amount = 12,32,181.09
					Discount (0.14%) = 1725.05
					Net Amount = 12,30,456.04
					SGST @ 9% = 1,10,741.04
					CGST @ 9% = 1,10,741.04
					Total Amount = 14,51,938.12

Passed & charged to Shukhla Prasad
 2.5.5 of Dist. Guwahati.
