

76

Comp 40P

FIELD TEST REPORT				
NAME OF SCHEME		Markanti Water Supply Scheme		
LOCATION OF T/W		Near Toilet House/Temple		
REQUIRED DISCHARGE AS PER SCHEME		360 LPM		
DATE OF TESTING		08.12.2021		
TASTE OF WATER		Sweet		
PHYSICAL WATER QUALITY		Sand free		
S.No.	S.W.L. IN MTR.	R.W.L. IN MTR.	DEPRESSION IN MTR.	DISCHARGE IN LPM
1.	11.00 mtr	13.00 mtr	2.00 mtr	1960 Lpm
REMARKS:-				
RECOMMENDED DISCHARGE				
 BGCC		VIVEK AGNIHOTRI NAME OF SWSM/JALNIGAM /PMC/TPI ENGINEER		 SIGNATURE OF SWSM/JALNIGAM /PMC/TPI ENGINEER

76

Request for Inspection (RFI)

Client:-	STATE WATER SANITATION MISSION		
PMC:-	TES-WTES(J.V.) PMC JHANSI		
CONTRACTOR:-	BRIJGOPAL CONSTRUCTION COMPANY		
SCHEME NAME:-	IMLOTA / TEHARKA / BARTHARI / JALAUN		
Request for inspection / Approval		Village - Harkoti Block - Jalaun	
RFI NO. :-		Request Date/Time:- 7/12/2021	
Request for Inspection on scheme work (tick as applicable)			
INSTRUMENTATION	CIVIL	MECHANICAL	ELECTRICAL
		COMMISSIONING	
WORK PARTICULARS:-			
Description of works	Comments be PMC/Client/	Signature by PMC/Client / T.P.F	Remark
Water discharge checking (OP level)	① Gravel packing is not satisfactory		
	② Calibration		
Village - Harkoti	Certificate of		
Block - Jalaun	flow meter not available		
Inspection Date:-		Inspection Time:-	
Request by BGCC Representative		Received by PMC Representative / T.P.F	
NAME Manish Kumar		NAME - Vivek Agnihotri	
Signature		Signature -	
Inspection Date 8/12/2021		Inspection Date - 8/12/21	
Inspection Time		Inspection Time - 04:00 P.M.	
Encl. :-			

REQUEST FOR INSPECTION

PROJECT	Construction of Kota Muskil ,Raipura and Madepura Group of Villages water Supply Scheme (Surface Water) and Electric /Solar based pipe Ground Water Supply Schemes (270 Nos.) in Villages of Blocks, District Jalaun with Relevant works including commisioning and operation and maintenance for 10 years .		
RFI NO			
DATE	12/8/21		
CLIENT	STATE WATER AND SANITATION MISSION (SWSM)		
CONTRACTOR	BRIJ GOPAL CONSTRUCTION COMPANY PVT. LTD. & SPML (JV)		
CONTRACT NO.	ED/35/2020-21 DATE:-19.12.2021		
NODE NO.			
LOCATION	Village - Harkauti ,Block - Jalaun.		
S.No.	DESCRIPTION OF WORK		
	Bore well drilling start.		
NAME OF SITE ENGINEER (BGCC)	Munish Sr	DATE & TIME OF INSPECTION	
SIGNATURE OF SITE ENGINEER (BGCC)	(Munish)	12/8/21, 10.20 Am	
INSPECTION BY-			
SWSM/JAL NIGAM	☐	PMC/TPI ☒	DATE & TIME OF INSPECTION
REMARKS:-			
NAME OF SWSM/JALNIGAM /PMC/TPI ENGINEER		SIGNATURE OF SWSM/JALNIGAM /PMC/TPI ENGINEER	

Specialist in : Civil Mechanical, Steel Fabrication, Sand blasting, Painting, Tubewell Drilling, Rain Water Harvesting, Dewatering and its allied jobs.

Geophysical Well Logging Report

Ref No -ADCO/JJN/Logging/11

Date 20/09/2021


Block :- Jalaun
Site Location :- Village - Harkothi Jaloun
Distt :- Jalaun
Drilling Depth :- 104 MBGL
Logged Depth :- 102 MBGL
Date of Logging :- 19/06/2021
Types of Log :- S.P & Resistivity
Logger used :- Er. Prashant Singh, Er. Shakir & Er. Pawan Singh

The following permeable granular zones have been deciphered with the help of Electrical Logger

Depth Range From M.B.G.L.	Depth Range M.B.G.L.	Thickness Mtrs.	Inferred Litho logy	Quality of G.W.
44	58	14	Core Sand	Good
67	76	09	Core Sand	Good
55	100	15	Core Sand	Good

Encl. - E. Logs

ADCO
FF B4/51, Paschim Vihar
New Delhi-110063
(ADCO)

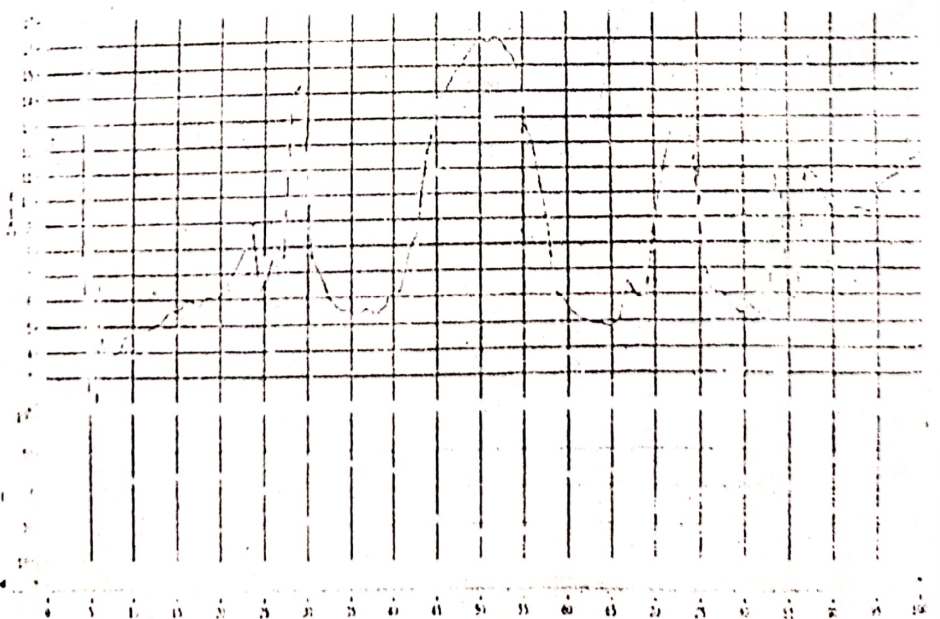

Yield Test Report Bt 250 P.S.I Compressor

Date Of Test :- 03-10-21

Static W/L

Taste of Water

Village :- Maarkoli

Discharge		ST.PR.	RU PR	Depre		Sand Contents				Remarks			
INC	LPM	Kg/Cm2	Kg/Cm2	Kg	MTR	Start	5 Min.	10 Min.	15 Min.	20 Min.	25 Min.		
		5.90	5.40	0.50	5.00	3.60	3.00	2.00	1.60	900			
		8.70	8.10	0.60	6.00	4.20	3.60	2.40	1.80	1000			
		9.60	8.90	7.0	7.00	46.00	4.00	2.60	2.00	1200			
		1200	11.20	8.0	8.00	48.00	4.20	2.80	2.40	1400			

Note:- Recommended For Further Development by O.P. Unit.

Note:- Recommended For Further Development by O.P. Unit.

高

Proposed tubewell Assembly Haskoth's Talam Block, Talam.

Logging report 20.09.2021

- 1- 44.0 - 58.0 = 14.0
- 2- 67.0 - 76.0 = 09.0
- 3- 85.0 - 100.0 = 15.0

200mm dia MVERW Plain pipe

- 1-
- 2-
- 3-
- 4-
- 5-
- 6-
- 7-
- 8-
- 9-


150mm dia MVERW Plain pipe

- 1-
- 2-
- 3-
- 4-





150mm dia MVERW slotted pipe

- 1-
- 2-
- 3-
- 4-

150mm dia Plain pipe cutting



150mm dia slotted pipe cutting

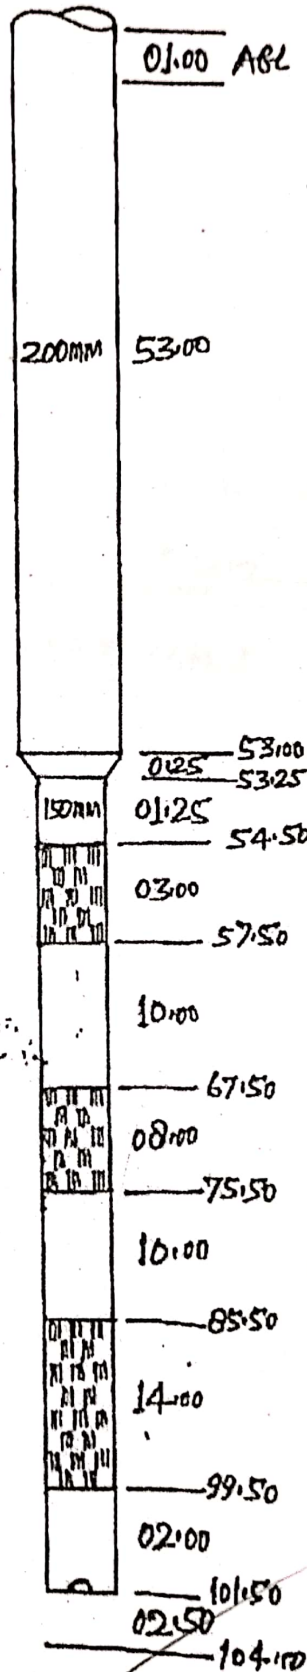

Drill rod length

- 1-
- 2-
- 3-
- 4-
- 5-
- 6-
- 7-
- 8-
- 9-
- 10-
- 11-
- 12-
- 13-
- 14-
- 15-



Jhansi Khand-1st
U.P. Jal Nigam, Jhansi
