


Phase-II

Completion Plan of Gobindpur Tawara-GP, Kaudihar- Block, District- Prayagraj

DETAILS OF T/W ASSEMBLY & STRATA

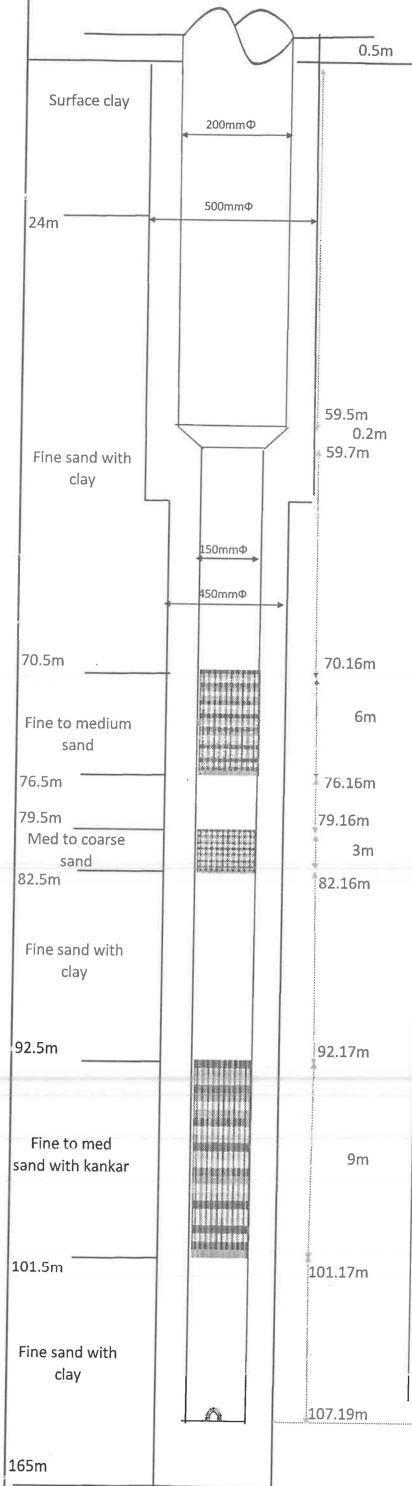

Agency of construction : LARSEN & TOUBRO LTD
 Drilling Started On : 12-04-2023
 Drilling Completed On : 20-03-2023
 Assembly lowered on : 21-04-2023
 Size of bore : 500mmφ from GL to 65m BGL
 450mmφ from 65m BGL to 165m BGL
 Size of tubewell : 200*150mm
 Req. Discharge : 560LPM

LOGGING REPORT

Logging report Date : 19-04-2023
 Depth Logged : 166mtr
 Directed by : Dr.S.SHUKLA
 MANAGER(GROUND WATER)
 U.P.JN-LUCKNOW

Sl.No	Depth Range in Meter B.G.L	Thickness in Meter	Remarks	Note
1	44-54	10	GOOD	1.All zones intermixed with thin band of kankar.
2	56-60	4	GOOD	2.The formation water is determonitoring from marginal to saline below
3	70-77	7	GOOD	
4	79-83	4	GOOD	
5	92-102	10	GOOD	120Mbgl to till ddepth logged

T.W Constructed By

Subhankar sil(PM)
L&T Construction

TPI
Sanjay paswan

(Jitendra yadav)
Junior Engineer

(Karunakar Singh)
Assistant Engineer

(Syed. Mohd. Shabaz)
Executive Engineer

Division office E&M,UP Jal Nigam (Rural) Prayagraj
