


Completion Plan of Dadupur_Dhudehri_Benipur-GP Saidabad- Block, District- Prayagraj

Agency of construction : LARSEN & TOUBRO LTD
 Drilling Started On : 10-10-2023
 Drilling Completed On : 17-10-2023
 Assembly lowered on : 18-10-2023
 Size of bore : 600mm ϕ from GL to 65m BGL
 500mm ϕ from 65m BGL to 165m BGL
 Size of tubewell : 300*200 mm
 Req. Discharge : 1070 LPM

LOGGING REPORT

Logging report Date : 17-10-2023
 Depth Logged : 164m
 Directed by : Mr Sanjeet Sharma(Hydrogeologist)
 (All Geo Solution)
 STPI,MNIT Campus,Teliarganj
 UPJN-Prayagraj

DETAILS OF T/W ASSEMBLY & STRATA

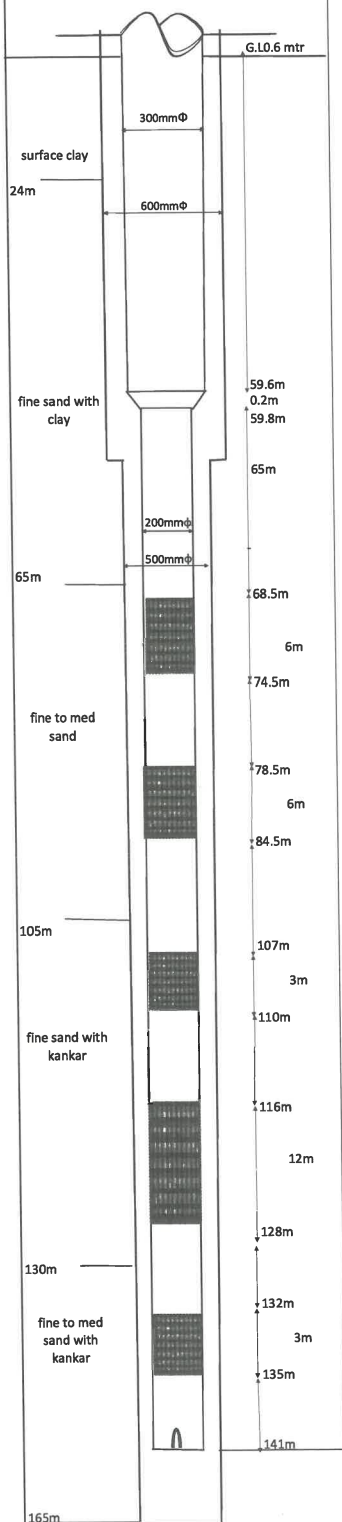

| Sl.No | Depth Range in Meter B.G.L | Thickness in Meter | Remarks | Note |
|-------|----------------------------|--------------------|---------|---|
| 1 | 68-75 | 7 | GOOD | 1.All zone are intermixed with thin band of kankar. |
| 2 | 78-85 | 7 | GOOD | |
| 3 | 107-110 | 3 | GOOD | |
| 4 | 116-128 | 12 | GOOD | |
| 5 | 131-145 | 14 | GOOD | |
| 6 | 152-157 | 5 | GOOD | |
| 7 | 159-163 | 4 | GOOD | |

T.W Constructed By

Subhankar sil(PM)
L&T Construction

Vishal Singh
MTCPL(TPI)

(Bandana)
Junior Engineer

(Karnakar Singh)
Assistant Engineer

(Syed. Mohd. Shabaz)
Executive Engineer
