



अधिशालसी अभियन्ता, खण्ड कार्यालय

उ० प्र० जल निगम (ग्रामीण), ग्वालियर रोड झाँसी (उ०प्र०)।

Email Add.- eecdupjnjhansi@gmail.com Mob. No. 9473942725

पत्रांक
सेवा में,

1327 / कार्र-७२

164

दिनांक-23/6/2026

राज्य समन्वयक
राज्य पेयजल एवं स्वच्छता मिशन
लखनऊ।

विषय :-

जनपद झाँसी में नोडल अधिकारी द्वारा किये गये निरीक्षण के दौरान पायी गयी कमियों की निस्तारण आख्या प्रेषित करने के सम्बन्ध में।

महोदय,

उपरोक्त विषयक आपके पत्रांक पत्रांक 722/JJM/WQ-2/Vol-1/2025-26 (Tech.) दिनांक 26 मई, 2026 क्रम में जनपद झाँसी में नोडल अधिकारी द्वारा जल जीवन मिशन के अन्तर्गत निर्मित पेयजल योजनान्तर्गत कराये गये कार्यों के स्थलीय निरीक्षण के दौरान पायी गयी कमियों का, योजना के कार्यों हेतु अनुबन्धित फर्मों द्वारा निस्तारण कराते हुये आख्या इस खण्ड में उपलब्ध करायी गयी है।

अतः फर्मों द्वारा उपलब्ध करायी गयी निस्तारण आख्या संलग्न कर अग्रिम कार्यवाही हेतु सादर प्रेषित है।

संलग्नक :- उपरोक्तानुसार।

भवदीय


(मुकेश कुमार सिंह)
अधिशालसी अभियन्ता

संख्या एवं दिनांक यथोपरि।

प्रतिलिपि :- निम्नलिखित सादर सूचनार्थ एवं आवश्यक कार्यवाही हेतु प्रेषित।

1. अधिशालसी निदेशक, राज्य पेयजल एवं स्वच्छता मिशन, लखनऊ।
2. मुख्य अभियन्ता (बुन्देलखण्ड क्षेत्र), उ०प्र० जल निगम (ग्रामीण), झाँसी।
3. अधीक्षण अभियन्ता, मण्डल कार्यालय, उ०प्र० जल निगम (ग्रामीण), झाँसी।
4. अपर जिलाधिकारी, नमामि गंगे एवं ग्रामीण जलापूर्ति विभाग झाँसी।
5. सम्बन्धित सहायक अभियन्ता/जूनियर इंजीनियर।

अधिशालसी अभियन्ता



Unipro Techno Infrastructure Pvt. Ltd.

Admin. Office & Corsp. Add.: Plot No-43, Industrial Area, Phase-II, Panchkula-134113, Haryana.
Tel/Fax: 0172-5008892, 5008758. Web: www.uniproinfra.com. E-mail: pro@uniproinfra.com, uniprochandigarh@gmail.com

UTIPL/SO/221/SWSM/JHANSI/2026-27

Dated 15.06.2026

सेवा में,

अधिकासी अभियंता


जल निगम ग्रामीण, झाँसी उत्तर प्रदेश.

योजना . बरवार ग्राम समूह पेयजल योजना


विषय -जनपद झाँसी में नोडल अधिकारी द्वारा किये गए निरिक्षण के दौरान पाई गयी कमियों के निस्तारण के सम्बन्ध में

महोदय,

उपरोक्त विषयक आपके पत्रांक 955 /कार्य-92/57 दिनांक 30-05-2026 द्वारा जनपद झाँसी में बरवार ग्राम समूह पेयजल योजना में नोडल अधिकारी द्वारा किये गए निरिक्षण के दौरान ग्राम भास्नेह की एक गली के 8 घरों में पानी की सप्लाई नहीं जा रही थी, जिसको संज्ञान में लेकर वाल्व का इंस्टालेशन कर सभी कनेक्शन में पानी दे दिया गया है, एवं ग्राम भादोकर के उपर के एक स्थान पर चोकेज की बजह से पानी नहीं जा रहा था उसे भी ठीक करा दिया गया है जिसकी फोटो इस पत्र के साथ संलग्न है

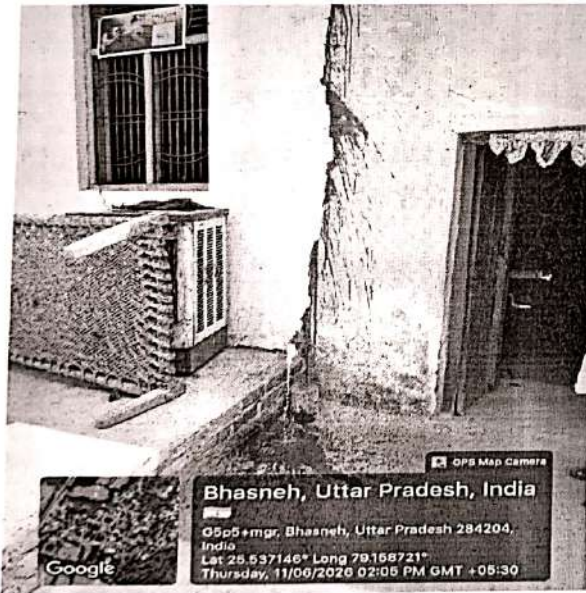

ग्राम भास्नेह की गली की फोटो

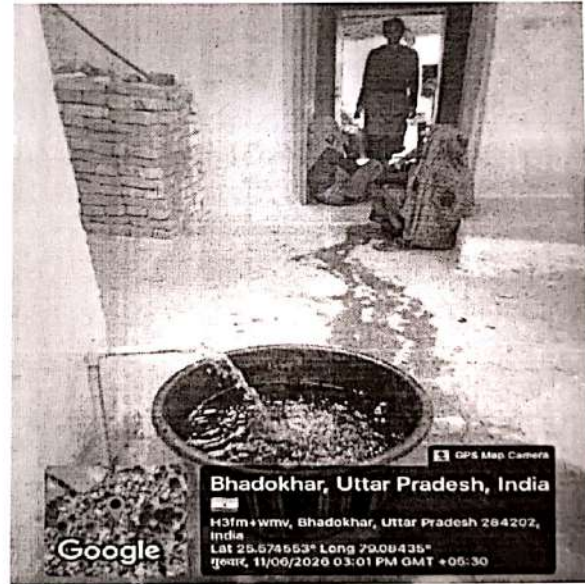

ग्राम भाडोखर के उपरी स्थान की फोटो

यूनीप्रो टेक्नो इंफ्रा स्ट्रक्चर प्राइवेट लिमिटेड





NCC

NCC/W&E/GBT-Burpura/2026-27/861

दिनांक:- 22/06/2026.

To,
अधिशाली अभियंता
खंड कार्यालय, जल निगम, झाँसी।

विषय:- गुलारा, बचावली एवं तिलैथा & बुढ़पुरा पेयजल योजनान्तर्गत जनपद झाँसी में नोडल अधिकारी द्वारा किये गये निरीक्षण के दौरान पायी गयी कमियों की निस्तारण आख्या उपलब्ध कराने के सम्बन्ध में।

Ref: - 1. Agreement No. 10/ED/2020-21, dated- 01/07/2020.
2. Agreement No. 11/ED/2020-21, dated- 01/07/2020.
3. SWSM Letter No. 722/JJM/WQ-2/Vol-1/2025-26 (Tech), dated- 26/05/2026.
4. NCC Letter No. NCC/W&E/GBT&Burpura-Jhansi/Pln/2026-27/851, dated- 01/06/2026.

उपरोक्त योजनान्तर्गत SWSM टीम, लखनऊ द्वारा साइट विज़िट के बाद अनुपालन के संबंध में बिंदुवार जवाब उपलब्ध करा रहे हैं। ये विज़िट झाँसी ज़िले के बड़ागाँव, चिरगाँव और बबीना ब्लॉक में की गई थीं। जिन स्थानों/ग्रामों का दौरा किया गया वे थे-

- बड़ागाँव ब्लॉक: कोलवां, तेंदोल, तिलैथा और बराठा गांव,
- चिरगाँव ब्लॉक: जरयाई गांव &
- बबीना ब्लॉक: गणेशपुर, रसोई, चमरौआ, बैदौरा और किलचवारा गांव।

उपरोक्त ग्रामों के संबंध में बिंदु-वार अनुपालन रिपोर्ट संलग्न है। अतः आपसे अनुरोध है कि उपरोक्त पर विचार करने की कृपा करें।

धन्यवाद

कार्य प्रबंधक
एन0सी0सी0, झाँसी।

प्रतिलिपि -

1. मुख्य अभियंता, जल निगम (ग्रामीण), झाँसी।
2. अपर जिलाधिकारी, नमामि गंगे एवं ग्रामीण जलापूर्ति, झाँसी।
3. टीम लीडर, टीपीआई/पीएमसी, झाँसी।

NCC LIMITED

Water & Environment Division, C/o Ramesh Prasad Gupta, A4, Phase - 1, Growth Centre,
Jhansi (Dist), U.P - 284135. CIN: L72200AP1990PLC011146



Scanned with OKEN Scanner

GULARA GOV WSS-JHANSI

Date of Inspection- 10.05.2026
Block- Chirgaon

Gram Panchayat	RV Name	Points raised by SWSM Team			Reply by Agency	Photos
		Road Restoration Status	Water Supply Status	Specific issue found at site		
Jarayai	Jarayai	100%	Regular /No time schedule	-	Water is supplying as per Roster. Sometimes, water supply is disrupted due to erratic power supply.	

BACHAULI GOV WSS-JHANSI

Date of Inspection- 10.05.2026
Block- Badagaon

Gram Panchayat	RV Name	Points raised by SWSM Team			Reply by Agency	Photos
		Road Restoration Status	Water Supply Status	Specific issue found at site		
Barata	Barata	100%	Regular /No time schedule	-	Water is supplying as per Roster. Sometimes, water supply is disrupted due to erratic power supply.	

TILAETHA GOV WSS-JHANSI

Date of Inspection- 10.05.2026
Block- Badagaon



Gram Panchayat	RV Name	Points raised by SWSM Team			Reply by Agency	Photos
		Road Restoration Status	Water Supply Status	Specific issue found at site		
Kolwan	Kolwan	95%	Irregular /No time schedule	No Water Supply & no pipeline laying in Nohtachir.	As per instructions, we have re-laid 1.6 km pipe along with an alternative alignment to ensure 100% water supply coverage. This work will be completed within a week. Road restoration work 100% completed. Additionally, regarding Notachhir, the work has been completed and commissioned as per the approved drawing.	
Tendol	Tendol	100%	Regular /No time schedule	No Water Supply in 10-12 Houses.	Water supply is regular. However, in some houses people have installed Tullupumps/motors, which results in huge wastage of water.	
Tilaetha	Tilaetha	100%	Regular /No time schedule	-	Water is supplying as per Roster. Sometimes, water supply is disrupted due to erratic power supply.	



BURPURA GOV WSS-JHANSI

Date of Inspection- 09.05.2026

Block- Babina

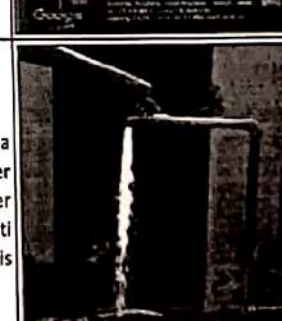Points raised by SWSM Team					Reply by Agency	Photos
Gram Panchayat	RV Name	Road Restoration Status	Water Supply Status	Specific Issue found at site		
Thakurpura	Ganeshpura	100%	Irregular /No time schedule	No Water Supply in Thakurpura approx. 50 FHTC	Water supply is regular. The sluice valve has now been repaired. However, in some houses people have installed Tulupumps /motors, which results in huge wastage of water.	
Rasoi	Rasoi	100%	Regular /No time schedule	No Water Supply in 4 Habitation. Pipeline not laying in 2 Habitation.	We have completed the work as per design and drawing and are supplying water as per designed ESR capacity. As per instructions, we re-laying 2.4 km pipeline along with an alternative alignment to ensure 100% water supply coverage. Furthermore, 2 Habitation (Khadiri and Gujar Majra's) are also not within our scheme.	
Chamaraua	Chamaraua	90%	Regular /No time schedule	No Water Supply in 10-15 Houses in Chamrauha & 50 Houses of Pal Basti	As per instructions, we re-laying 2.0 km pipeline along with an alternative alignment to ensure 100% water supply coverage. Road restoration work 100% completed.	
Baidaura	Baidaura	100%	Regular /No time schedule	No Water Supply in approx. 20 Household in Tunka	We have completed the work as per design and drawing and are supplying water regularly. We re-laying 550-meter pipeline to ensure a 100% water supply. 400 meters of the pipeline work has been completed, but the remaining 150 meters of work is pending due to permission from the landowner.	
Kilchwara Bujurg	Kilchwara Bujurg	100%	Regular /No time schedule	No Water Supply in Mati Habitation	This village actually receives a 100% regular water supply as per the roster. The lack of water supply mentioned in Mati Habitation, which is not in this village.	





NCC

Ref: NCC/W&E/GBT&Burpura -Jhansi/Pln/2026-27/851
Date: June 01, 2026

To
The Executive Engineer,
Jal Nigam, Jeevan Shah Tirha,
Gwalior Road, Dist. Jhansi, Uttar Pradesh

Sub: "Reply to the SWSM Team, Lucknow compliance" Construction of GBT & Burpura Gov Water Supply Scheme, District- Jhansi (Based on Surface Water) and relevant works including Commissioning and Operation & Maintenance for 10 Years - Reg

Ref: 1) Agreement No.10/ED/2020-21, dated 01/07/2020
2) Agreement No.11/ED/2020-21, dated 01/07/2020
3) SWSM letter No 722/JM/WQ-2/Vol-1/2025-26 (Tech), dated 26/05/2026

Dear Sir,

We are writing to provide our point-wise compliance response to the SWSM team, Lucknow, following their recent site visits. The visits were conducted across the Badagaon, Chirgaon, and Babina blocks in the Jhansi district, and included inspections of the Intake Well-cum-Pump House. The specific locations visited were:

- Badagaon Block: Kolwan, Tendol, Tilaetha, and Baratha villages
- Chirgaon Block: Jaryai village
- Babina Block: Ganeshpur, Rasoi, Chamraua, Baidura, and Kichwara villages

Please find our point-wise compliance detailed below.

- 1) We have strictly adhered to the scheduled water supply roster and maintained water quality by periodically testing physical, chemical, and bacteriological parameters in accordance with established norms for the aforementioned villages. However, we have identified numerous areas where beneficiaries are using suction pumps and booster motors, leading to excessive water consumption. Since we lack the authority to penalize or stop this practice, the Department must take immediate enforcement action for above said villages.
- 2) Kolwan village under Badagaon block has a total of 220 water connections. While the majority receive a regular water supply, a few connections could not be reached due to the high elevation. Despite trying multiple solutions, the issue could not be resolved. Consequently, as per instructions, we have re-laid 1.6 KM of 100 mm DI K7 pipe along with an alternative alignment to ensure 100% water supply coverage. This work is currently in progress and will be completed shortly. Additionally, regarding Notachhir, the work has been completed and commissioned as per the approved drawing".
- 3) Regarding the issue mentioned in reference letter No. 3, there is no water supply in the 'Mati Habitation' of Kilchwara Bujurg village. However, this village actually receives a 100% regular water supply as per the roster. The lack of water supply mentioned is actually in Mazara, not in this specific village habitation.

NCC LIMITED

Water & Environment Division, C/O Anju Yadav House, Block - C, Pasupati Homes, Besides Baragaon Block Office, Bachouli, Jhansi (Dist), U.P - 284121. CIN: L72200AP1990PLC011146





NCC

Contd ... 02

:: 02 ::

Thank you and look forward to your kind cooperation in this regard.

Yours faithfully,

for NCC Limited

R.L. [Signature]
Project in charge



Copy to:

- a) The Chief Engineer, UPJN, Jhansi – Kind information
- b) The ADM, Dist. Nodal Head, Jhansi – Kind information
- c) The Team Leader, PMC / TPI, Jhansi – for information

NCC LIMITED

Water & Environment Division, C/o Anju Yadav House, Block - C, Pasupati Homes, Besides Baragaon Block
Office, Bachouli, Jhansi (Dist), U.P - 284121. CIN: L72200AP1990PLC011146

