




Completion Plan of Dhrauli-GP, Bahadurpur- Block, District- Prayagraj

Agency of construction : LARSEN & TOUBRO LTD
 Drilling Started On : 12-07-2023
 Drilling Completed On : 21-07-2023
 Assembly lowered on : 22-07-2023
 Size of bore : 600mmφ from GL to 65m BGL
 450mmφ from 65m BGL to 165m BGL
 Size of tubewell : 300*150mm
 Req. Discharge : 810LPM

LOGGING REPORT

Logging report Date : 19-07-2023
 Depth Logged : 164m
 Directed by : Mr Sanjeet Sharma(Hydrogeologist)
 (All Geo Solution)
 STPI, MNIT Campus, Teliarganj
 UPJN-Prayagraj

SL.No	Depth Range in Meter B.G.L	Thickness in Meter	Remarks	Note
1	36-46	10	GOOD	All zones are intermixed with thin bands of kankar.
2	58-65	7	GOOD	
3	68-71	3	GOOD	
4	76-79	3	GOOD	
5	83-93	10	GOOD	
6	108-112	4	GOOD	
7	117-120	3	GOOD	
8	123-130	7	GOOD	
9	136-140	4	GOOD	
10	144-151	7	GOOD	

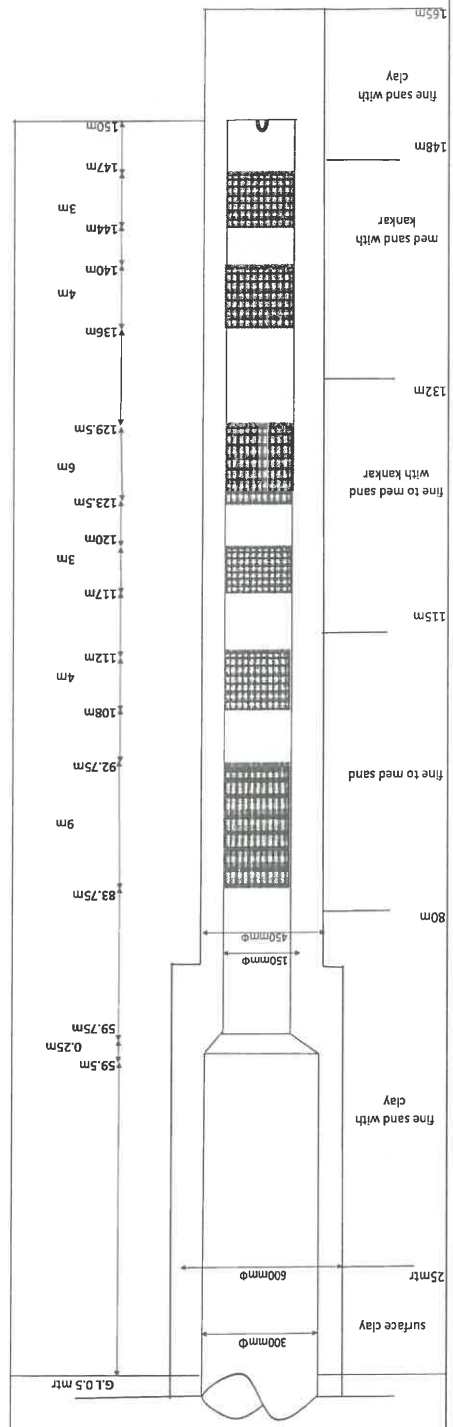

T/W Constructed By

Subhanakar sII(PM)
 L&T Construction

Sanjay Paswan
 MTCPL(TPI)

Uttendra Yadav
 Junior Engineer

(Karunakar Singh)
 Assistant Engineer

(Syed. Mohd. Shabaz)
 Executive Engineer
 Division office E&M,UP Jal Nilgam (Rural) Prayagraj
