

NAME OF THE DISTRICT-	GORAKHPUR
NAME OF THE BLOCK-	GARHA
NAME OF THE GRAM PANCHAYAT-	TIKARI
NAME OF THE VILLAGE-	TIKARI
TYPE OF RIG M/C-	RC
SIZE OF BORE-	550/500 mm φ
STATIC WATER LEVEL-	12 M
A.B. Incharge	

DISCHARGE - 400 LPM

DEPTH B.G.L. IN METER	0 M
BORING CHART	
STRATA	CL

EXECUTED ASSEMBLY

200 mm Dia Housing Pipe A.G.L. = 0.50 m	36.10 m
200 mm Dia Housing Pipe	35.80 m
150 mm Dia BLIND pipe 35.80 m to 103.20 m	103.20 m
150 mm Dia SLOTTED pipe 103.20 m to 109.85 m	109.85 m
150 mm Dia BLIND pipe 109.85 m to 116.54 m	116.54 m
150 mm Dia SLOTTED pipe 116.54 m to 119.56 m	119.56 m
150 mm Dia BLIND pipe 119.56 m to 133.56 m	133.56 m
150 mm Dia SLOTTED pipe 133.56 m to 138.59 m	138.59 m
150 mm Dia BLIND pipe 138.59 m to 138.61 m	138.61 m


35.80 M  
35.60 M

ASSEMBLY

Total Assembly = 138.61 m + A.G.L. (m) = 139.11 m
1. Drilling Started - 21/1/22
2. Drilling Completed/Lowering - 150.0 M
3. Drilling Depth (m) - 139.11 M
4. Assembly Lowered (m) - 139.11 M
5. Housing Pipe (m) - 36.10 M
6. Plain Pipe (m) - 84.73 M
7. Slotted Pipe (m) - 100.8 M
8. Reducer (m) - 0.20 M

LOGGING REPORT

1. 22 - 38 → 16.0	CLAY	150.0 M
2. 45 - 50 → 5.0		134.0 M
3. 53 - 60 → 7.0		
4. 92 - 96 → 4.0		
5. 102 - 110 → 8.0		
6. 116 - 120 → 4.0		
7. 123 - 133 → 10.0		

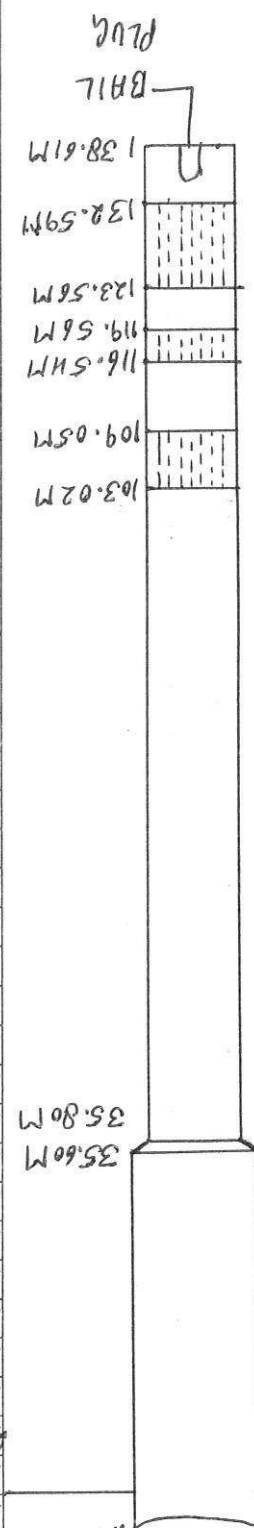

SOUND TEST  
VERTICALITY TEST  
NCC LTD.

(Mandu Meena) (Babbar gada)

(Mandiraj)

E.E.
