



KALPA-TARU

aarvee associates
architects engineers & consultants pvt. ltd



QUALITY MANAGEMENT SYSTEM

Format No :
KPTL/232221F/00023

DEPTH OF STARTA

PROPOSED ASSEMBLY DETAILS

Block- Sheetalpur

GP- Kusari

SL. DPR Details -

Lowering Date - 21/04/2023

1 Water Discharge in LPM - 350

2. Bore well Drilling dia- 500mm.

3. Bore well Drilling depth- 110m


LOGGING REPORT

Depth- 110m

Date- 15/04/2023

SL.	Depth Range	Thickness	Remarks
1	42-50	08 m	
2	50-77	19 m	
3			
4			
5			
6			
7			
8			
9			
10			
11			

G.L.

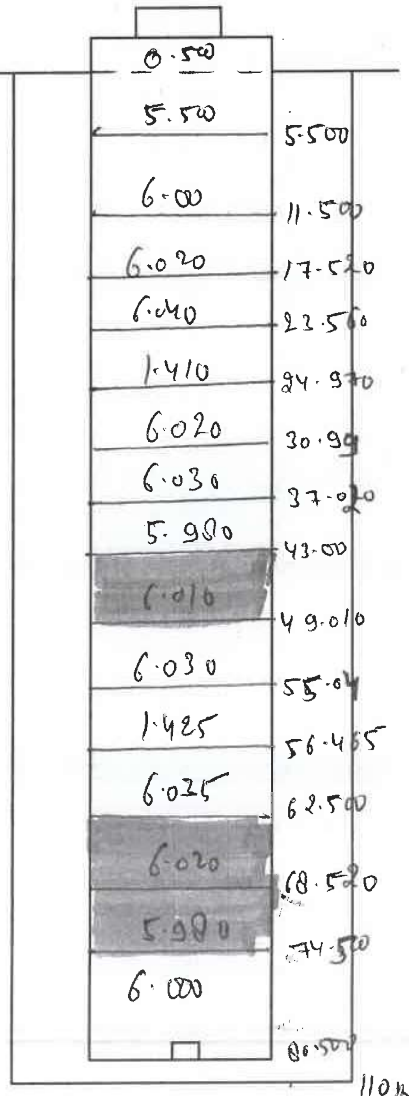

110m

Assembly Details

Total Assembly - 81.00m

Proposed Assembly for Lowering

1. 300mm dia MS Plain Pipe-

2. 200mm dia MS Plain Pipe 69.990m

3. 200mm dia MS Slotted Pipe- 18.01m

4. 200mm dia LCG Pipe -

5. 300/200 mm dia Reducer -

6. MS Bail Plug- 01

7. MS Ring 300mm-

8. MS Ring 200mm- 14.

9. MSSl Clamp- 01

10. Centre Guide - 03

11. TW Assembly Support- 01

12. Pea Gravel Packing- 19.01 Lvm

13. Maxwell Cap - 01

Backs
KPTL

TPI
TPI

CLIENT (UPJN)

Lowering work
executed as per
assembly chart.
