



**darvee associates**  
architects engineers & consultants pvt. ltd



QUALITY MANAGEMENT SYSTEM

Format No :  
KPTL/232221F/00023

DEPTH OF STARTA

**PROPOSED ASSEMBLY DETAILS**

Block- Shitelpur

GP- Calgachi

SL.	DPR Details -
	Lowering Date - 18/2/23
1.	Water Discharge in LPM - 460 LPM
2.	Bore well Drilling dia- 500 mm
3.	Bore well Drilling depth- 110 m for


**LOGGING REPORT**

Depth-	Date-	14/2/23	
SL.	Depth Range	Thickness	Remarks
1	37-48	11	
2	56-77	25	
3	82-93	10	
4			
5			
6			
7			
8			
9			
10			
11			

**Assembly Details**

**Proposed Assembly for Lowering**

1.	300mm dia MS Plain Pipe-	
2.	200mm dia MS Plain Pipe	23.02
3.	200mm dia MS Slotted Pipe-	24.06
4.	200mm dia LCG Pipe -	
5.	300/200 mm dia Reducer -	
6.	MS Bail Plug-	01
7.	MS Ring 300mm-	
8.	MS Ring 200mm-	16
9.	MSSI Clamp-	01
10.	Centre Guide -	03
11.	TW Assembly Support-	01
12.	MS Well Cap -	01
13.	Pea Gravel Packing-	22

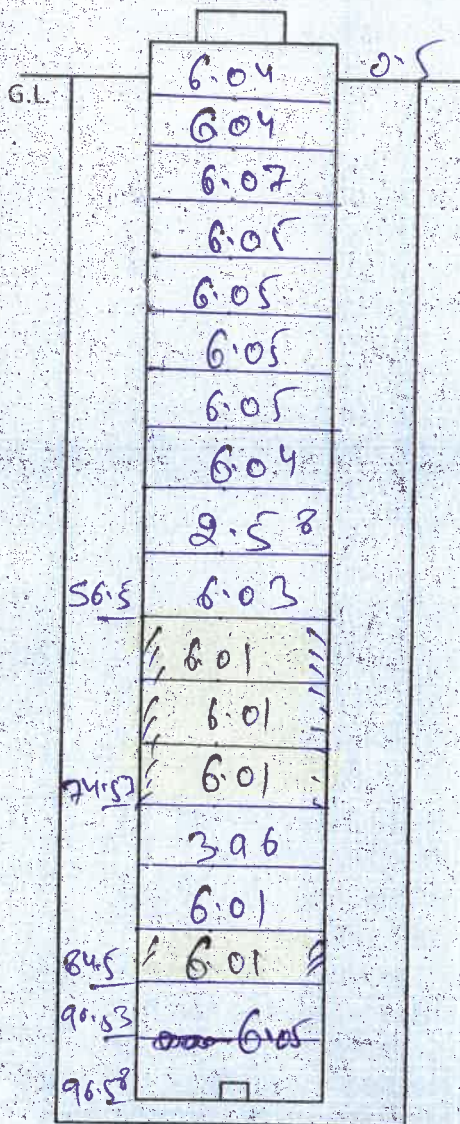

Total Length = 96.58 + 5 = 101.58

KPTL

TPI

CLIENT (UPJN)

Lowering work executed as per assembly work
