
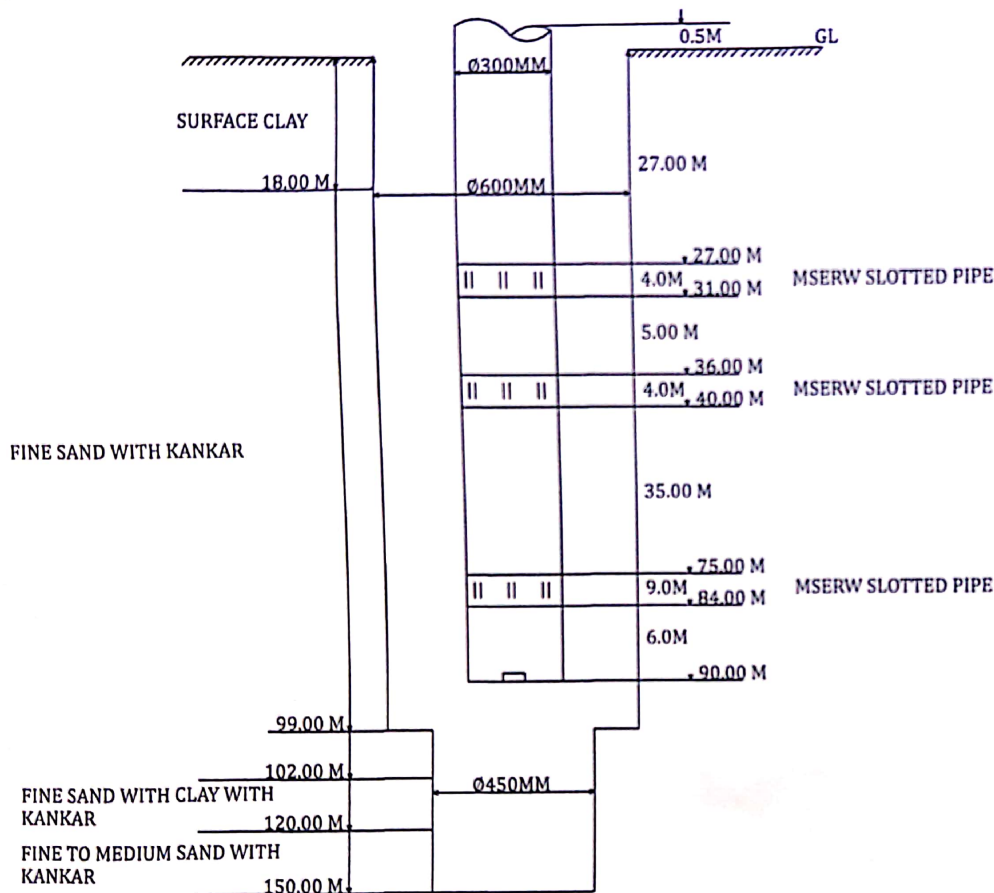


JMC-LCEPL JOINT VENTURE
JAL JEEVAN MISSION PROJECT: PRATAPGARH, U.P.



(A) PROPOSED TUBE WELL ASSEMBLY LOWERING DETAILS

Actual

1.	DISTRICT-PRATAPGARH
2.	BLOCK- SADAR
3.	VILLAGE- BADHANI
4.	DATE OF LOGGING- 06.05.2023
5.	DATE OF LOWERING- 12.05.2023
6.	SIZE OF ASSEMBLY - 0300MM X 0300MM
7.	SIZE OF BORE- GL TO 150M BGL- 0600MM X 0600MM 150M TO 150M BGL- 0450MM X 0450MM
8.	REQUIRED DISCHARGE- 402LPM
9.	LOGGING DEPTH- 150M BGL
10.	LOGGING BY- M.C. GEO SOLUTIONS <i>Mumbai Tech,</i>
11.	MSERW SLOTTED PIPES-0300MM= 17M

-- LOGGING REPORT--

S.N.	DEPTH RANGE (M)	THICKNESS (M)	WATER QUALITY
1.	16-20	04	GOOD
2.	24-31	07	GOOD
3.	36-40	04	MODERATE
4.	75-84	09	MODERATE

- NOTE:**
- 1) Fine bands of Kankar are Intemixed with almost all the Zones.
 - 3) Quality of Ground Water Is deteriorating In marginal to saline Below 90.0M BGL to till Depth Logged.
 - 4) Please ensure pre-monsoon water level before lower the well Assembly.

LOGGING REPORT VERIFIED BY GURAV. SHUKLA (ASST. HYDRO.)
YANTRIK MANDAL UP JAL NIGAM (RURAL), PRAYAGRAJ

CLIENT: STATE WATER SANITATION MISSION
(NAMAMI GANGE & RURAL WATER SUPPLY DEPARTMENT)
GOVERNMENT OF UTTAR PRADESH.

PROJECT: PRATAPGARH GROUP OF VILLAGES WATER
SUPPLY SCHEME

EPC CONTRACTOR: JMC - LCEPL JOINT VENTURE
6TH FLOOR, KALPATARU SYNERGY, OPP. GRAND
HYATT, SANTACRUZ EAST, MUMBAI 400055.

NAME	SIGN	TITLE	SCALE
DRWN: RAHUL RANJAN		PROPOSED TUBE WELL ASSEMBLY LOWERNG DRAWING BADHANI WATER SUPPLY SCHEME	
DSGN			PROJECTION
CHKD			
APPD			
DATE:	11.05.2023	SHEET NO.:	01 OF 01
DRAWING NO.	00-WSE-CV-GA-95	SIZE	AA
		REV.	RS

JMC PROJECT(I) LIMITED

TPIA

JE

AE

EE
