



LARSEN & TOUBRO

L&T Construction
Water & Effluent Treatment
8/18, Stanley Road
Judges Colony
Prayagraj-211002
Uttar Pradesh, INDIA
www.Lntecc.com

Ref.: LTCD/SITE/WET-IC/RWS/PRAYAGRAJ/2021/210

Date: 29.03.2022

To,
The Executive Engineer (E&M),
Second CD Jal Nigam,
407 New Mumfodganj
Prayagraj (U.P.) 211002

Sub: - Survey, Design, Preparation of DPR, Construction, Commissioning and O&M for 10 years of various rural water supply project in the state of Uttar Pradesh as per request for proposal for division Prayagraj
District-: Regarding Submission of bore hole Logging Report Gram Panchayat – Udaepur Gram Panchayat - Block -Pulphur.

DEAR SIR,
With reference to the above-cited subject, we would like to inform your good office that we are hereby submitting the Bore Hole Logging Report Udaepur Gram Panchayat Block – Pulphur which bore hole already done.

We request you to kindly review above Logging Report Udaepur Gram Panchayat Block – Pulphur and send your approval for further action.

Thanking you and assuring best of our services at all time, we remain.

Yours Truly,
For Larsen & Toubro
Construction Division

(Jai Prakash Singh)
DGM (Civil)

Ref. No. : AGS/EL/2022/04
 Date : 28/03/2022

GEOPHYSICAL BOREHOLE LOGGING REPORT


Site Name	Village- Udaepur	Block	Phoolpur
District	Prayagraj	State	Uttar Pradesh
Coordinates	25.576747, 82.045038		
Date of Logging	26/03/2022		
Logging Depth	169 Mbgf ?	Drilling Depth	174 Mbgf (As Reported By Driller) ?
Parameter Used	SP, Short Normal Resistivity (N16), Long Normal Resistivity (N64) and Lateral		
Logged By	Sanjeet Sharma	Logger Make	GIT
Tube well Drilled By	M/S L&T, Prayagraj, Uttar Pradesh		
Representative	Mr. Nitin Tripathi		

S. No	Depth (Mbgf)		Thickness (In Meter)	Quality Remarks (in term of Salinity)
	From	To		
1	22	25	3	Good
2	77	85	8	Good
3	105	112	7	Good
4	123	126	3	Good
5	130	133	3	Good
6	138	145	7	Good
7	150	153	3	Good

Note: Sr no 3, 5 and 7 are Higly kankar intermixed, and all zone are intermixed with fine bands of kankar

Verified as per logs provided.

ASSISTANT HYDROGEOLOGIST
 KANERIK MANDAL
 U.P. JAL NIGAM (RURAL)
 28 PRAYAGRAJ



**LARSEN & TOUBRO LTD.- PRAVAGRAJ TUBEWELL SCHEME
PROPOSED ASSEMBLY LOWERING DETAIL**

Name of Scheme: Udaipur-Phoolpur block
Letter Ref. NO :

Agency of construction: LARSEN & TOUBRO LTD

Assembly lowered on :
Size of tubewell :
Req. Discharge :

200x150mm
430LPM


LOGGING REPORT

Logging report Date : 26-03-2022

Drilled Depth : 174.0mtr
Depth Logged : 165 mtr

Directed by :

Dr.S.SHUKLA
MANAGER(GROUND WATER)
U.P.JN-LUCKNOW

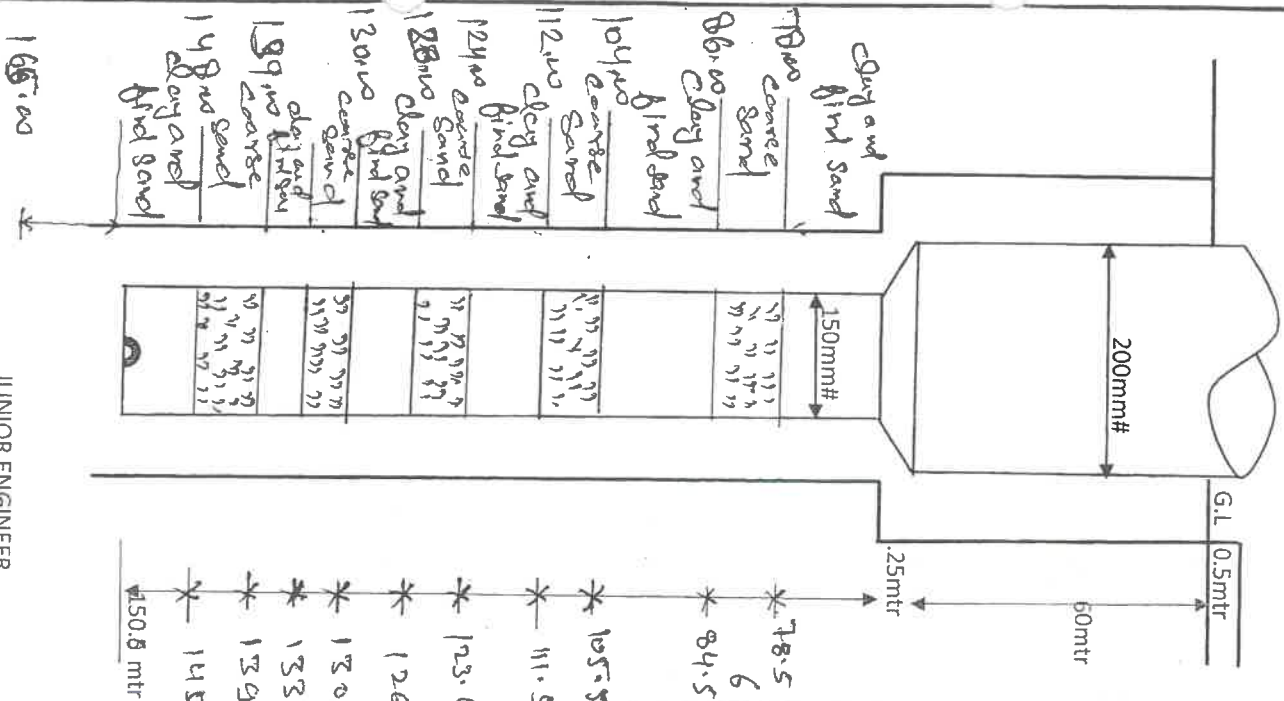

SLNO	Depth Range in Meter B.G.L	Thickness in Meter	Remarks
1	22.0-25.0	3	GOOD
2	77.0-85.0	8	GOOD
3	105.0-112.0	7	GOOD
4	123.0-126.0	3	GOOD
5	130.0-133.0	3	GOOD
6	138.0-145.0	7	GOOD
7	150.0-153.0	3	GOOD

T/W CONSTRUCTED BY
[Signature]
L&T LTD-PRAVAGRAJ

165.00

JUNIOR ENGINEER ASSISTANT ENGINEER EXECUTIVE ENGINEER
[Signature] *[Signature]* *[Signature]*
 2nd CONSTRUCTION DIVISION 2nd CONSTRUCTION DIVISION 2nd CONSTRUCTION DIVISION
 (E&M) UP JAL NIGAM (E&M) UP JAL NIGAM (E&M) UP JAL NIGAM PRAVAGRAJ
 PRAVAGRAJ PRAVAGRAJ PRAVAGRAJ
