

Scheme:- Barwa Ratapur  
 Block- Ichaulin  
 Date: 08/19/2023

Assembly Size: 300x150 mm  
 Base drilling size: 60x50 mm  
 Discharge: 10 LPM

Logged Report

So. depth thickness.

1. 30-55  $\Rightarrow$  25
2. 60-78  $\Rightarrow$  18
3. 85-92  $\Rightarrow$  07
4. 102-106  $\Rightarrow$  04
5. 115-123  $\Rightarrow$  08


Plain Pipe (150mm)      Slotted (150mm)

- |           |                      |
|-----------|----------------------|
| 1) 6.03 ✓ | 1) 6.00 ✓            |
| 2) 6.06 ✓ | 2) 6.00 ✓            |
| 3) 6.08 ✓ | 3) 6.07 ✓            |
| 4) 6.07 ✓ | 4) 6.06 = 3.06 + 3 ✓ |
| 5) 6.04 ✓ | 5) 1.05 ✓            |

6) 6.03 ✓  
 7) 6.03 = (4 + 2.03) ✓  
 8) 6.06 = (3 + 3.06) ✓

9) 6.05 ✓  
 10) 6.06 ✓  
 11) 6.05 = (1.50 + 4.55) ✓  
 12) 6.04 = (5.92 + 0.12) ✓

Total - 121.82  
 $\phi$ 300 Hauling Pipe - 36.21  
 $\phi$ 150 plain pipe - 55.28  
 $\phi$ 150 slotted pipe - 30.13

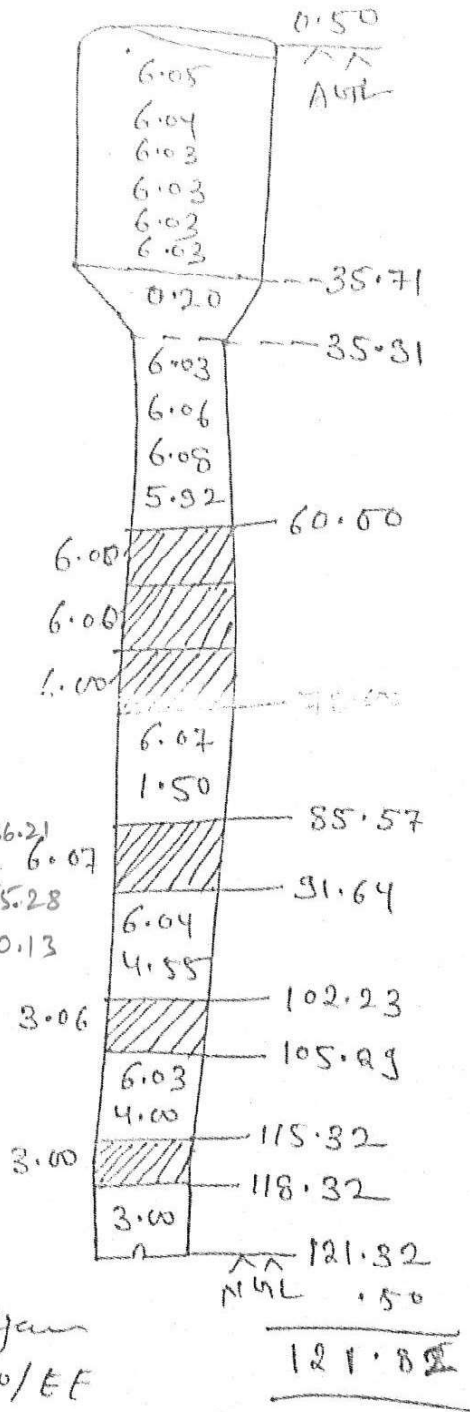

Kuldev Kumar  
 NCC Staff

TPI

Jal Nigam  
 JE/S20/EE

121.82  
 1.50  
121.82
