


Completion plan of Kolepur T.W. (Danti Group of Village W/s Scheme Under J.J.M.) Block -Chhanbay, District- Mirzapur.

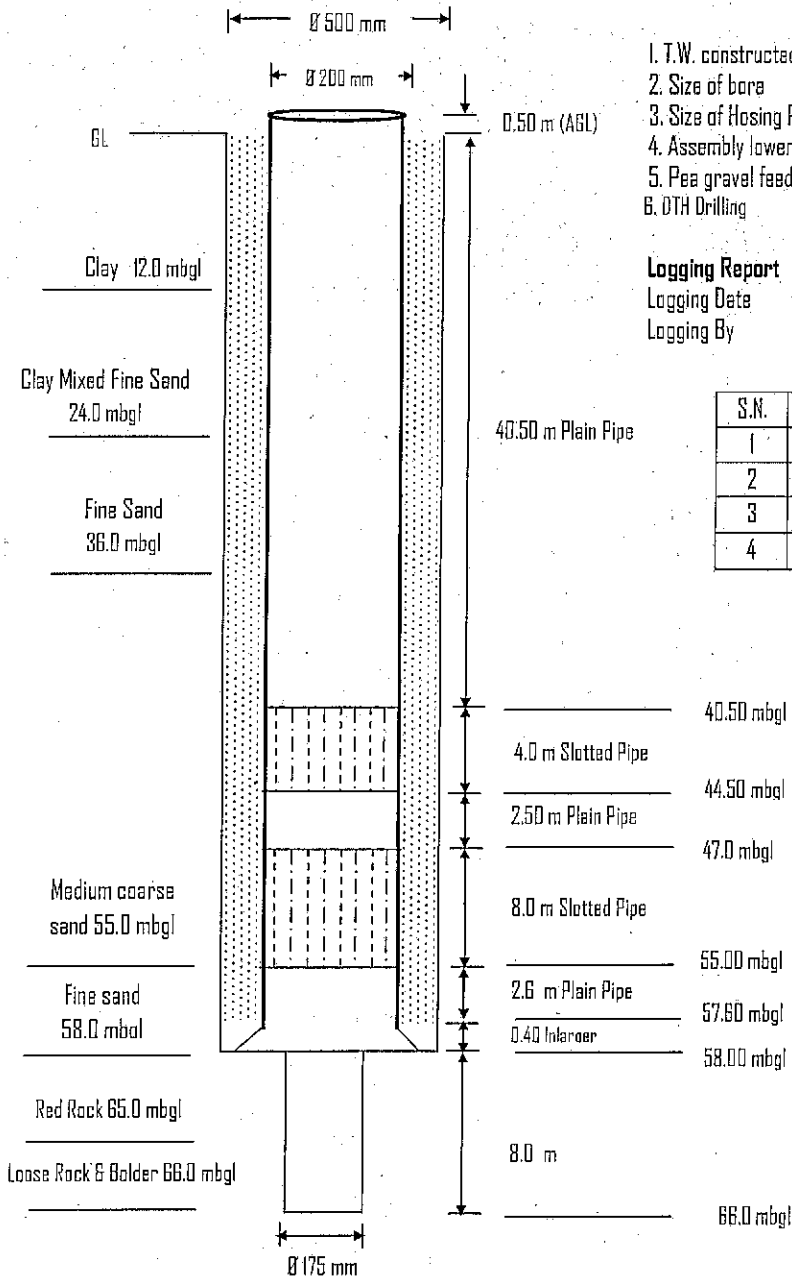

- 1. T.W. constructed by : M/S RAMKY BABA, (J.V.)
- 2. Size of bore : Dia. 500x175 mm
- 3. Size of Hosing Pipe : Dia. 200 mm
- 4. Assembly lowered on : 02.07.2021
- 5. Pea gravel feed : 02.07.2021
- 6. OTH Drilling : 07.01.2022

Logging Report

- Logging Date : 21.06.2021
- Logging By : Aqua Explore

S.N.	Depth Range in Mtr. (B.G.L.)	Thickness(Mtr)	Remarks
1	27.00 To 31.00	4.00	Good
2	33.00 To 38.00	5.00	Good
3	40.00 To 45.00	5.00	Good
4	47.00 To 55.00	8.00	Good

- 40.50 mbgl
- 4.0 m Slotted Pipe
- 44.50 mbgl
- 2.50 m Plain Pipe
- 47.0 mbgl
- 8.0 m Slotted Pipe
- 55.00 mbgl
- 2.6 m Plain Pipe
- 57.60 mbgl
- 0.40 Inlet
- 58.00 mbgl
- 8.0 m
- 66.0 mbgl

(RAMKY BABA (J.V.)
Contractor

PMC

TPI

(M.K. Maurya)
Junior Engineer

(S.K. Yadav)
Assistant Engineer

(G.P. Singh)
Executive Engineer
