

**Completion Plan Of Tubewell**

Name Of Work :- Construction of T. W. of G.P. Majhara Purab, Block- Ramia Behar, District, Lakhimpur Kheri.

Name Of Program :- J. J. M-2

Name Of client :- S.W.S.M. & U.P. JAL NIGAM ( R )

Name Of Contractor :- M/S NCC Limited


Name Of TPI :- Ceinsys Tech Limited

Contract Agreement :- 64/ED/2020-21 Dt. 12.03.2021

Cover Agreement :- 464/ED/Phase-2/2022-23/XI, Dt. 27.02.2023

**Lowered Assembly Chart of T. W of Majhara Purab G.P W/S Scheme District :- Lakhimpur Kheri.**

Strata		
0	-	5 M. Surface Soil
5	-	10 M. Clay Kankar
10	-	38 M. Medium Sand
38	-	45 M. Clay Kankar
45	-	80 M. Medium Sand
80	-	87 M. Clay Kankar
87	-	100 M. Medium Sand
100	-	106 M. Kankar
106	-	126 M. Medium Sand
126	-	132 M. Clay Kankar
132	-	138 M. Medium Sand
138	-	153 M. Clay Kankar
153	-	165 M. Medium Sand

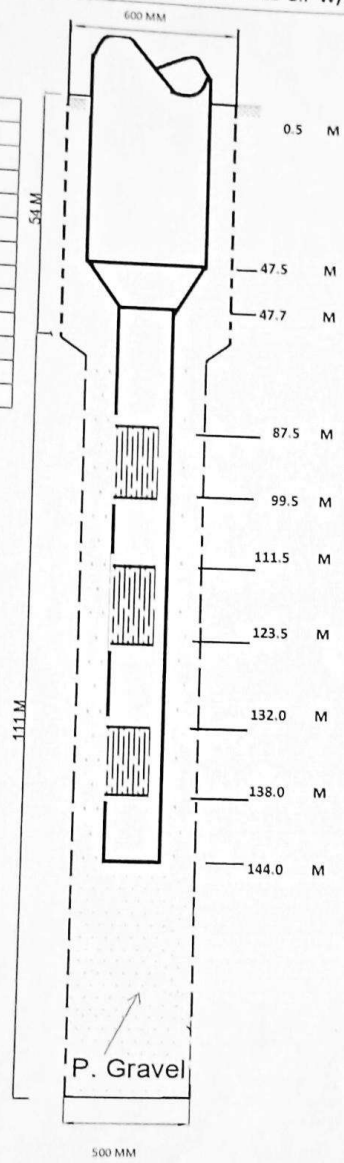

ABSTRACT		
1	Type of Rig Machine	:- DC/RC
2	Static Water level	:-
3	Required Discharge	:- 1580 LPM
4	Bore Size (MM)	:- 600 X 500
5	Assembly Size (MM)	:- 300 X 200
6	Drilling Starting Date	:- 07-05-2023
7	Drilling Completion Date	:- 11-05-2023
8	Total Depth Of Drilling	:- 165 M
9	Logging Date	:- 12-05-2023
10	Logging Depth	:- 165 M

Logging Report			
Sl No	Depth (mbgl)	Thickness (m)	Remarks
1	45 - 80	35	(Good All)
2	87 - 100	13	
3	106 - 126	20	
4	132 - 138	6	

11 Details of Lowered Assembly			
i)	300	MM Dia Housing Pipe	:- 48.0 M
ii)	200	MM Dia M. S. Slotted pipe	:- 30.0 M
iii)	200	MM Dia M. S. Plain pipe	:- 66.3 M
iv)	300 X 200	MM Dia M S Reducer	0.2 M
		Total	:- 144.50 Meter
		AGL	:- 0.50 Meter
		BGL	:- 144.00 Meter
12	Date of Lowering	:-	13-05-2023

Recommended & Prepared by  
M/S. NCC Ltd.

Verified by  
M/S. Ceinsys Tech Ltd.

**VIKAS K B YADAV**  
 JUNIOR ENGINEER  
 DIVISIONAL OFFICE (E&M),  
 U.P. JAL NIGAM (R)  
 LUCKNOW

Recommended by  
  
**A E E**  
 13th Division UP Jal Nigam (R) Lucknow  
 Assistant Engineer  
 Divisional officer (E&M)  
 U.P. Jal Nigam (R)  
 Lucknow

Approved by  
**E E**  
 13th Division U P Jal Nigam  
 (R) Lucknow

# REPORT ON GEOPHYSICAL WELL LOGGING AT

GRAM PANCHAYAT- MARJA PURAB, BLOCK- RAMIYA BEHAD,  
DISTT-LAKHIMPUR KHIRI  
UNDER  
JAL JIVAN MISSION

**Introduction :**

A Deep bore hole was drilled 165 mtrs. depth. and Logged depth 165 mtrs. at above site. Was drilled by M/s NCC, Lakhimpur Khiri.

On the request of M/s NCC, Lakhimpur Khiri. a Geophysical well Logging in the above bore hole using IGIS Well Logger on 12.May.2023.

Logging Para meters - Self potential, short normal (N-16), Long Normal (N-64), Lateral. Details of major Aquifer formations explored from logging of bore hole combined with the study of Strata Chart prepared from drill cuttings are given in the following table:-

Mud Resistivity = 23.30 Ohms.

Drilling Water Resistivity = 24.42 Ohms.

Approx Water Level = 3 Mtr.

S.No.	Depth range(m)	Thickness(m)	Lithology	Expected Water Quality
1.	0 - 5	5	Surface soil	
2.	5 - 10	5	Clay kankar	
3.	10 - 38	28	Medium sand	Good
4.	38 - 45	7	Clay kankar	
5.	45 - 80*	35	Medium sand	Good
6.	80 - 87	7	Clay kankar	
7.	87 - 100*	13	Medium sand	Good
8.	100 - 106	6	Kankar	
9.	106 - 126*	20	Medium sand	Good
10.	126 - 132	6	Clay kankar	
11.	132 - 138*	6	Medium sand	Good
12.	138 - 153	15	Clay kankar	
13.	153 - 165*	12	Medium sand	Good

- All zones are intermixed with kankar.

13/05/23



- Logging performed as per SWSM guidelines.  
- Groundwater quality interpreted by firm as per their logger calibration log.
