

42/20/20

Lowering of Shahpajpur WLS scheme DIST - Pilibhit Block, Pooranpur
 T.W Size - 300 x 200 mm & lowering Date - 17/7/23 discharge - 690 lpm / 150/140

300mm housing pipe

- 1 - 6.00
- 2 - 6.00
- 3 - 6.00
- 4 - 6.00
- 5 - 6.00
- 6 - 6.00
- 7 - 6.00

- 42.00M

200mm Plain Pipe

- 1 - 6.02L
- 2 - 6.03L
- 3 - 6.00L
- 4 - 6.01L
- 5 - 6.04L
- 6 - 6.05L
- 7 - 6.03L
- 8 - 6.02L
- 9 - 6.03L
- 10 - 6.03
- 11 - 6.00L
- 12 - 6.01

200mm slotted Pipe

- 1 - 6.00L
 - 2 - 6.00L
 - 3 - 6.00L
 - 4 - 6.00
- 24.00M
- 3.00ML
3.00ML

5.00ML
1.03M

72.25M

Logging Report As:-

- 64m — 90m — m-sand — 6+3
- 96m — 107m — m-sand — 6
- 113m — 127m — m-sand — 6+3
- 132m — 137m — fine sand

Plain Pipe

6.03 — 5.00ML
1.03M


Slotted Pipe

6.00 — 3.00ML
3.00ML

- 300mm housing pipe — 42.00M
- 300x200mm Reducer — 0.25M
- 200mm plain Pipe — 65.21M
- 200mm slotted Pipe — 24.00M

- 131.46M
- ABL (-) 0.50M

- 130.96M

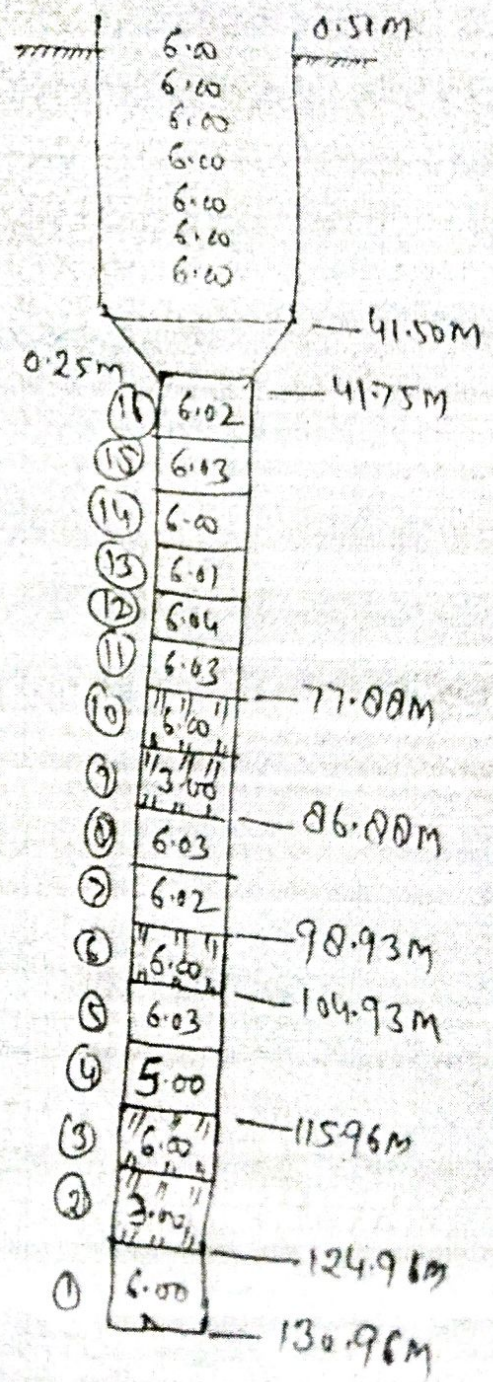

TUBEWELL ASSEMBLY CHART


PROJECT: RURAL WATER SUPPLY SCHEME UNDER SWSM-IJM
 EPC CONTRACTOR: VISHVARAJ ENVIRONMENT PVT.LTD
 COVER AGREEMENT No.: 564 ED/PHASE-3/2022-23 IV
 SCHEME NAME: SHAHBAJAPUR
 LOA NO.: 564 ED/PHASE-3/2022-23 IV-20060808
 BLOCK: PURANPUR
 LOWERING DATE: 17/7/2023

LIST OF TUBE WELL ASSEMBLY UNITS

SR. NO.	DISCRPTION	QTY. (M)	DIAMETER
1	PLAIN PIPES	42.00	300 mm
2	PLAIN PIPES	65.21	200 mm
3	SLOTTED PIPES	24.00	200 mm
300 mm	MM DIA PLAIN PIPES		42.00 M
300X200	MM DIA REDUCER		0.25 M
200 mm	MM DIA PLAIN PIPES		65.21 M
200 mm	MM DIA SLOTTED PIPES		24.00 M
TOTAL DEPTH			131.46 M
TOTAL LOWERING DEPTH			-0.50 M
TOTAL LOWERING DEPTH			130.96 M

LOGGING REPOET AS-

64 M	90 M	Medium sand
96 M	107 M	Medium sand
113 M	127 M	Medium sand
132 M	137 M	Fine & Medium sand

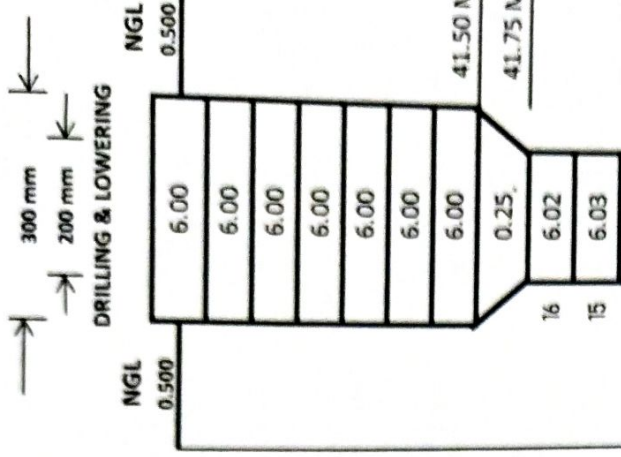

NO.	DIAMETER	LENGTH (M)	TOTAL DEPTH (M)	REMARKS
16	300 mm	6.00	6.00	NGL 0.500
15	200 mm	6.00	12.00	
14	200 mm	6.00	18.00	
13	200 mm	6.00	24.00	
12	200 mm	6.00	30.00	
11	200 mm	6.00	36.00	
10	200 mm	6.00	42.00	SLOTTED 77.88 M
9	200 mm	3.00	45.00	SLOTTED 86.88 M
8	200 mm	6.03	51.03	
7	200 mm	6.02	57.05	
6	200 mm	6.00	63.05	SLOTTED 98.93 M
5	200 mm	6.03	69.08	
4	200 mm	5.00	74.08	
3	200 mm	6.00	80.08	SLOTTED 115.96 M
2	200 mm	3.00	83.08	SLOTTED 124.96 M
1	200 mm	6.00	89.08	SLOTTED 130.96 M



Handwritten signature

M/S BLG CONSTRUCTION
(TPI)

Handwritten signature
 J.E.
 A.E.
 (E&M U.P. JAL NIGAM RURAL)
