


NAME OF THE BLOCK
 NAME OF THE GRAM PANCHAYAT
 NAME OF THE VILLAGE

Blatal
 Karmnara
 Dislong - 800 LPM.

SIZE OF BORE
 STATIC WATER LEVEL
 LE Indage
 F. Manu'sya
 LE Indage
 Babbar yadar

DEPTH B.G.L. IN METER	BORING CHART	STRATA	EXECUTED ASSEMBLY
0M		clay.	AGL + 50
24.1M		Medium sand.	
86.1M		Sandy clay.	
148.8M		Medium to fine sand.	
50.5M		Soft clay.	
61.2M		Medium sand.	
165M		clay with small konkan.	
72.8M		Coarse sand	
96M		Sandy clay with konkan.	
96.2M		Medium sand	
108.5M		hard clay.	

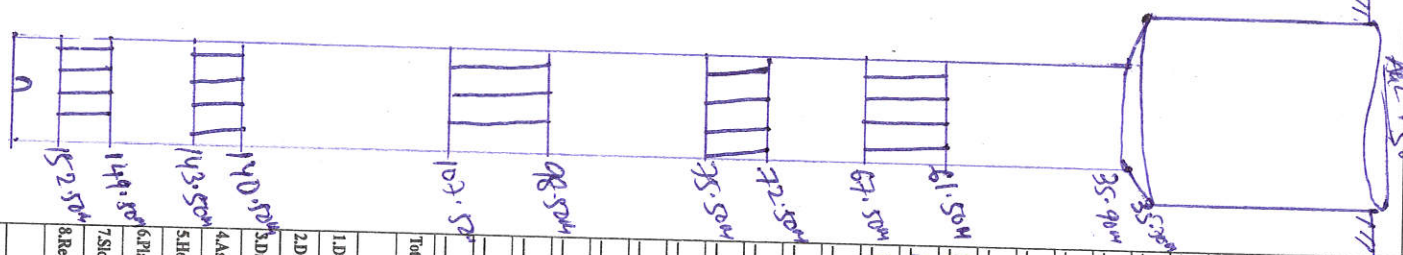

ASSEMBLY DETAILS	
300 mm Dia Housing Pipe	AGL = 52 m
300 mm Dia Housing Pipe	0 m to 35.70 m
300 mm Dia Reducer	35.70 m to 35.90 m
150 mm Dia Blind pipe	35.90 m to 61.50 m
150 mm Dia Slotted pipe	61.50 m to 63.50 m
150 mm Dia Blind pipe	63.50 m to 72.20 m
150 mm Dia Slotted pipe	72.20 m to 98.50 m
150 mm Dia Blind pipe	98.50 m to 103.50 m
150 mm Dia Slotted pipe	103.50 m to 140.50 m
150 mm Dia Blind pipe	140.50 m to 142.50 m
150 mm Dia Blind pipe	142.50 m to 149.50 m
150 mm Dia Slotted pipe	149.50 m to 150.50 m
150 mm Dia Slotted pipe	150.50 m to 158.00 m
Total Assembly = 158 m + A.G.L. (m) = 159.04m	
ABSTRACT	
1. Drilling Started -	
2. Drilling Completed/Lowering -	
3. Drilling Depth (m) - 170	
4. Assembly Lowered (m) - 159.04.	
5. Housing Pipe (m) - 36.20	
6. Plain Pipe (m) - 95.64.	
7. Slotted Pipe (m) - 27	
8. Reducer (m) - 20.	
LOGGING REPORT	
1.	24 - 36 = 12M
2.	43 - 50 = 7M
3.	61 - 68 = 7M
4.	72 - 78 = 6M
5.	98 - 108 = 12M
6.	140 - 144 = 4M
7.	149 - 153 = 3M.
8.	
9.	
10.	

SOUND TEST

VERTICALITY TEST

NCCI LTD

JE & AE

PM/CP/PLA

AGL

AGL

E.E
