


Project Name Implementation of Fatehpur District Villages Rural Water Supply Project Including O&M for 10 Year for RAMPUR THARIYANW ZONE 2 village, Block-Haswa District-Fatehpur of the State of Uttar Pradesh Under Jal Jeevan Mission

UTTAR PRADESH JAL NIGAM

ACTUAL ASSEMBLY CHART OF TUBEWELL

Name of Scheme	JAL JEEVAN MISSION PHASE-III	District	FATEHPUR
Name of Site	RAMPUR THARIYANW ZONE 2	Block	HASWA
Name of Contractor	PMPL-BRCCPL (JV)	Size of Assembly	(300x200) mm
Type of Rig. Machine	D.C.	Size of Borewell	(600x500) mm
Boring cum Assembly chart (Depth in Mtr)		Discharge	450LPM

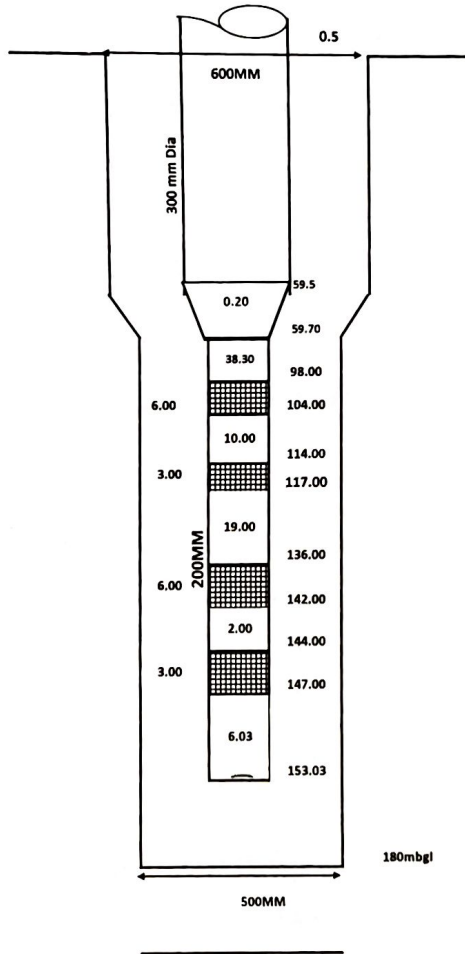

Abstract			
Date of Lowering		14-09-2023	
1	Drilling Depth.	180	mtr
2	300 mm dia Plain Housing pipe.	60.00	mtr
3	300x200 mm Dia Reducer.	0.20	mtr
4	200 mm dia Plain pipe.	75.33	mtr
5	200 mm dia Slotted pipe.	18.00	mtr
6	Total Assembly	153.53	mtr

Logging By : GEO-TECHNICAL CONSULTANT

Date of Logging					
10-09-2023					
Sl. No.	Depth Range From M.B.G.L.	Depth Range To M. B.G.L.	Thickness In Mtr.	Quality of G.W	Remarks
1	18.00	22.00	4.00	Good To Moderate	
2	34.00	37.00	3.00	Moderate	
3	43.00	48.00	5.00	Good	
4	50.00	53.00	3.00	Good	
5	91.00	95.00	4.00	Good To Moderate	
6	98.00	104.00	6.00	GOOD	
7	114.00	117.00	3.00	GOOD	
8	122.00	125.00	3.00	Moderate	
9	129.00	132.00	3.00	Moderate	
10	136.00	142.00	6.00	GOOD	
11	144.00	147.00	3.00	GOOD	

Note : 1) 23.9 OHM MTR AND RM -22.8 OHM MTR

Note : 2) BELOW 150 MBGL NOT PROPER GRANULAR ZONE ENCOUNTERED TILL LOG DEPTH.



PMPL -BRCCPL JV

*[Signature]*  
TPI ME Engg.

*[Signature]*  
Junior Engineer

*[Signature]*  
Assistant Engineer

*[Signature]*  
Executive Engineer
