




**JMC-LCEPL JOINT VENTURE**  
**JAL JEEVAN MISSION PROJECT: PRATAPGARH, U.P.**

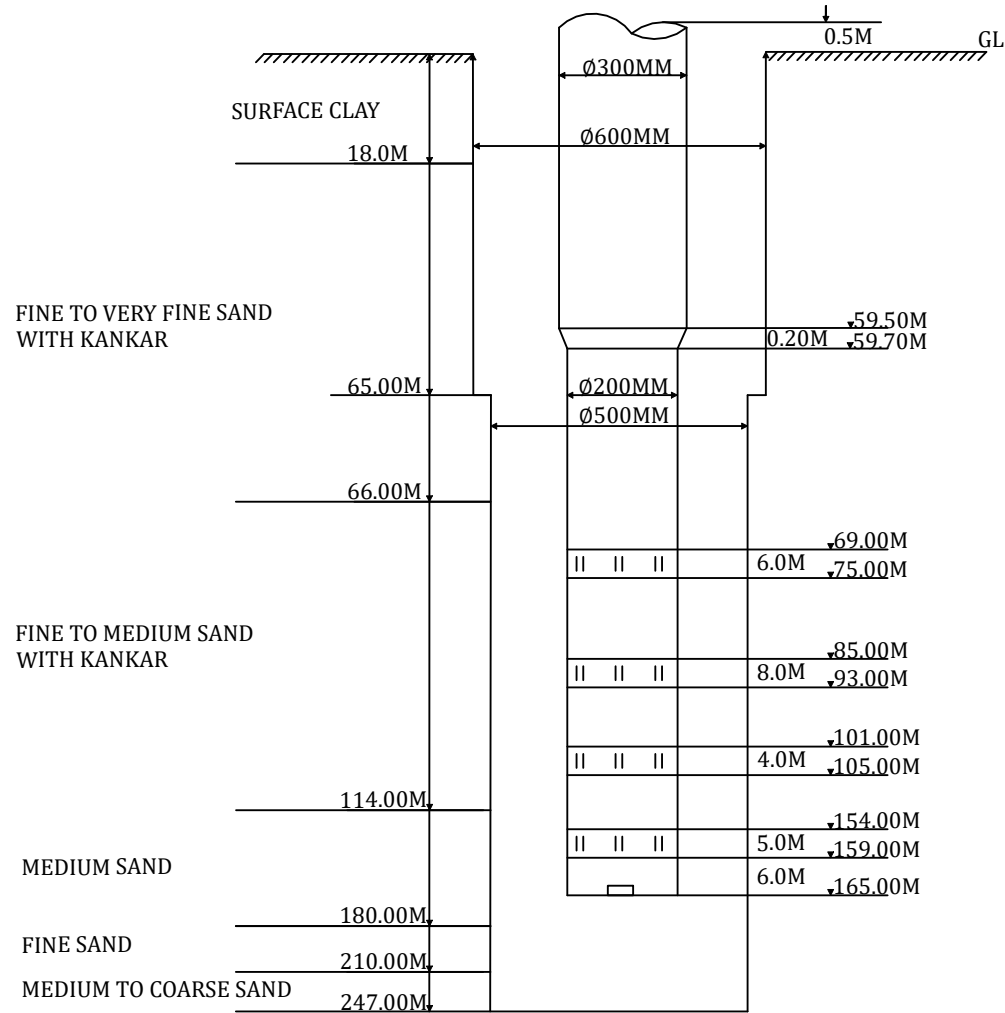

**(A) ACTUAL TUBE WELL ASSEMBLE LOWERING DETAILS**

1.	DISTRICT-PRATAPGARH
2.	BLOCK- RAMPUR SANGRAMGARH
3.	VILLAGE - JEWAIN
4.	DATE OF LOGGING- 11.09.2023
5.	DATE OF LOWERING- 16.09.2023
6.	SIZE OF ASSEMBLE - Ø300MM X Ø200MM
7.	SIZE OF BORE- GL TO 65M- Ø600MM X Ø600MM 65M TO 247M BGL- Ø500MM X Ø500MM
8.	REQUIRED DISCHARGE- 790LPM
9.	LOGGING DEPTH- 214.1M BGL
10.	LOGGING BY- GEO TECHNICAL CONSULTANT

**-- LOGGING REPORT--**

S.N.	DEPTH RANGE(M)	THICKNESS (M)	WATER QUALITY
1.	30-36	06	GOOD
2.	44-48	04	GOOD
3.	69-75	06	GOOD
4.	85-93	08	GOOD
5.	101-105	04	GOOD
6.	154-159	05	GOOD TO MODERATE

**NOTE :1)** Below 160M BGL no proper granular zone Encountered till log Depth.

CLIENT : STATE WATER SANITATION MISSION (NAMAMI GANGE & RURAL WATER SUPPLY DEPARTMENT) GOVERNMENT OF UTTAR PRADESH.

PROJECT : PRATAPGARH GROUP OF VILLAGES WATER SUPPLY SCHEME

EPC CONTRACTOR : JMC - LCEPL JOINT VENTURE  
6TH FLOOR, KALPATARU SYNERGY, OPP. GRAND HYATT, SANTACRUZ EAST, MUMBAI 400055.

NAME	SIGN	TITLE :	SCALE
RAHUL RANJAN		ACTUAL TUBE WELL ASSEMBLE LOWERING DRAWING	
DRWN		JEWAIN	PROJECTION
DSGN		WATER SUPPLY SCHEME	
CHKD			
APPD			
DATE :		SHEET NO :	SIZE REV.
DRAWING NO :		01 OF 01	A4 R0

JMC PROJECT(I) LIMITED

TPIA

JE

AE

EE
