




**JMC-LCEPL JOINT VENTURE
JAL JEEVAN MISSION PROJECT:PRATAPGARH,U.P.**

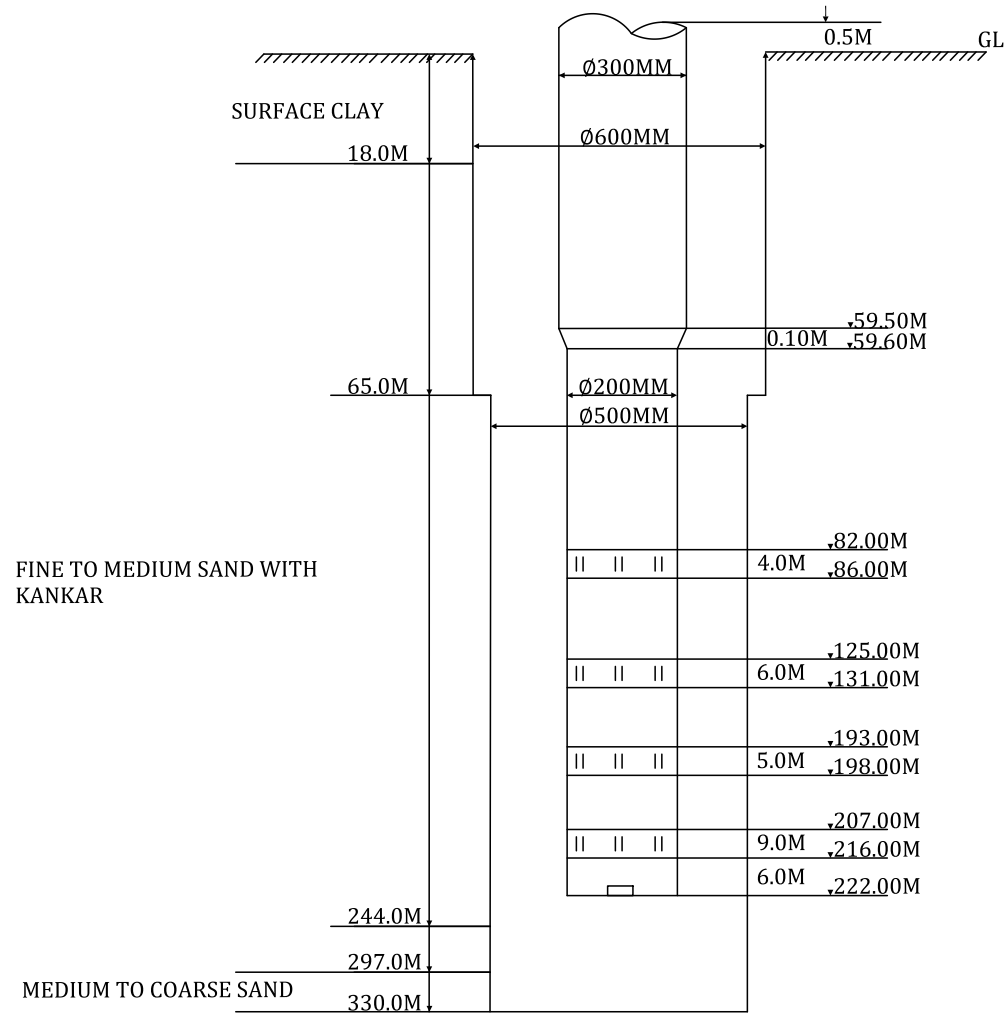

(A) PROPOSED TUBE WELL ASSEMBLE LOWERING DETAILS

1.	DISTRICT-PRATAPGARH
2.	BLOCK- RAMPUR SANGRAMGARH
3.	VILLAGE - RAMPUR KHASH
4.	DATE OF LOGGING- 31.07.2023
5.	DATE OF LOWERING-
6.	SIZE OF ASSEMBLE - Ø300MM X Ø200MM
7.	SIZE OF BORE- GL TO 65M- Ø600MM X Ø600MM 65M TO 330M BGL- Ø500MM X Ø500MM
8.	REQUIRED DISCHARGE- 825LPM
9.	LOGGING DEPTH- 287M BGL
10.	LOGGING BY- GEO TECHNICAL CONSULTANT

-- LOGGING REPORT--

S.N.	DEPTH RANGE(M)	THICKNESS (M)	WATER QUALITY
1.	36-45	04	GOOD
2.	82-86	10	GOOD
3.	125-131	04	GOOD TO MODERATE
4.	193-198	07	MODERATE
5.	207-216	06	GOOD
6.	251-256	04	MODERATE

RW-34.6 OHM MTR AND RM-16.1 OHM MTR.

NOTE :1) Below 260.0M BGL formation water is deteriorating Till log depth.

LOGGING REPORT VERIFIED BY GURAV. SHUKLA(ASST. HYDRO.) UP JAL NIGAM(RURAL) HQ, PPRBD LUCKNOW

CLIENT : STATE WATER SANITATION MISSION (NAMAMI GANGE & RURAL WATER SUPPLY DEPARTMENT) GOVERNMENT OF UTTAR PRADESH.

PROJECT : PRATAPGARH GROUP OF VILLAGES WATER SUPPLY SCHEME

EPC CONTRACTOR : JMC - LCESPL JOINT VENTURE
6TH FLOOR, KALPATARU SYNERGY, OPP. GRAND HYATT, SANTACRUZ EAST, MUMBAI 400055.

NAME	SIGN	TITLE	SCALE
DRWN RAHUL RANJAN		PROPOSED TUBE WELL ASSEMBLE LOWERING DRAWING RAMPUR KHASH WATER SUPPLY SCHEME	PROJECTION
DIGN			
CHKD			
APPD			

DATE :	04.08.2023	SHEET NO :	01 OF 01	SIZE	A4	REV.	RO
DRAWING NO :	00-WSE-CV-GA-119						

JMC PROJECT(I) LIMITED

TPIA

JE AE EE
