




**JMC-LCEPL JOINT VENTURE**  
**JAL JEEVAN MISSION PROJECT:PRATAPGARH,U.P.**

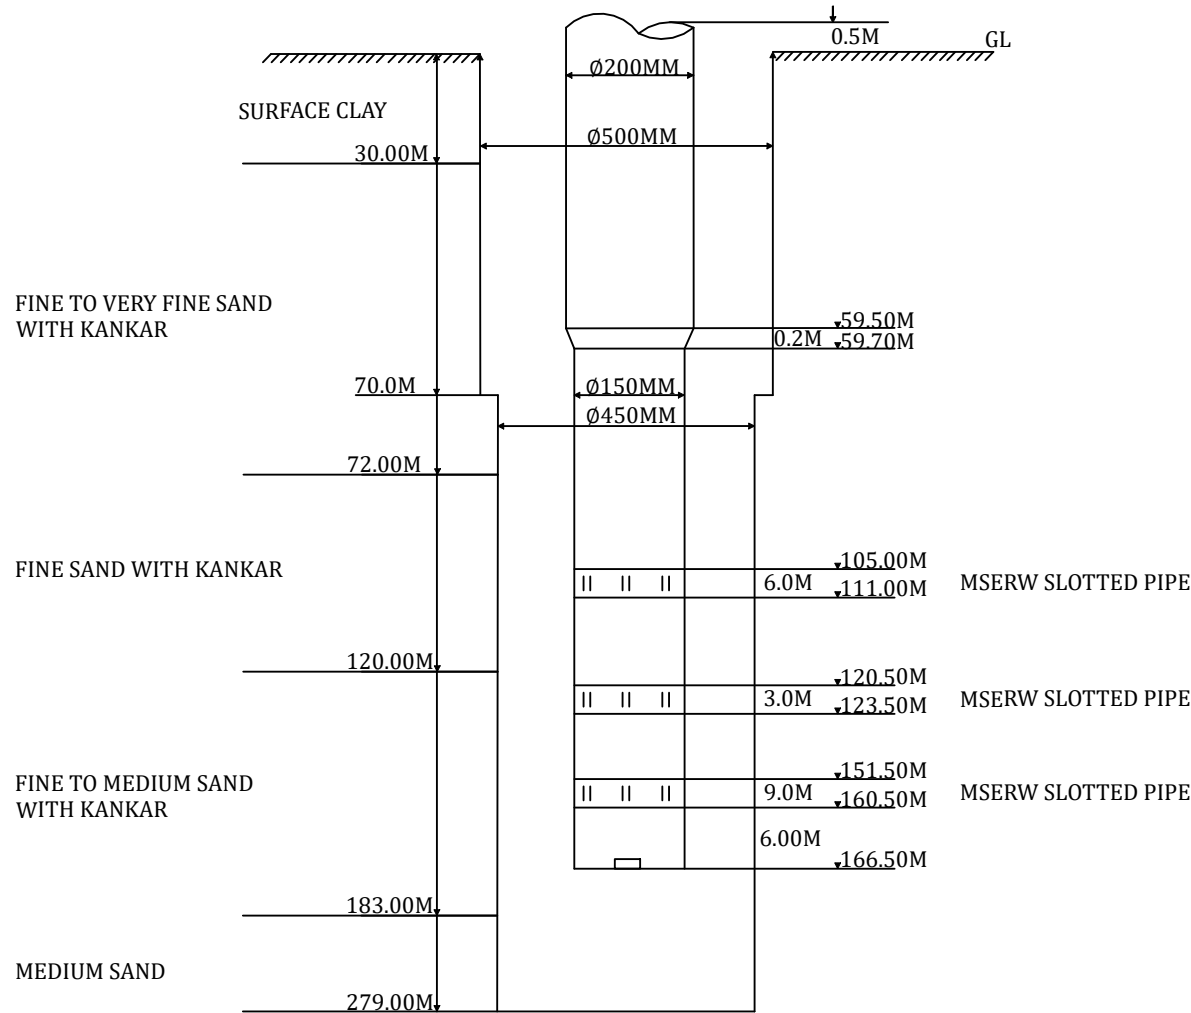

**(A) ACTUAL TUBE WELL ASSEMBLE LOWERING DETAILS**

1.	DISTRICT-PRATAPGARH
2.	BLOCK- RAMPUR SANGRAMGARH
3.	VILLAGE - PURE RAMCHANDRA
4.	DATE OF LOGGING- 08.01.2024
5.	DATE OF LOWERING- 10.02.2024
6.	SIZE OF ASSEMBLE - Ø200MM X Ø150MM
7.	SIZE OF BORE- GL TO 70M- Ø500MM X Ø500MM 70M TO 279M BGL- Ø450MM X Ø450MM
8.	REQUIRED DISCHARGE- 184LPM
9.	LOGGING DEPTH- 243M BGL
10.	LOGGING BY- ALL GEO SOLUTIONS

**-- LOGGING REPORT--**

S.N	DEPTH RANGE (M)	THICKNESS (M)	WATER QUALITY
1.	32-39	07	GOOD
2.	42-47	05	GOOD
3.	72-75	03	GOOD
4.	89-91	02	GOOD
5.	105-111	06	GOOD
6.	120-124	04	GOOD
7.	151-161	10	GOOD

Note: 1- The formation water quality is deteriorating from Marginal to saline below 170.0M BGL totill depth logged.

CLIENT : STATE WATER SANITATION MISSION  
(NAMAMI GANGE & RURAL WATER SUPPLY DEPARTMENT)  
GOVERNMENT OF UTTAR PRADESH.

PROJECT : PRATAPGARH GROUP OF VILLAGES WATER SUPPLY SCHEME

EPC CONTRACTOR  
KALPATARU PROJECTS INTERNATIONAL LIMITED  
6TH FLOOR, KALPATARU SYNERGY, OPP. GRAND HYATT, SANTACRUZ EAST, MUMBAI 400055.

NAME	SIGN	TITLE :	SCALE
RAHUL RANJAN		ACTUAL TUBE WELL ASSEMBLE LOWERING DRAWING	
DRWN		PURE RAMCHANDRA WATER SUPPLY SCHEME	PROJECTION
DSGN			⊕
CHKD			
APPD			
DATE :		SHEET NO :	SIZE REV.
DRAWING NO :		01 OF 01	A4 R0

JMC PROJECT(I) LIMITED

TPIA

JE AE EE
