


RITHWIK KOYA JV

CONSTRUCTION DIVISION (E/M) U.P. JAL NIGAM, GORAKHPUR

COMPLETION PLAN OF :- **BARWABHOJ & LODHASI** SIZE OF BORE :- **500X500 MM**
 TUBE WELL ASSEMBLY SIZE :- **200X150 MM** BLOCK :- **NAUTANWA**
 REQUIRED DISCHARGE :- **600 LPM** DISTRICT :- **MAHARAJGANJ**

Depth B.G.L Mtr	Boring Chart	Stara Details	Lowering Assembly	Assembly Details																																																																																																																																																										
0.0				<table border="1"> <tr> <td>300 m.m. Dia Housing Pipe :-</td> <td>35.54</td> <td>m</td> </tr> <tr> <td>300x150 m.m. Dia REDUCER</td> <td>35.54</td> <td>to 35.74 m</td> </tr> <tr> <td>150 m.m. Dia Plain Pipe</td> <td>35.74</td> <td>to 98.45 m</td> </tr> <tr> <td>150 m.m. Dia Slotted Pipe</td> <td>98.45</td> <td>to 104.46 m</td> </tr> <tr> <td>150 m.m. Dia Plain Pipe</td> <td>104.46</td> <td>to 112.48 m</td> </tr> <tr> <td>150 m.m. Dia Slotted Pipe</td> <td>112.48</td> <td>to 118.48 m</td> </tr> <tr> <td>150 m.m. Dia Plain Pipe</td> <td>118.48</td> <td>to 141.00 m</td> </tr> <tr> <td>150 m.m. Dia Slotted Pipe</td> <td>141.00</td> <td>to 147.02 m</td> </tr> <tr> <td>150 m.m. Dia Plain Pipe</td> <td>147.02</td> <td>to 162.03 m</td> </tr> <tr> <td>150 m.m. Dia Slotted Pipe</td> <td>162.03</td> <td>to 168.04 m</td> </tr> <tr> <td>150 m.m. Dia Plain Pipe</td> <td>168.04</td> <td>to 174.06 m</td> </tr> <tr> <td>TOTAL ASSEMBLY:-</td> <td>174.06</td> <td>+AGL 0.5 = 174.56</td> </tr> </table>	300 m.m. Dia Housing Pipe :-	35.54	m	300x150 m.m. Dia REDUCER	35.54	to 35.74 m	150 m.m. Dia Plain Pipe	35.74	to 98.45 m	150 m.m. Dia Slotted Pipe	98.45	to 104.46 m	150 m.m. Dia Plain Pipe	104.46	to 112.48 m	150 m.m. Dia Slotted Pipe	112.48	to 118.48 m	150 m.m. Dia Plain Pipe	118.48	to 141.00 m	150 m.m. Dia Slotted Pipe	141.00	to 147.02 m	150 m.m. Dia Plain Pipe	147.02	to 162.03 m	150 m.m. Dia Slotted Pipe	162.03	to 168.04 m	150 m.m. Dia Plain Pipe	168.04	to 174.06 m	TOTAL ASSEMBLY:-	174.06	+AGL 0.5 = 174.56																																																																																																																						
300 m.m. Dia Housing Pipe :-	35.54	m																																																																																																																																																												
300x150 m.m. Dia REDUCER	35.54	to 35.74 m																																																																																																																																																												
150 m.m. Dia Plain Pipe	35.74	to 98.45 m																																																																																																																																																												
150 m.m. Dia Slotted Pipe	98.45	to 104.46 m																																																																																																																																																												
150 m.m. Dia Plain Pipe	104.46	to 112.48 m																																																																																																																																																												
150 m.m. Dia Slotted Pipe	112.48	to 118.48 m																																																																																																																																																												
150 m.m. Dia Plain Pipe	118.48	to 141.00 m																																																																																																																																																												
150 m.m. Dia Slotted Pipe	141.00	to 147.02 m																																																																																																																																																												
150 m.m. Dia Plain Pipe	147.02	to 162.03 m																																																																																																																																																												
150 m.m. Dia Slotted Pipe	162.03	to 168.04 m																																																																																																																																																												
150 m.m. Dia Plain Pipe	168.04	to 174.06 m																																																																																																																																																												
TOTAL ASSEMBLY:-	174.06	+AGL 0.5 = 174.56																																																																																																																																																												
17.50		CLAY																																																																																																																																																												
22.50		FINE SAND																																																																																																																																																												
31.00		CLAY																																																																																																																																																												
38.00		FINE SAND																																																																																																																																																												
43.00		CLAY WITH KANKAR																																																																																																																																																												
49.00		FINE SAND																																																																																																																																																												
53.00		SAND WITH KANKAR																																																																																																																																																												
60.00		FINE SAND																																																																																																																																																												
98.00		Clay																																																																																																																																																												
105.00		MEDIUM SAND	6.01																																																																																																																																																											
112.00		CLAY WITH KANKAR																																																																																																																																																												
119.00		MEDIUM SAND	6.00																																																																																																																																																											
140.50		CLAY																																																																																																																																																												
147.65		MEDIUM SAND	6.02																																																																																																																																																											
161.50		FINE SAND WITH																																																																																																																																																												
168.50		MEDIUM SAND	6.01																																																																																																																																																											
184.00		Clay																																																																																																																																																												
188.00		FINE SAND																																																																																																																																																												
200.00		Clay																																																																																																																																																												
				<table border="1"> <tr> <td colspan="7" style="text-align: center;">ABSTRACT</td> </tr> <tr> <td colspan="7">Date of Lowering:- 02.11.2023</td> </tr> <tr> <td colspan="7">LPM:- 650</td> </tr> <tr> <td colspan="7">Drilling Depth:- 252 M</td> </tr> <tr> <td colspan="7">Total Assembly Lowered 174.56 M</td> </tr> <tr> <td colspan="7">Housing Pipe:- 36.04 M</td> </tr> <tr> <td colspan="7">Plain Pipe:- 114.28 M</td> </tr> <tr> <td colspan="7">Slotted Pipe :- 24.04 M</td> </tr> <tr> <td colspan="7">Reducer :- 0.20 M</td> </tr> <tr> <td colspan="7" style="text-align: center;">LOGGING REPORT Date:- 26.11.2023</td> </tr> <tr> <td colspan="7">Logging Depth:- 200</td> </tr> <tr> <td></td> <td>SI N</td> <td>Depth Range</td> <td>Thickness</td> <td>SI N</td> <td>Depth Range</td> <td>Thickness</td> </tr> <tr> <td></td> <td>1</td> <td>31 - 38</td> <td>7</td> <td>11</td> <td>140 - 149</td> <td>9</td> </tr> <tr> <td></td> <td>2</td> <td>43 - 49</td> <td>6</td> <td>12</td> <td>160 - 170</td> <td>10</td> </tr> <tr> <td></td> <td>3</td> <td>53 - 60</td> <td>7</td> <td>13</td> <td>174 - 178</td> <td>4</td> </tr> <tr> <td></td> <td>4</td> <td>63 - 67</td> <td>4</td> <td>14</td> <td>184 - 188</td> <td>4</td> </tr> <tr> <td></td> <td>5</td> <td>79 - 83</td> <td>4</td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td>6</td> <td>85 - 92</td> <td>7</td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td>7</td> <td>98 - 105</td> <td>7</td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td>8</td> <td>112 - 119</td> <td>7</td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td>9</td> <td>122 - 126</td> <td>4</td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td>10</td> <td>130 - 134</td> <td>4</td> <td></td> <td></td> <td></td> </tr> </table>	ABSTRACT							Date of Lowering:- 02.11.2023							LPM:- 650							Drilling Depth:- 252 M							Total Assembly Lowered 174.56 M							Housing Pipe:- 36.04 M							Plain Pipe:- 114.28 M							Slotted Pipe :- 24.04 M							Reducer :- 0.20 M							LOGGING REPORT Date:- 26.11.2023							Logging Depth:- 200								SI N	Depth Range	Thickness	SI N	Depth Range	Thickness		1	31 - 38	7	11	140 - 149	9		2	43 - 49	6	12	160 - 170	10		3	53 - 60	7	13	174 - 178	4		4	63 - 67	4	14	184 - 188	4		5	79 - 83	4					6	85 - 92	7					7	98 - 105	7					8	112 - 119	7					9	122 - 126	4					10	130 - 134	4			
ABSTRACT																																																																																																																																																														
Date of Lowering:- 02.11.2023																																																																																																																																																														
LPM:- 650																																																																																																																																																														
Drilling Depth:- 252 M																																																																																																																																																														
Total Assembly Lowered 174.56 M																																																																																																																																																														
Housing Pipe:- 36.04 M																																																																																																																																																														
Plain Pipe:- 114.28 M																																																																																																																																																														
Slotted Pipe :- 24.04 M																																																																																																																																																														
Reducer :- 0.20 M																																																																																																																																																														
LOGGING REPORT Date:- 26.11.2023																																																																																																																																																														
Logging Depth:- 200																																																																																																																																																														
	SI N	Depth Range	Thickness	SI N	Depth Range	Thickness																																																																																																																																																								
	1	31 - 38	7	11	140 - 149	9																																																																																																																																																								
	2	43 - 49	6	12	160 - 170	10																																																																																																																																																								
	3	53 - 60	7	13	174 - 178	4																																																																																																																																																								
	4	63 - 67	4	14	184 - 188	4																																																																																																																																																								
	5	79 - 83	4																																																																																																																																																											
	6	85 - 92	7																																																																																																																																																											
	7	98 - 105	7																																																																																																																																																											
	8	112 - 119	7																																																																																																																																																											
	9	122 - 126	4																																																																																																																																																											
	10	130 - 134	4																																																																																																																																																											

JJM=III

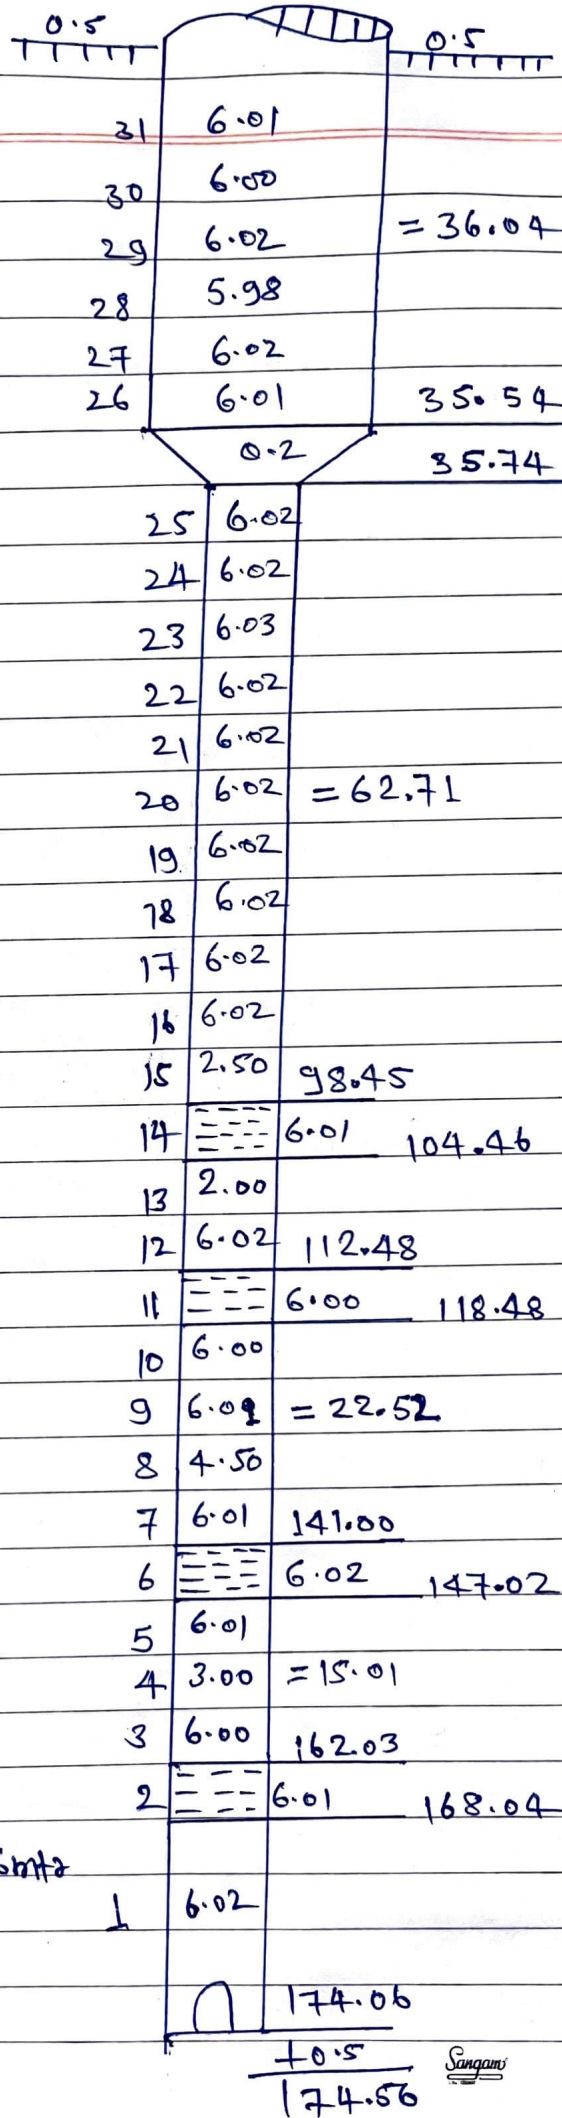

Gp:- Barwa Bhoj
 Block:- Nautanwa, Maharajganj
 Drilling Depth:- 252, 500x500
 Logging Depth:- 188,
 Logging Date:- 26-11-23
 LPM :- 600, 200x150
 Date:- 30-11-23
 Slotted - 24 mdr
 Logging Report

- ① 31-38 = 07
- ② 43-49 = 06
- ③ 53-60 = 07
- ④ 63-67 = 04
- ⑤ 79-83 = 04
- ⑥ 85-92 = 07
- ⑦ 98-105 = 07 = 06
- ⑧ 112-129 = 07 = 06
- ⑨ 122-126 = 04
- ⑩ 130-134 = 04
- ⑪ 140-149 = 09 = 06
- ⑫ 160-170 = 10 = 06
- ⑬ 174-178 = 04
- ⑭ 184-188 = 04

total Lowering = 174.56mtr
