

# Rithwik-Koya Joint Venture

Site Office: Plot No. 191D-1, Sarojini Nagar, Ward No. 20, Maharajganj, 221303, Uttar Pradesh

PN: 010 23530027, Email: kcc@rithwik.com


NAYANSR 17/01/2023

Block:- Brijmanganj  
 PHASE-III  
 LPM:- 1150

Size Of Bore:- 600 X 500 MM  
 Size Of Assembly:- 300 X 150MM  
 Date of logging:- 01.06.2023


Depth Logged:- 224 M

Depth of Strata In M.R.G.L



Strata Details

Lowering Assembly

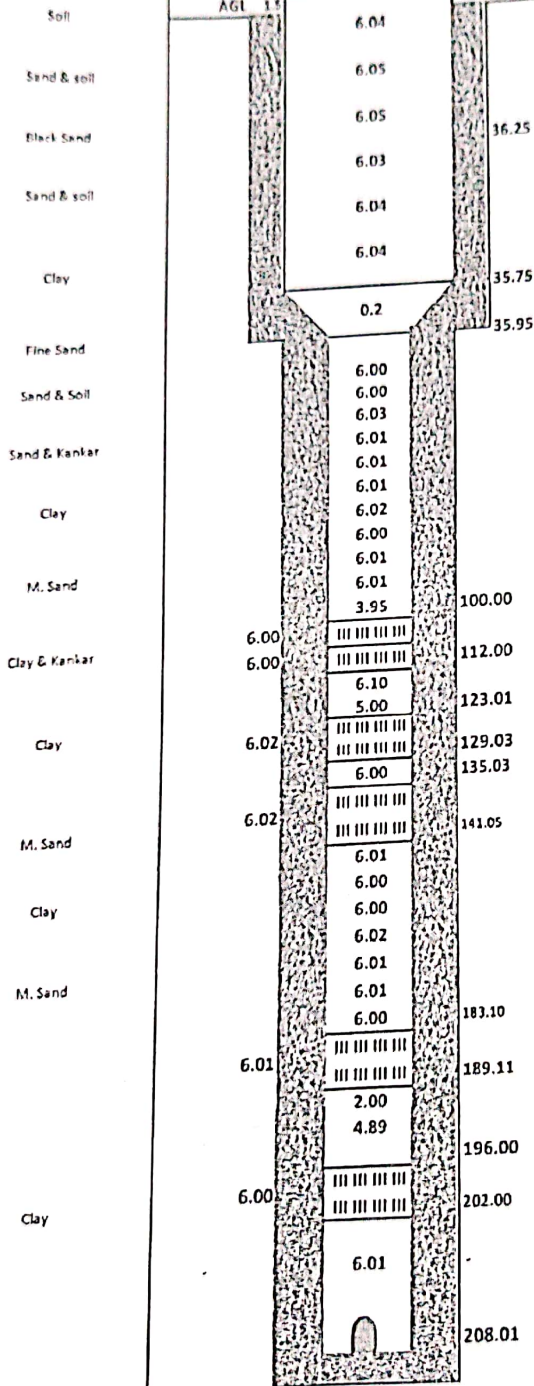

Sl No	Depth Range MBGL	Thickness (Mtr)	Remarks
1	38 - 41	3.0	Good
2	94 - 98	4.0	Good
3	100 - 112	12.0	Good
4	122 - 130	8.0	Good
5	134 - 142	8.0	Good
6	146 - 151	5.0	Good
7	182 - 190	8.0	Good
8	196 - 202	6.0	Good


Note:- All zones are intermixed with fine band of kankar.

- Drilling Started Date: 27.05.2023
  - Drilling Completed date: 01.06.2023
  - Lowering Complete Date: 08.06.2023
  - Assembly Lowered on Dated: 08.06.2023
- A) Housing Pipe 300 mm dia (AGL) = 0.5  
 B) Housing Pipe 300 mm dia (BGL) = 35.75  
 C) Reducer 300 mm X 150 mm = 0.2  
 D) Slotted pipe 150 mm dia = 36.05  
 E) Plain Pipe 150 mm dia = 136.01
- With AGL = 208.51  
 Total Assembly: 208.01 + 0.5 = 208.51  
 Without AGL = 208.01

Assembly Details		Total in MTR
M to M		
#	300MM Housing Pipe	0.00 - 35.75
#	300X150MM Reducer	35.75 - 35.95
#	150MM Plain Pipe	35.95 - 100.00
#	150MM Slotted Pipe	100.00 - 112.00
#	150MM Plain Pipe	112.00 - 123.01
#	150MM Slotted Pipe	123.01 - 129.03
#	150MM Plain Pipe	129.03 - 135.03
#	150MM Slotted Pipe	135.03 - 141.05
#	150MM Plain Pipe	141.05 - 183.10
#	150MM Slotted Pipe	183.10 - 189.11
#	150MM Plain Pipe	189.11 - 196.00
#	150MM Slotted Pipe	196.00 - 202.00
#	150MM Plain Pipe	202.00 - 208.01

AGL = 0.5 MTR  
 TOTAL = 208.01 + .50 = 208.51

AGL+1.5+ 208.51



*Jah*  
 TPI (M/S Medhal)

*PAK*  
 I.E

*Pa*  
 A.E

E.E
