


Name of work :- Construction of T. W. of G.P. Gajraura, Block-Palia, District, Lakhimpur Kheri.
 Name of Program :- J. J. M-2
 Name of client :- S.W.S.M. & U.P. JAL NIGAM (R)
 Name of Contractor :- M/S NCC Limited
 Name of TPI :- Ceinsys Tech Limited
 Contract Agreement :- 64/ED/2020-21 Dated on 12.03.2021
 Cover Agreement :- 102/ED/Phase-2/2022-23/VI

Lowered Assembly Chart of T. W of Gajraura G.P W/S Scheme District :- Lakhimpur Kheri.

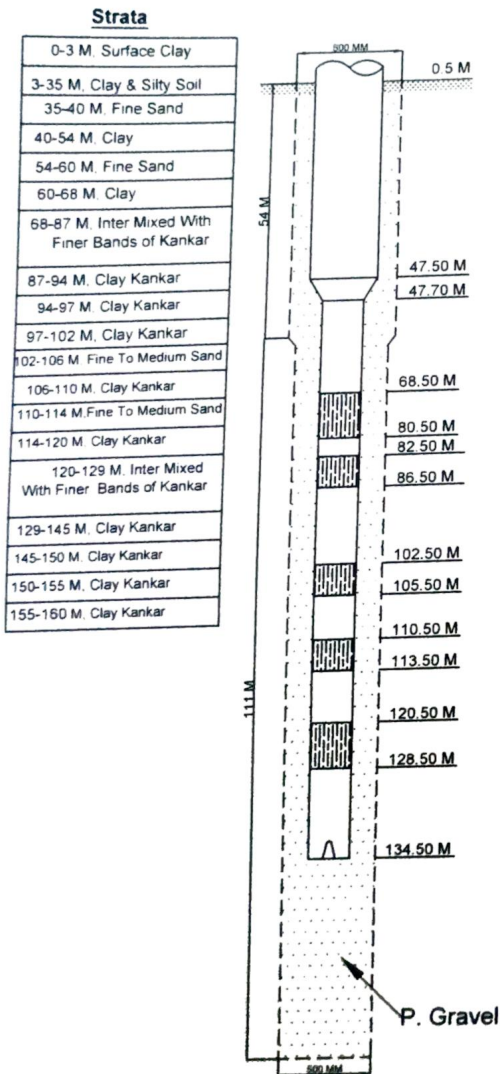

1	Type of Rig Machine	- DC/RC
2	Static Water level	-
3	Required Discharge	- 1000 LPM
4	Bore Size (MM)	- 600x500
5	Assembly Size (MM)	- 300 x 150
6	Drilling Starting Date	- 18.07.2022
7	Drilling Completion Date	- 21.07.2022
8	Total Depth Of Drilling	- 170 M
9	Logging Date	- 22.07.2022
10	Logging Depth	- 165 M

Sl.No	Depth (mbgl)	Thickness (m)	Remarks
1	35-40	5	Fine to Medium Sand (Good All)
2	54-60	6	
3	68-87	19	
4	94-97	3	
5	102-106	4	
6	110-114	4	
7	120-129	9	
8	145-150	5	
9	155-160	5	

i) 300 mm Dia Housing Pipe	- 48.00 Meter
ii) 150 mm Dia M. S. Slotted pipe	- 30.00 Meter
iii) 150 mm Dia M. S. Plain pipe	- 56.80 Meter
iv) 300 x 150 mm Dia M S Reducer	- 0.20 Meter
Total	- 135.00 Meter
AGI	- 00.50 Meter
BGL	- 134.50 Meter
12. Date of Lowering	- 23.07.2022

Recommended & Prepared by

Verified by

Recommended by

Approved by

M/S. NCC Ltd.

M/S. Ceinsys Tech Ltd.

VIKAS KR. YADAV
 JUNIOR ENGINEER
 DIVISIONAL OFFICE (E&M)
 U.P. JAL NIGAM (R)
 13th Division UP Jal Nigam (R) Lucknow

A.E
 13th Division UP Jal Nigam (R) Lucknow

E.E
 13th Division U.P. Jal Nigam (R) Lucknow
