




Jal Jeevan Mission
Village-Bautha Jamalpur, Block-Banda, District-Shahjahanpur
 AGENCY: M/S NCC LIMITED- HYDERABAD
Tubewell Assembly Chart


Dt: 13.09.2022

Discharge 678 LPM




Strata as per Logging Report:

S.NO	IN METER		STRATA	
1	54	Mtr.	75	Mtr. Medium Sand
2	80	Mtr.	90	Mtr. Medium Sand
3	95	Mtr.	109	Mtr. Medium Sand
4	113	Mtr.	134	Mtr. Medium Sand

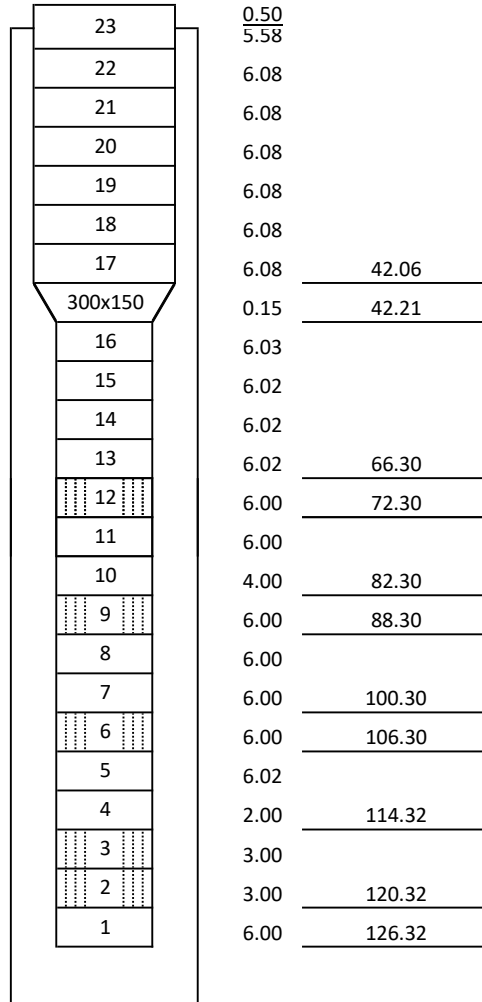

1	Reducer 300x150 mm	0.15 M
2	AGL	0.50
3	BGL	126.32
4	Total assembly lower	126.82
5	300 mm Plain MS Pipe	42.56
6	150 mm Plain MS Pipe	60.11
7	150 mm slotted pipe	24.00
8	Drilling Depth 600 Dia	42.0 M
9	Drilling Depth 500 Dia	98.0 M
9	Drilling logged	140.00 m



M/S NCC LTD

M/s BLG Construction
3rd Party Inspection

J.E

A.E

EE

(E&M) U.P JAL NIGAM, MORADABAD
