



**Jal Jeevan Mission**


**Village-BADHAURA & BASKHERA BUZURG,BLOCK-POWAYAN, District-Shahjahanpur**

**AGENCY: M/S NCC LIMITED- HYDERABAD**

**Tubewell Assembly Chart**

**20.03.2023**


Discharge 860 LPM



Drilling and lowering

**Strata as per Logging Report:**

S.NO	IN METER		STRATA	
1	55	Mtr. 70	Mtr.	MEDIUM SAND
2	75	Mtr. 84	Mtr.	FINE TO MEDIUM SAND
3	87	Mtr. 94	Mtr.	FINE TO MEDIUM SAND
4	97	Mtr. 122	Mtr.	FINE TO MEDIUM SAND

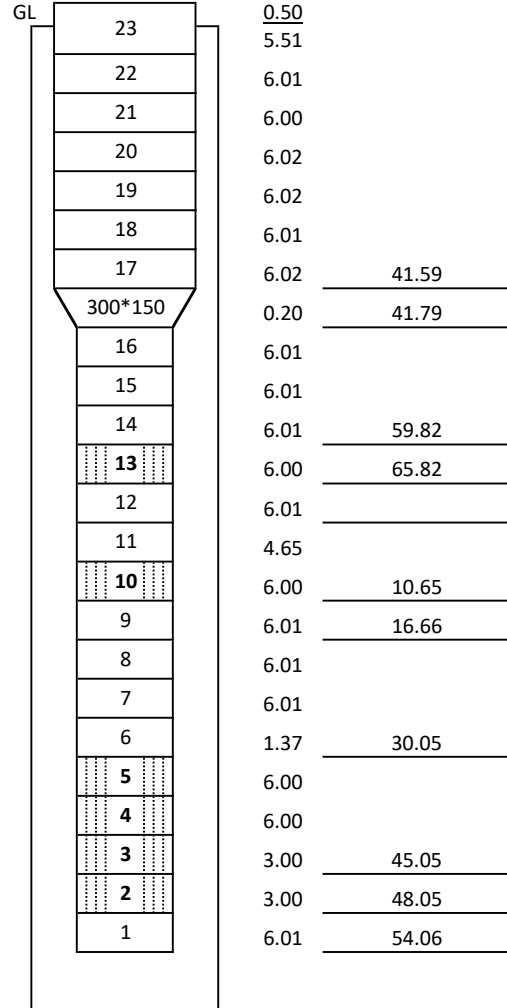

1	AGL	0.50
2	BGL	54.06
3	Total assembly lower	54.56
4	300 mm Plain MS Pipe	42.09
5	150 mm Plain MS Pipe	54.10
6	150 mm slotted pipe	30.00
7	Drilling Depth 600 Dia	45.00M
7	Drilling Depth 500 Dia	95.00M
8	Drilling logged	130.00M



M/S NCC LTD

M/s BLG Construction  
3rd Party Inspection

J.E

A.E

EE

(E&M) U.P JAL NIGAM,MORADABAD
