



Jal Jeevan Mission


Village-DABHAURA & NAWADIA DHUSAR, BlocK-BANDA, District-Shahjahanpur

AGENCY: M/S NCC LIMITED- HYDERABAD

Tubewell Assembly Chart

18.02.2023


Discharge 1750 LPM




Drilling and lowering

Strata as per Logging Report:

S.NO	IN METER		STRATA	
1	30	Mtr.	54	Mtr. MED SAND& KANKAR
2	57	Mtr.	66	Mtr. MEDIUM SAND
3	83	Mtr.	105	Mtr. MED SAND& KANKAR
4	108	Mtr.	135	Mtr. MED SAND & KANKAR

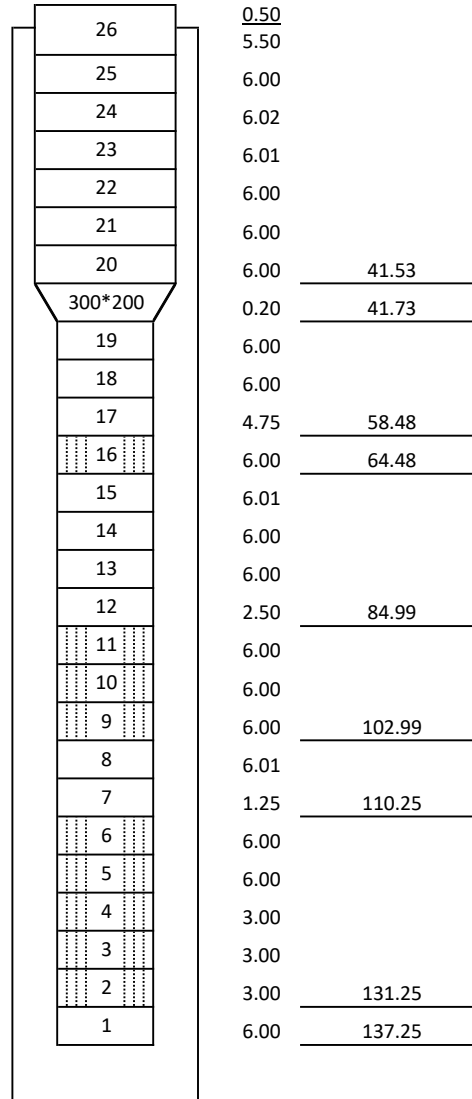

1	AGL	0.50
2	BGL	137.25
3	Total assembly lower	137.75
4	300 mm Plain MS Pipe	42.03
5	200 mm Plain MS Pipe	50.52
6	200 mm slotted pipe	45.00
8	Drilling Depth 600 Dia	45.00M
8	Drilling Depth 500 Dia	110.00M
9	Drilling logged	155.00M



M/S NCC LTD

M/s BLG Construction
3rd Party Inspection

J.E

A.E

EE

(E&M) U.P JAL NIGAM,MORADABAD
