



Jal Jeevan Mission


Village-BEHTA J JEWAN & FATTEPUR BUZURG, Block-POWAYAN, District-Shahjahanpur

AGENCY: M/S NCC LIMITED- HYDERABAD

Tubewell Assembly Chart

07-01-2023



Discharge 1110 LPM



Drilling and lowering

Strata as per Logging Report:

S.NO	IN METER		STRATA
1	50	Mtr. 64	Mtr. fine to Medium sand
2	90	Mtr. 97	Mtr. fine to Medium Sand
3	101	Mtr. 116	Mtr. fine to Medium Sand

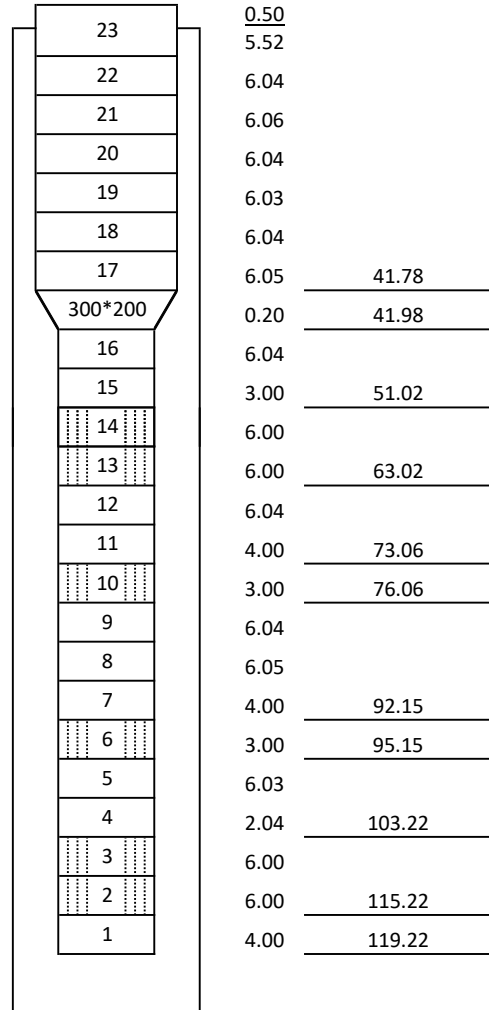

1	AGL	0.50
2	BGL	119.22
3	Total assembly lower	119.72
4	300 mm Plain MS Pipe	42.28
5	200 mm Plain MS Pipe	47.24
6	200 mm slotted pipe	30.00
7	Drilling Depth 600 Dia	45.0M
7	Drilling Depth 500 Dia	85.0M
9	Drilling Logged	130.0M

M/S NCC LTD

M/s BLG Construction
3rd Party Inspection

J.E

A.E

EE

(E&M) U.P JAL NIGAM, MORADABAD
