



Jal Jeevan Mission


Village-BARHARU BIJLA & UMAR SANDA, BLOC-POWAYAN, District-Shahjahanpur

AGENCY: M/S NCC LIMITED- HYDERABAD

Tubewell Assembly Chart

01.04.2023


Discharge 690 LPM



Drilling and lowering

Strata as per Logging Report:

S.NO	IN METER		STRATA	
1	61	Mtr.	70	Mtr. MEDIUM SAND
2	74	Mtr.	80	Mtr. MEDIUM SAND
3	85	Mtr.	115	Mtr. MEDIUM SAND

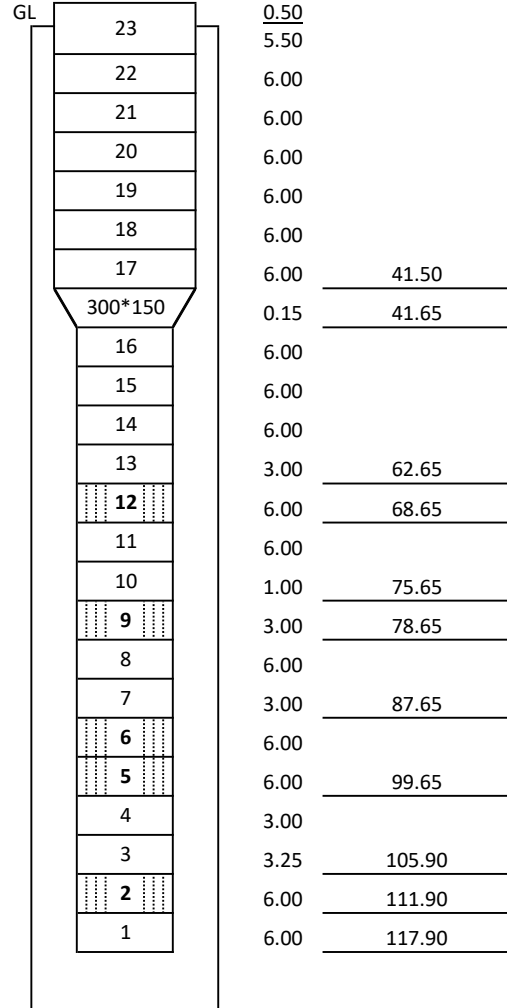

1	AGL	0.50
2	BGL	117.90
3	Total assembly lower	118.40
4	300 mm Plain MS Pipe	42.00
5	150 mm Plain MS Pipe	49.25
6	150 mm slotted pipe	27.00
7	Drilling Depth 600 Dia	45.00M
7	Drilling Depth 500 Dia	85.00M
8	Drilling logged	130.00



M/S NCC LTD

M/s BLG Construction
3rd Party Inspection

J.E

A.E

EE

(E&M) U.P JAL NIGAM, MORADABAD
