



Jal Jeevan Mission


Village-BARHELA& KOTAWARI, Block-SINDHAULI, District-Shahjahanpur

AGENCY: M/S NCC LIMITED- HYDERABAD

Tubewell Assembly Chart

19-01-2023


Discharge 910 LPM




Drilling and lowering

Strata as per Logging Report:

S.NO	IN METER		STRATA	
1	54	Mtr.	59	Mtr. MEDIUM SAND
2	66	Mtr.	72	Mtr. MEDIUM SAND
3	80	Mtr.	102	Mtr. MEDIUM SAND
4	108	Mtr.	118	Mtr. MEDIUM SAND

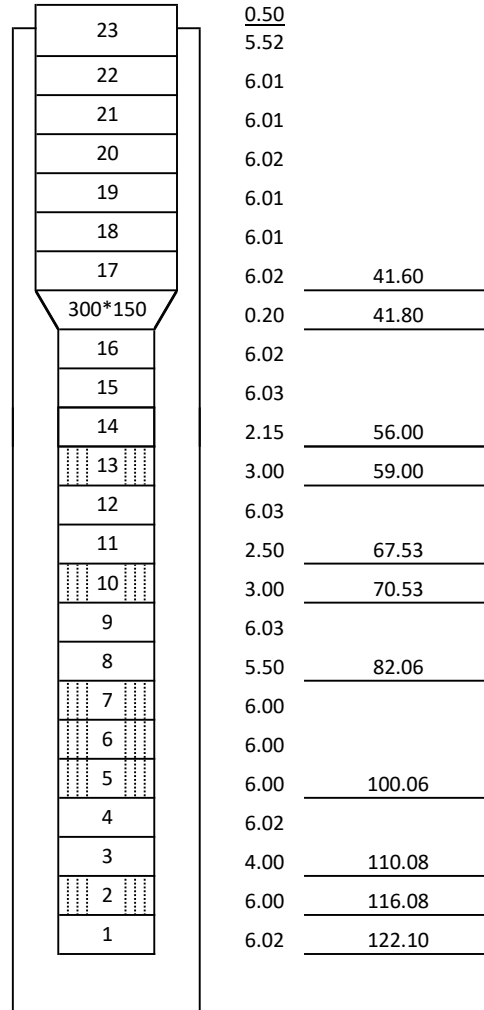

1	AGL	0.50
2	BGL	122.10
3	Total assembly lower	122.60
4	300 mm Plain MS Pipe	42.10
5	150 mm Plain MS Pipe	50.30
6	150 mm slotted pipe	30.00
7	Drilling Depth 600 Dia	45.00
8	Drilling Depth 500 Dia	95.00
9	Drilling Logged	140.00



M/S NCC LTD

M/s BLG Construction
3rd Party Inspection

J.E

A.E

EE

(E&M) U.P JAL NIGAM, MORADABAD
