



Jal Jeevan Mission
Village-GANPATPUR ,Block-SINDHAULI, District-Shahjahanpur


AGENCY: M/S NCC LIMITED- HYDERABAD

Tubewell Assembly Chart

PHASE 3

19.03.2023


Discharge 630 LPM




Drilling and lowering

Strata as per Logging Report:

S.NO	IN METER	STRATA
1	30 Mtr. 63	Mtr. MEDIUM SAND
2	98 Mtr. 112	Mtr. MEDIUM SAND
3	125 Mtr. 130	Mtr. FINE TO MED SAND

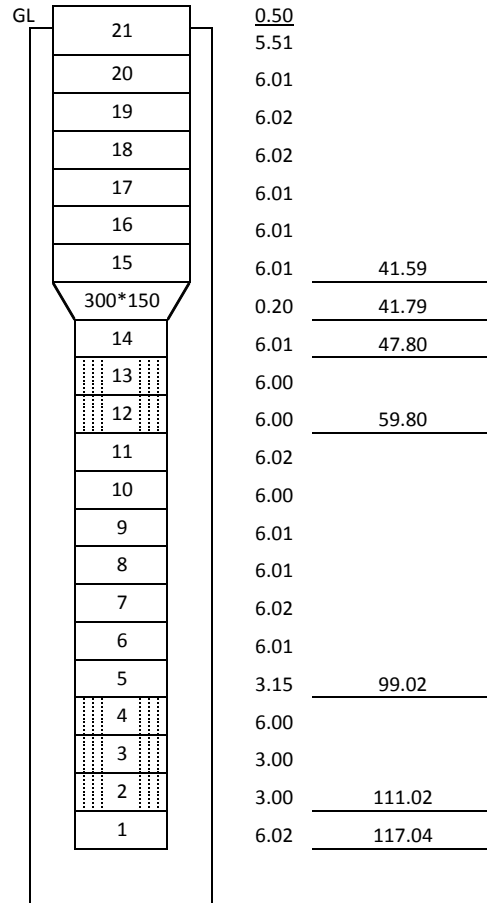

1	AGL	0.50
2	BGL	117.04
3	Total assembly lower	117.54
4	300 mm Plain MS Pipe	42.09
5	150 mm Plain MS Pipe	51.25
6	150 mm slotted pipe	24.00
8	Drilling Depth 600 Dia	45.00M
8	Drilling Depth 500 Dia	85.00M
9	Drilling logged	130.00M



M/S NCC LTD

M/s BLG Construction
3rd Party Inspection

J.E

A.E

EE

(E&M) U.P JAL NIGAM, MORADABAD
