


Guwawan

Welspun^w ENTERPRISES

RURAL WATER SUPPLY SCHEME, UNDER SWSM-JJM

Date- / /

Actual T/W Assembly chart of 300X150 mm Size of Guwawan, Block- Gauriganj
District-Amethi
Q=650 LPM.

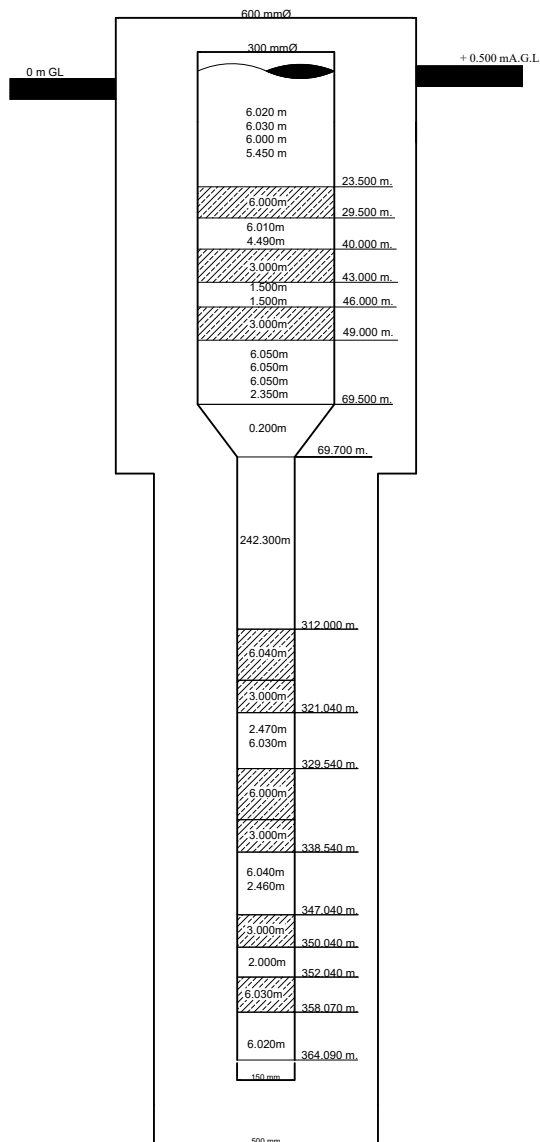

1. Bore Size (Dia)	=	600 x 500 mm
2. Assembly Size (Dia)	=	300 x 150mm
3. Drilling Depth	=	400.000 m
4. Logging Depth	=	380.700 m
5. Date of Logging	=	28.9.2023
6. Date of Lowering	=	11.10.2023

Logging Report

S.No.	Depth Range (mbgl)	Thickness (m)	Remarks
1.	13-16	03	Moderate
2.	23-30	07	Good
3.	40-43	03	Good
4.	46-49	03	Good
5.	59-62	03	Moderate
6.	312-321	09	Good to Moderate
7.	329-339	10	Good to Moderate
8.	347-350	03	Good
9.	352-359	07	Good
10.	363-366	03	Moderate
11.	369-373	04	Moderate

1. 300 mm @ Housing Pipe	=	57.500m
2. 300 mm @ Slotted pipe	=	12.000m
3. 200mm @ Slotted Pipe	=	27.070m
4. 200 mm @ Plain Pipe	=	267.320m
5. 300 X200 mm @ Reducer	=	0.200m
A.G.L =		0.500m
B.G.L =		364.090m
Total Lowering =		364.590m
