



CONST. DIVISION (E/M), U. P. JAL NIGAM, GHAZIABAD

Completion Plan of Tw. No. at MURADABAD VILLAGE DISTRICT BSR.

Type of Rig m/c R.C. RIG Size of Bore 450MM S.W.L. 6:20 Mts

Agency RENTAL

Depth B.G.L. Meter	Boring Chart	Stratum	Lowered Assembly	ASSEMBLY DETAILS
GL.			AGL 30cm	
6.00		SURFACE CLAY		150 m. m. Dia Housing pipe.. 0:30 MSL to 47:70 MSL
				X m. m. Dia Reducer..... X..... m to X..... M
25.00		FINE SAND		150 m. m. Dia Slotted Pipe... 47:70 m to 59:70 m
30.00		SANDY CLAY		150 m. m. Dia Blind Pipe... 59:70 m to 71:70 m
38.00		FINE SAND		150 m. m. Dia Slotted Pipe... 71:70 m to 77:70 m
45.00		CLAY		150 m. m. Dia Blind Pipe... 77:70 m to 80:80 m
			47.70	+ BAIL PLUG
		FINE to MED. SAND	59.70	m. m. Dia Pipe..... m to m
61.00		CLAY		m. m. Dia Pipe..... m to m
70.00		MED. SAND	71.70	m. m. Dia Pipe..... m to m
78.50		CLAY	77.70	m. m. Dia Pipe..... m to m
90.00			80.80	m. m. Dia Pipe..... m to m
				Total Assembly..... 81:10 m

ABSTRACT

- Drilling Started on.....
- Drilling Completed on..... 27.8.06
- Assembly Lowered on..... 27.8.06
- Drilling Depth..... 90.00 m
- Assembly Lowered..... 81.10 m
- Housing Pipe..... 150 m. m. dia 48.00 m
- Blind Pipe..... 150 m. m. dia 15.10 m
- Slotted Pipe..... 150 m. m. dia 18.00 m

As Executed

Representative

(R.C. JAIN) (G.D. KHANDELWAL)

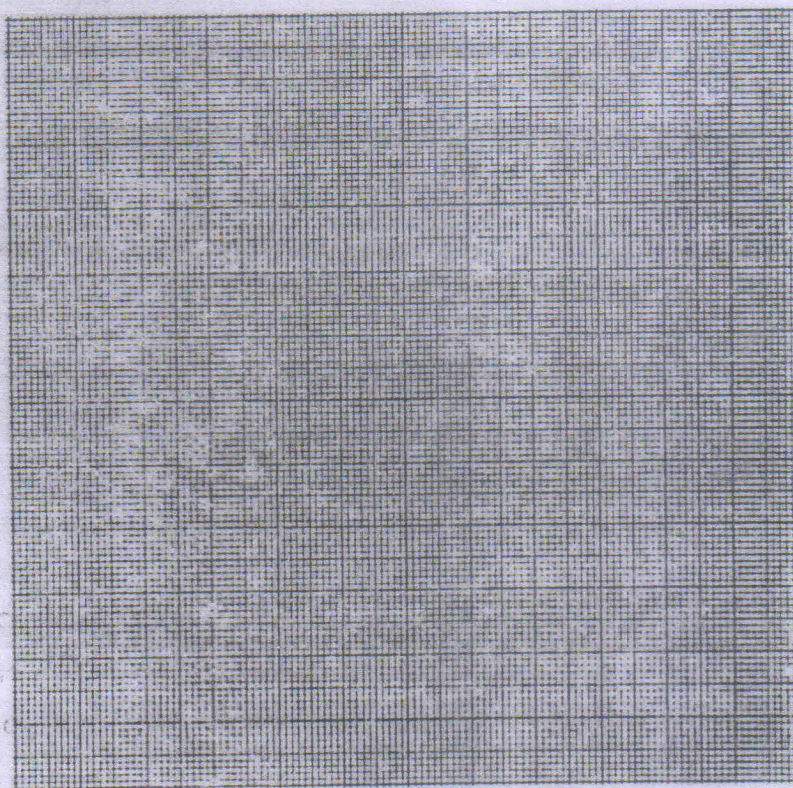
Countersigned

(NAVIN CHAND)
Executive Engineer

S.W.L. 6.20 m Taste of Water Sweet V-Notch/Orifice 220 mm Date of test 5.9.06

Recommended.....300..... discharge at...2.50..... mts depression

DIA OF Disc..... TOTAL HOUSING..... DATE OF TEST.....
Height of Suspension.....

[illegible]

CLEAR SPACE A1
 A1
 A1

WATER TEST RESULTS

AGENCY 120 MLD WATER TREATMENT PLANT (GANGAJAL) LAB REF: A-95 Dated 16.9.2006

PRATAP VIHAR, BHATINDAR.





 P. S. Saran J. E. A. E. Executive Engineer
