

Completion Plan of T W No. 1 at BHAINSAKHUR DISTRICT BSR.

Type of Rig m/c R.C. 600/27' Size of Bore 675X600mm S.W.L. 6.30 Mts.

Agency DEPARTMENTAL

As Executed

(R.C. JAIN)

20001
(A.K. TVAGI)

Countersigned

Representative

J. E.

A.E.

Executive Engineer

YIELD TEST REPORT

S.W.L. 6.30 M. Taste of Water SWEET..... V - Notch/Office 20.0X1.25mm. Date of test 29-5-2011.

[illegible]

Recommended 1200 LPM discharge at 4:00 mts depression

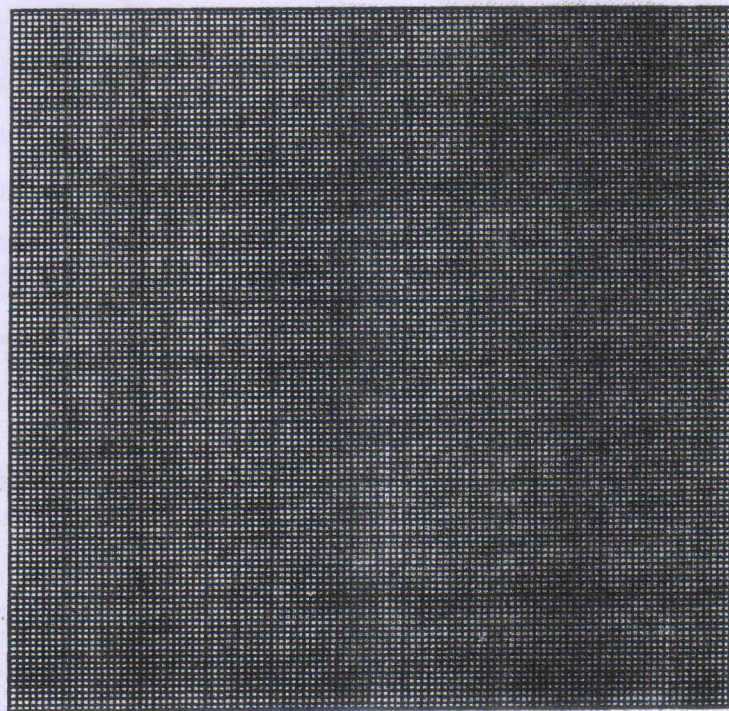
Gain Breed
J.E. A.E.

VERTICALITY TEST REPORT

DIA OF Disc TOTAL HOUSING DATE OF TEST

Height of Suspension ...

Circla diagram

[illegible]

CLEAR SPACE At

At

At

AGENCY

**C120 MLD WATER TREATMENT
LAB, PRATAP VIHAR, GHAZIABAD.**

WATER TEST RESULTS

REF :- H. M. DATED

1. TURBIDITY.....	NTU 0.7
2. PH	7.5
3. TOTAL DISSOLVED SOLIDS mg/l	320
4. TOTAL HARDNESS (as CaCO_3) mg/l.	12
5. CHLORIDES (as CL) mg/l.	32
6. SULPHATES (as SO_4) mg/l.	28
7. FLUORIDES (as F) mg/l.	0.2
8. NITRATES (as NO_3) mg/l.	3
9. CALCIUM (as Ca) mg/l.	44.90

10. MAGNESIUM (as mg) mgl. 19.30
11. IRON (as Fe) mgl. 0.05

_____'s Signature

J. E.

A. E.

Executive Engineer
