


315-051

Location of T.W. Assembly at Shivpur T/W Bench Day Begins With
 Drilling/Logging - 13/12/20
 Hole Size - 550 x 500 mm
 S.W.L. - 8-feet
 T.W. Assembly Size - 200 x 150 mm
 Recommended Discharge - 400 L per
 D.O.L. - 10/11/20

Logging Report

- 1. 17-18 ⇒ 4
- 2. 21-28 ⇒ 7
- 3. 33-46 ⇒ 7
- 4. 48-58 ⇒ 10
- 5. 62-72 ⇒ 10
- 6. 77-90 ⇒ 13
- 7. 112-119 ⇒ 7

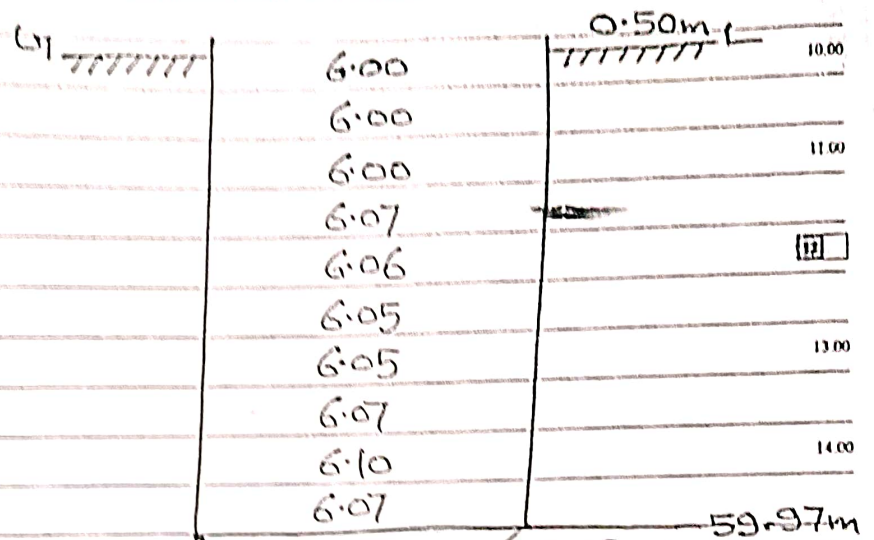

Strata as per Actual

0 - 13 clay			0.50m	10.00
13 - 19 M.Sand				11.00
19 - 22 clay				
22 - 30 F.to M.Sand				
30 - 40 clay	6.03			12.00
40 - 47 F.Sand	6.00			13.00
47 - 49 clay				
49 - 59 V.F. Sand				
59 - 61 clay				
61 - 73 V.F. Sand				
73 - 76 clay				
76 - 92 M.Sand				
92 - 111 clay				
111 - 120 M.Sand				
120 - 132 clay				
			AGL (+) 0.50m	
			Total ⇒	121.55m

DECEMBER
 7 14 21 28
 8 15 22 29
 9 16 23 30
 10 17 24 31
 11 18 25
 12 19 26
 13 20 27

(M/S Jai Babarsh Chaudhary) Contractors
 (Sampuranand) JE.
 (Bibban Yadav) AE
 (Adarsh Verma) EE.
 Scanned with CamScanner
