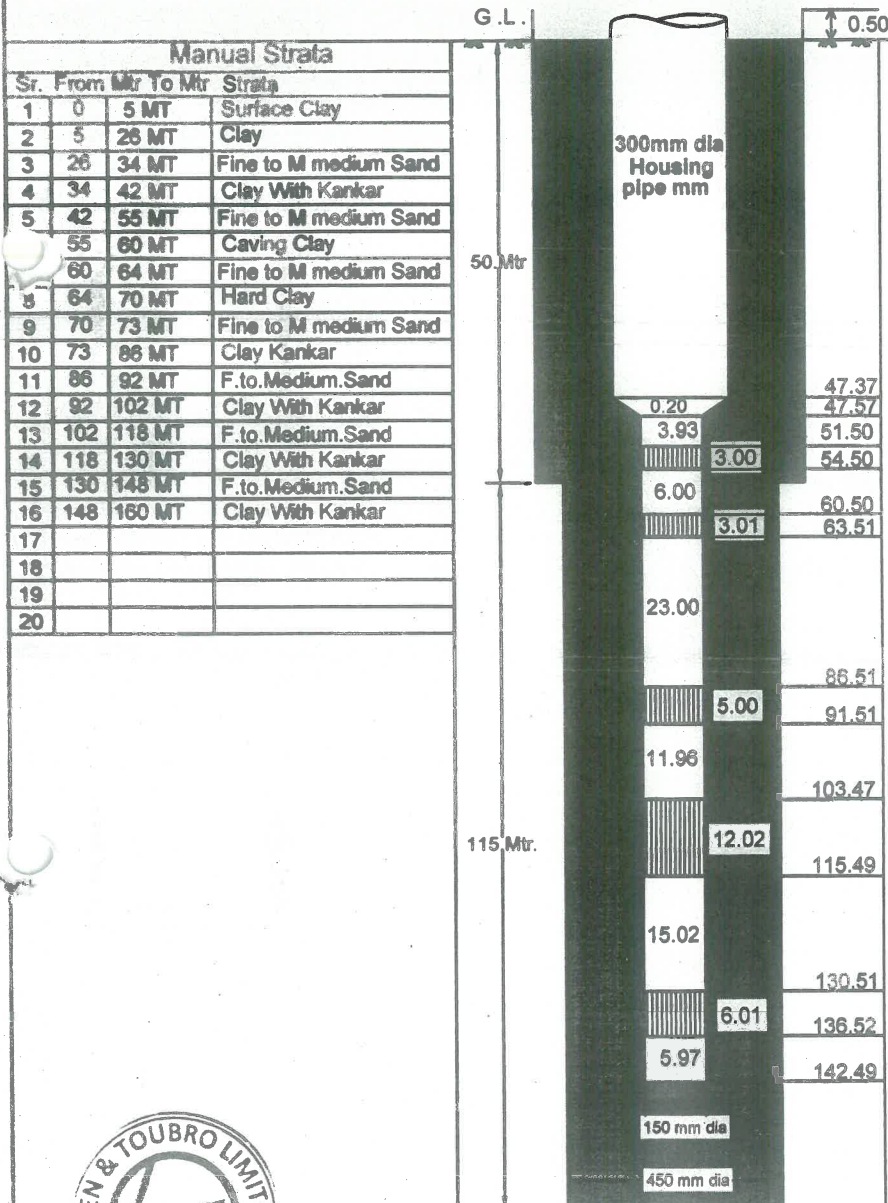


(43)

COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. HARRAIYA G.P W/S SCHEME BLOCK KASMANDA DISTRICT :- SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 206 /ED/21-22/III/DATED : 08-12-2021 -
 LOWERED ASSEMBLY CHART OF T.W. OF HARRAIYA G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT. 600 MM DIA BORE

**ABSTRACT**

1- Required Discharge	:- 730..LPM
2- Static Water Level	:- d2 Mtr
3- Type of Rig Machine	:- D.C/R.C
4- Bore Size	:- 600x450 mm dia
5- Assembly size	:- 300 x150 mm dtr
7- Total Depth of Bore	:- 165 Mtr
a- 600 mm dia o to 50	:- 50.00 m.
b- 300 mm dia 51 to 165	:- 115.00 m.
Total	:- 165.00 m.
8- Logging date	:- 30-03-2022
9- Logging Depth	:- 151.00 m.

LOGGING REPORT

Sr.	Depth Range Mbg	Thickness m.	Remarks
1	26 - 34	8.00 m	Good
2	42 - 55	13.00 m	Good
3	60 - 64	4.00 m	Good
4	70 - 73	3.00 m	Good
5	86 - 92	6.00 m	Good
6	102 - 118	16.00 m	Good
7	130 - 148	18.00 m	Good

11- Detail of Tubewell Assembly

(A) 300 mm dia Housing Pipe	:- 47.87 Meter
(B) 300x150 mm dia MS Reducer	:- 0.20 Meter
(C) 150 mm dia MS Plain Pipe	:- 65.88 Meter
(D) 150 mm dia Slotted Pipe	:- 29.04 Meter
Total	:- 142.99 Meter
A G L	:- 0.50 Meter
B G L	:- 142.49 Meter
12- Date of Lowering	:- 01/04/2022



PREPARED BY

RECOMMENDED BY

APPROVED BY

LARSEN AND TOUBRO
LIMITED SITAPUR

(VERIFIED BY)

(T.P.N)

DIVISIONAL OFFICE (E/M)
U.P. JAL NIGAM (R) LUCKNOW

(DINESH KUMAR)

(A E)

DIVISIONAL OFFICE (E/M)
U.P. JAL NIGAM (R) LUCKNOW

(VISHAL ARYA)

EXECUTIVE ENGINEER
DIVISIONAL OFFICE (E/M)
U.P. JAL NIGAM (R) LUCKNOW
