


(138)

COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. KABIRPUR G.P W/S SCHEME BLOCK GONDALMAU DISTRICT SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 206 /ED/21-22/111/DATED 08-12-2021
 LOWERED ASSEMBLY CHART OF T.W. OF KABIRPUR G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT. 500 MM DIA BORE

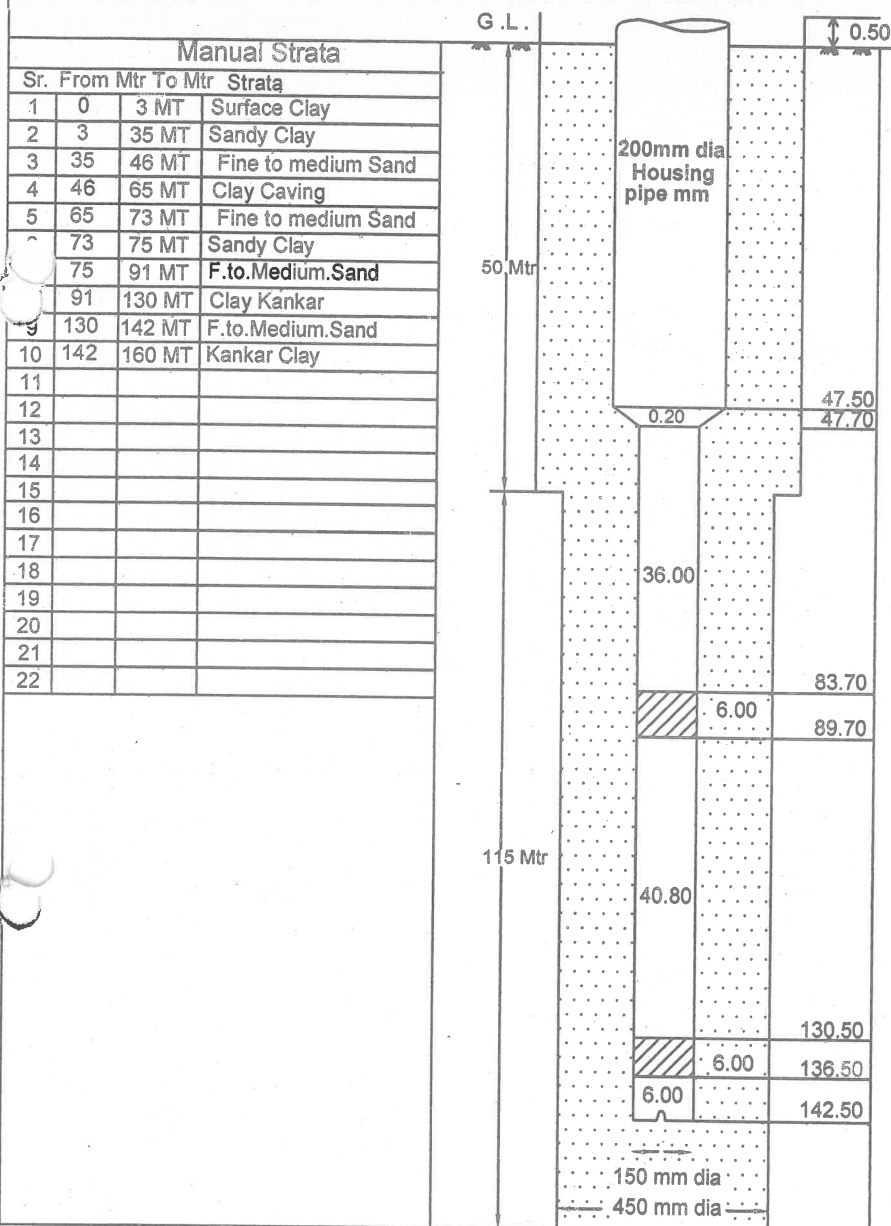

ABSTRACT		
1- Required Discharge	:-	270 LPM
2- Static Water Level	:-	10 MTR
3- Type of Rig Machine	:-	R.C./D.C
4- Bore Size	:-	500x450 mm dia
5- Assembly size	:-	200x150 mm dtr
6- Total Depth of Bore	:-	165 Mtr
a- 500 mm dia o to 50	:-	50.00 m.
b- 200 mm dia 50 to 165	:-	115.00 m.
Total	:-	165.00 m.
7- Logging date	:-	26-09-2022
8- Logging Depth	:-	160.00 m.

LOGGING REPORT

Sr.	Depth Range Mbgl	Thickness m.	Remarks
1	35 - 46	5.00 m	Good
2	65 - 73	8.00 m	Good
3	75 - 91	16.00 m	-6Mtr Good
4	130 - 142	12.00 m	-6Mtr Good
5			
6			
7			
8			
9			
10			

11- Detail of Tubewell Assembly

(A) 200 mm dia Housing Pipe	:-	48.00 Meter
(B) 200x150 mm dia MS Reducer	:-	0.20 Meter
(C) 150 mm dia MS Plain Pipe	:-	82.80 Meter
(D) 150 mm dia Slotted Pipe	:-	12.00 Meter
Total	:-	143.00 Meter
A G L	:-	0.50 Meter
B G L	:-	142.50 Meter
12- Date of Lowering	:-	28-09-2022

PREPARED BY

RECOMMENDED BY

APPROVED BY

(P. M.)
 LARSEN AND TOUBRO
 LIMITED SITAPUR

(VERIFIED BY)
 (T. P.I.)

(VIKRAM JEET)
 (J E)
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW

(RAJENDRA KUMAR)
 (A E)
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW

(SHRI RAM GUPTA)
 EXECUTIVE ENGINEER
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW
