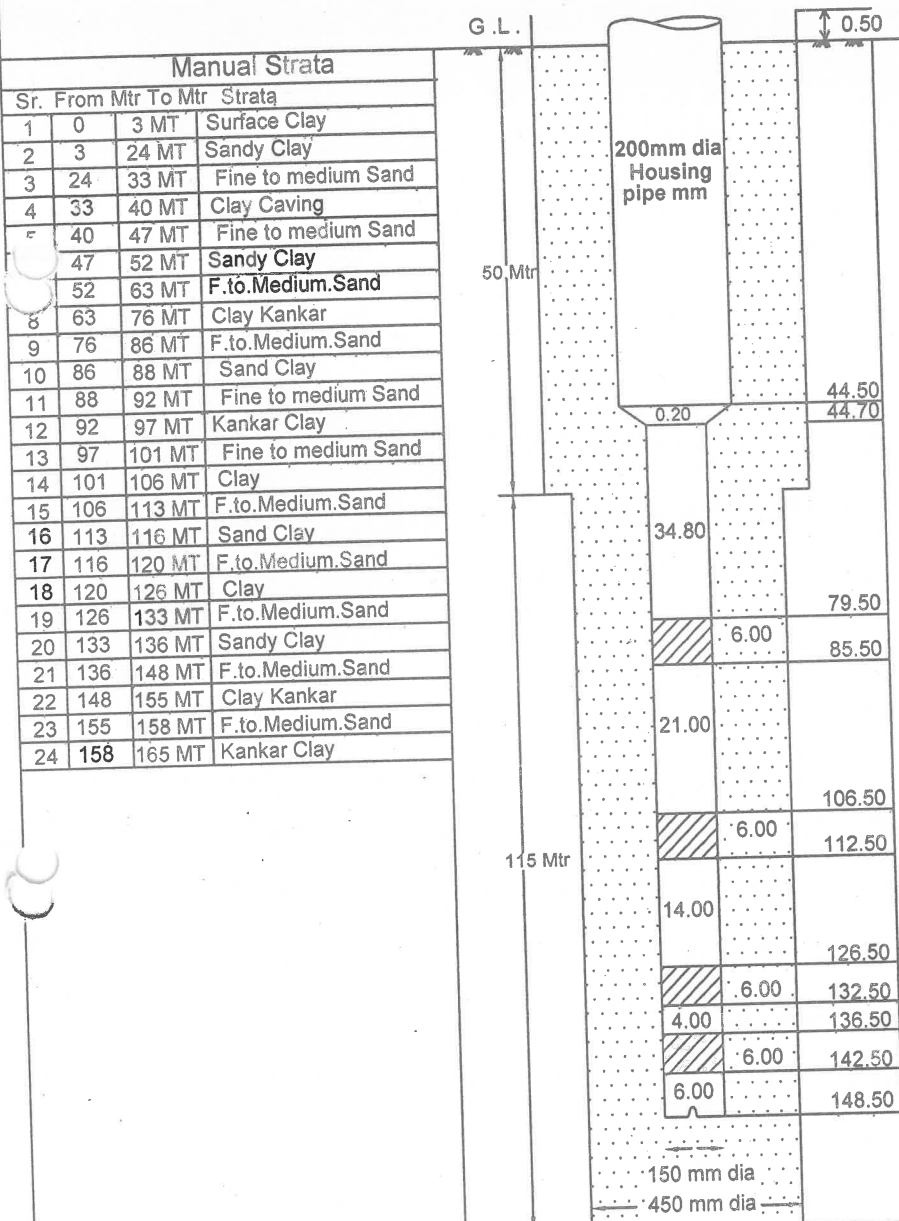


COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. KATSARIYA G.P W/S SCHEME BLOCK SIDHAULI DISTRICT SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 106 /ED/21-22.....DATED 10/08/2021
 LOWERED ASSEMBLY CHART OF T.W. OF KATSARIYA G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT. 500 MM DIA BORE

**ABSTRACT**

1-	Required Discharge	:- 550 LPM
2-	Static Water Level	:- 10 MTR
3-	Type of Rig Machine	:- R.C./D.C
4-	Bore Size	:- 500x450 mm dia
5-	Assembly size	:- 200x150 mm dtr
6-	Total Depth of Bore	:- 165 Mtr
a-	500 mm dia o to 50	:- 50.00 m.
b-	200 mm dia 50 to 165	:- 115.00 m.
	Total	:- 165.00 m.
7-	Logging date	:- 30-09-2022
8-	Logging Depth	:- 163.00 m.

LOGGING REPORT

Sr.	Depth Range Mbgl	Thickness m.	Remarks
1	24 - 33	9.00 m	Good
2	40 - 47	7.00 m	Good
3	52 - 63	11.00 m	Good
4	76 - 86	10.00 m	-6Mtr Good
5	88 - 92	4.00 m	Good
6	97 - 101	4.00 m	Good
7	106 - 113	7.00 m	-6Mtr Good
8	116 - 120	4.00 m	Good
9	126 - 133	7.00 m	-6Mtr Good
10	136 - 148	12.00 m	-6Mtr Good
11	155 - 158	3.00 m	Good

11- Detail of Tubewell Assembly

(A)	200 mm dia Housing Pipe	:- 45.00 Meter
(B)	200x150 mm dia MS Reducer	:- 0.20 Meter
(C)	150 mm dia MS Plain Pipe	:- 79.80 Meter
(D)	150 mm dia Slotted Pipe	:- 24.00 Meter
	Total	:- 149.00 Meter
	A G L	:- 0.50 Meter
	B G L	:- 148.50 Meter
12-	Date of Lowering	:-02-10- 2022

PREPARED BY

(P. M.)
 LARSEN & TOUBRO
 LIMITED SITAPUR

(VERIFIED BY)
 (T.P.I.)

RECOMMENDED BY

(VIKRAM JEET)
 (JE)
 DIVISION OFFICE (E/M)
 U.P. JAL NIGAM (R) LUCKNOW

APPROVED BY

(RAJENDRA KUMAR)
 (A E)
 DIVISION OFFICE (E/M)
 U.P. JAL NIGAM (R) LUCKNOW

(SHRI RAM GUPTA)
 EXECUTIVE ENGINEER
 DIVISION OFFICE (E/M)
 U.P. JAL NIGAM (R) LUCKNOW

