


PROPOSED ASSEMBLY CHART OF TUBEWELL

NAME OF SCHEME : -ATAGAON GP WSS
NAME OF SITE : -ATAGAON
BLOCK : -MADHOGARH
NAME OF COMPANY : -BGCCPL
TYPE OF RIG M/C : -D.C.

DISTRICT : -JALAUN (ORAI)
SIZE OF BORE : -500 X 450 MM
SIZE OF ASSEMBLY : -200 X 150 MM
SPRING WATER LEVEL: -.....MTR

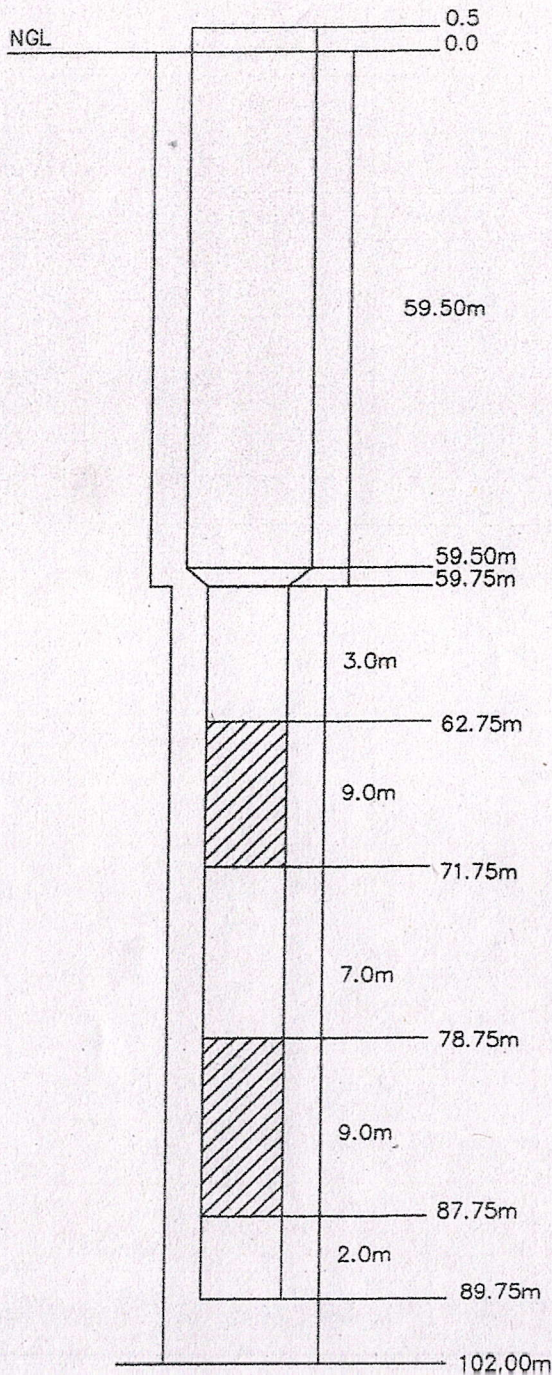

LOGGING DATE: - 03/06/2022

LPM REQUIRED: -420

Sr.N	Depth Range (M)	Thickness (M)	Remark
1			GOOD
2	62 TO 72	10	
3	78 TO 90	12	
4			
5			
6			
7			
8			
9			
10			

Abstract

1. Drilling completed on dt.....
2. Lowering on Dt.....
3. Drilling DepthM
4. 200 mm Dia Housing pipe.....M
5. 200x150 mm Dia reducer...0.25.M
6. 150 mm Dia Plain pipe.....M
7. 150 mm Dia Slotted Pipe.....M
8. Total Assy. Length.....M
9. Pea Gravel Quality.....



Proposed By

RECOMMENDED BY

JR. ENGINEER

ASS. ENGINEER

APPROVED BY

EXECUTIVE ENGINEER

CS2

M/S MAHALAXMI TUBE WELL

Geophysical Well Logging Report

Ref No- 1043

Date 10/06/2022

Site Location : - Village – Atagaon Madhougarh

District : - Jalaun

Logged Depth : - 90 M BGL


Date of Logging : - 09/05/2022

Types of Log : - S.P & Resistivity

Logger used : - IGIS

The following permeable granular zones have been deciphered with the help of Electrical Logger.

Depth Range From M.B.G.L.	Depth Range M.B.G.L.	Thickness Mtrs.	Inferred Litho logy	Quality of G.W.
0	40	40	Surface Clay With Sandy Kankar	
40	48	08	Sandy Kankar	Good
48	62	14	Clay Kankar	
62	72	10	Fine to Medium sand	Good
72	78	06	Clay Kankar	
78	90	12	Fine to Medium sand	Good



M/s Mahalaxmi Tube Well

Prop

YIELD TEST REPORT				
NAME OF SCHEME		270 Tabacoell Scheme-		
LOCATION OF T/W		Akagaon, madhogach		
REQUIRED DISCHARGE AS PER SCHEME		420		
DATE OF TESTING				
TASTE OF WATER		Sweet		
PHYSICAL WATER QUALITY		Good		
S.No.	S.W.L. IN MTR.	R.W.L. IN MTR.	DEPRESSION IN MTR.	DISCHARGE IN LPM
	22	25	3	1100
REMARKS:-				
RECOMMENDED DISCHARGE				
 BGCC		 NAME OF SWSM/JALNIGAM /PMC/TPI ENGINEER		
		SIGNATURE OF SWSM/JALNIGAM /PMC/TPI ENGINEER		

DATE OF TEST:-		Village: Akagaon		DISCHARGE		ST.PR.
INC	LPM	KG/CM ²				
		5.80				
		8.51				
		8.30				
		11.90				

Note: Recommended for further development



YIELD TEST REPORT BT 250 P.S.I COMPRESSOR

DATE OF TEST:-

STATIC W/L

TEST OF WATER

Sweet

Village: Alaggaon

DISCHARGE

INC

LPM

ST.PR.

KG/CM²

RU PR

KG/CM²

Depre

KG

MTR

SAND CONTENTS

START

5 MIN

10 MIN

15 MIN

20 MIN

25 MIN

REMARKS

Note: Recommended for further development by O.P. Unit.



Signature: T.P.T.
