


(71)

COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. KATHAWA G.P W/S SCHEME BLOCK SIDHAULI DISTRICT SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 106 /ED/21-22.....DATED 10 AUGUST 021
 LOWERED ASSEMBLY CHART OF T.W. OF KATHAWA G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT. 500 MM DIA BORE

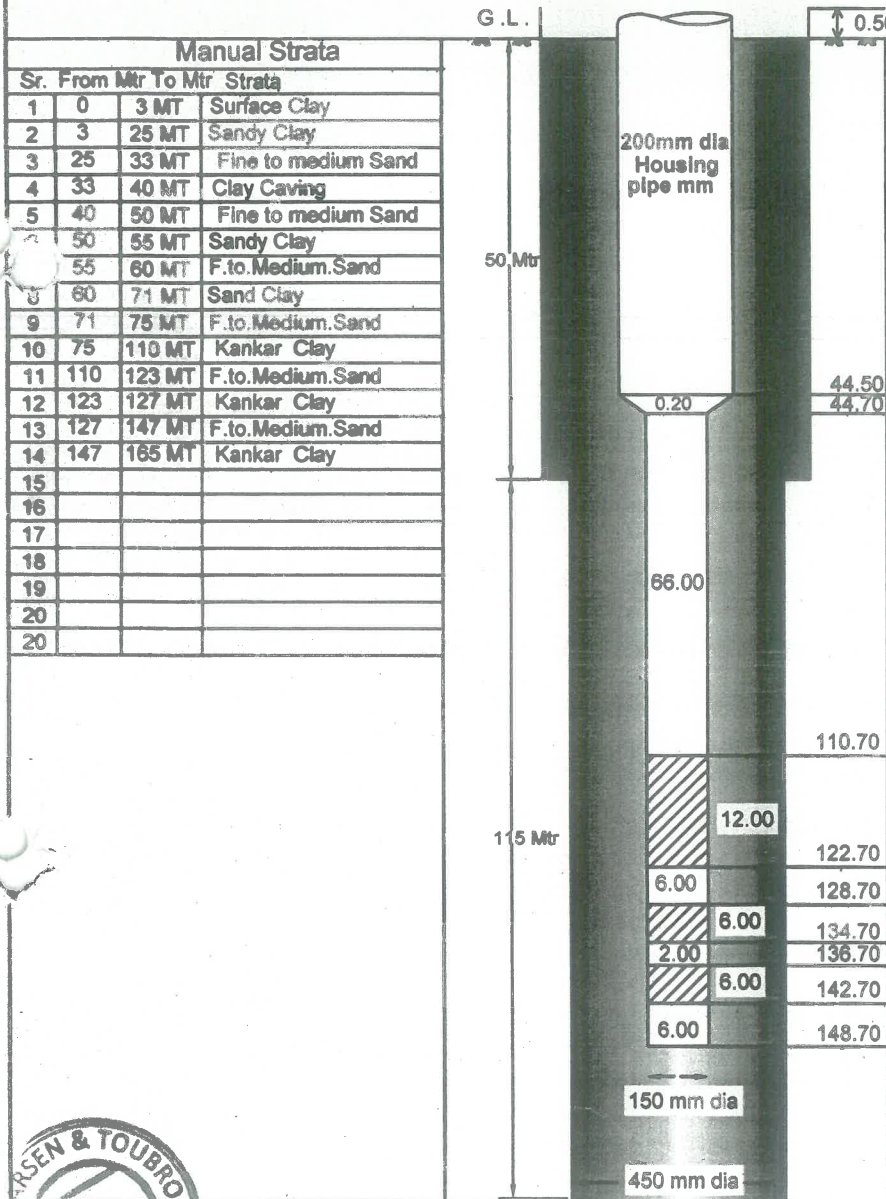

ABSTRACT	
1- Required Discharge	:- 600 LPM
2- Static Water Level	:- 12 MTR
3- Type of Rig Machine	:- R.C./D.C
4- Bore Size	:- 500x450 mm dia
5- Assembly size	:- 200 x150 mm dtr
6- Total Depth of Bore	:- 170 Mtr
a- 500 mm dia o to 50	:- 50.00 m.
b- 200 mm dia 51 to 165	:- 120.00 m.
Total	:- 170.00 m.
7- Logging date	:- 09-06-2022
8- Logging Depth	:- 165.00 m.

LOGGING REPORT


Sr.	Depth Range	Mbgi	Thickness m.	Remarks
1	25 - 33		8.00 m	Good
2	40 - 50		10.00 m	Good
3	55 - 60		5.00 m	Good
4	71 - 75		4.00 m	Good
5	110 - 123		13.00 m	Good
6	127 - 147		20.00 m	Good
7				
8				
9				
10				

11- Detail of Tubewell Assembly

(A) 200 mm dia Housing Pipe	:- 45.00 Meter
(B) 200x150 mm dia MS Reducer	:- 0.20 Meter
(C) 150 mm dia MS Plain Pipe	:- 80.00 Meter
(D) 150 mm dia Slotted Pipe	:- 24.00 Meter
Total	:- 149.20 Meter
A G L	:- 0.50 Meter
B G L	:- 148.70 Meter
12- Date of Lowering	:- 13/06/2022



PREPARED BY
 (P.M.)
 LARSEN AND TOUBRO
 LIMITED SITAPUR



RECOMMENDED BY
 Vilekam Jeet
 (J E)
 DIVISIONAL OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW

(DINESH KUMAR)
 (A E)
 DIVISIONAL OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW

APPROVED BY
 (VISHAL ARYA)
 EXECUTIVE ENGINEER
 DIVISIONAL OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW
