


COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. KURSANDA G.P W/S SCHEME BLOCK KASMANDA DISTRICT :- SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 206 /ED/21-22/1111 DATED 08-12-2021
 LOWERED ASSEMBLY CHART OF T.W. OF KURSANDA G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT. 600 MM DIA BORE

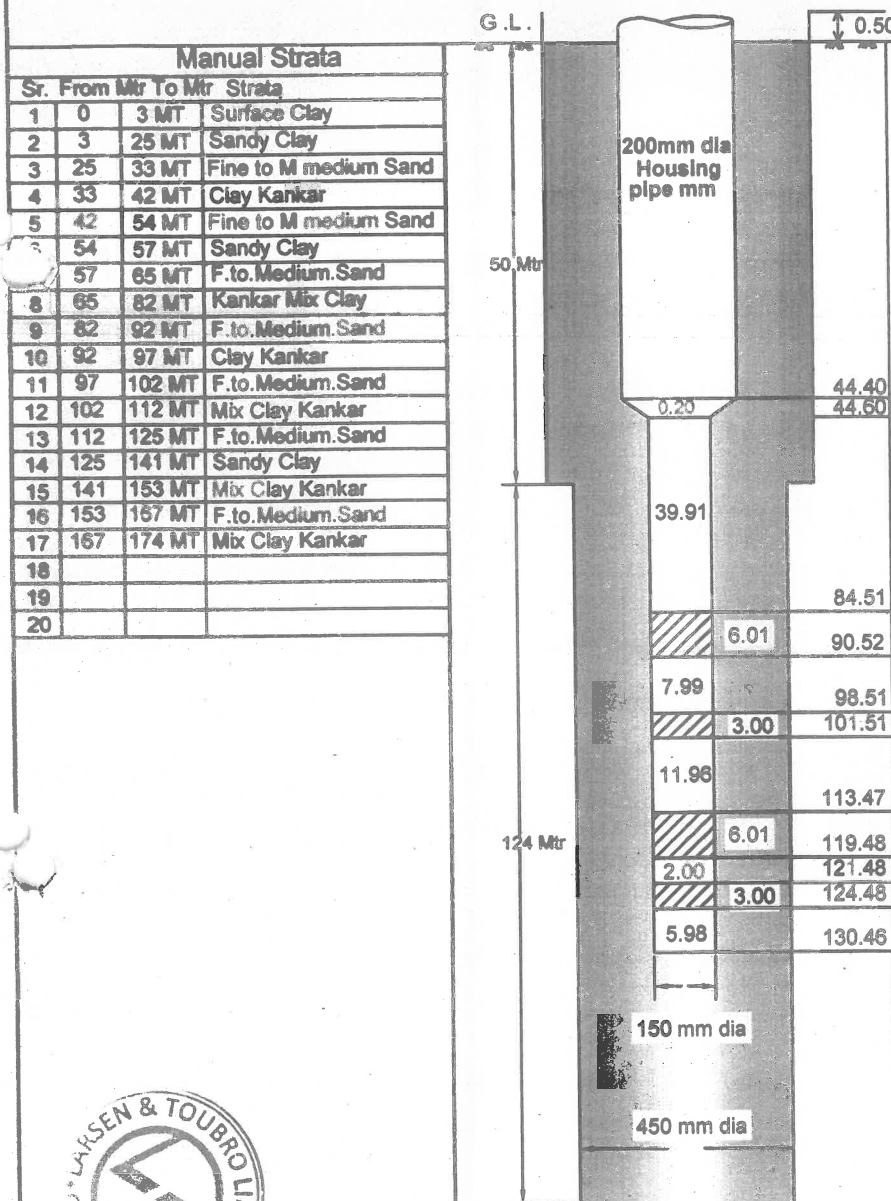

ABSTRACT	
1- Required Discharge	:- 320..LPM
2- Static Water Level	:- 8 mtd
3- Type of Rig Machine	:- R.C.D.C
4- Bore Size	:- 500x450 mm dia
5- Assembly size	:- 200 x150 mm dtr
6- Drilling Started on Date	:-
7- Total Depth of Bore	:-
a- 500 mm dia o to 50	:- 50.00 m.
b- 200 mm dia 51 to 124	:- 124.00 m.
Total	:- 174.00 m.
8- Logging date	:- 18-04-2022
9- Logging Depth	:- 174.00 m.

LOGGING REPORT

Sr.	Depth Range	Mbgi	Thickness m.	Remarks
1	25 - 33		8.00 m	Good
2	42 - 54		12.00 m	Good
3	57 - 65		8.00 m	Good
4	82 - 92		10.00 m	Good
5	97 - 102		5.00 m	Good
6	112 - 125		13.00 m	Good
7	141 - 153		12.00 m	Good
8	167 - 175		8.00 m	Good

BY W/S GEO INSTRUMENTS & TECHNIC'S - LKO

11- Detail of Tubewell Assembly	
(A) 200 mm dia Housing Pipe	:- 44.90 Meter
(B) 200x150 mm dia MS Reducer	:- 0.20 Meter
(C) 150 mm dia MS Plain Pipe	:- 67.84 Meter
(D) 150 mm dia Slotted Pipe	:- 18.02 Meter
Total	:- 130.96 Meter
A G L.	:- 0.50 Meter
B G L	:- 130.46 Meter
12- Date of Lowering	:- 19.4.22

PREPARED BY
 (P.M.)
 LARSEN AND TOUBRO
 LIMITED SITAPUR

RECOMMENDED BY
 Geet
 (VERIFIED BY)
 (T.P.I.)
 DIVISIONAL OFFICE (E/M)
 U.P. JAL NIGAM (R) LUCKNOW

APPROVED BY
 (DINESH KUMAR)
 (A.E.)
 DIVISIONAL OFFICE (E/M)
 U.P. JAL NIGAM (R) LUCKNOW

APPROVED BY
 (VISHAL ARYA)
 EXECUTIVE ENGINEER
 DIVISIONAL OFFICE (E/M)
 U.P. JAL NIGAM (R) LUCKNOW
