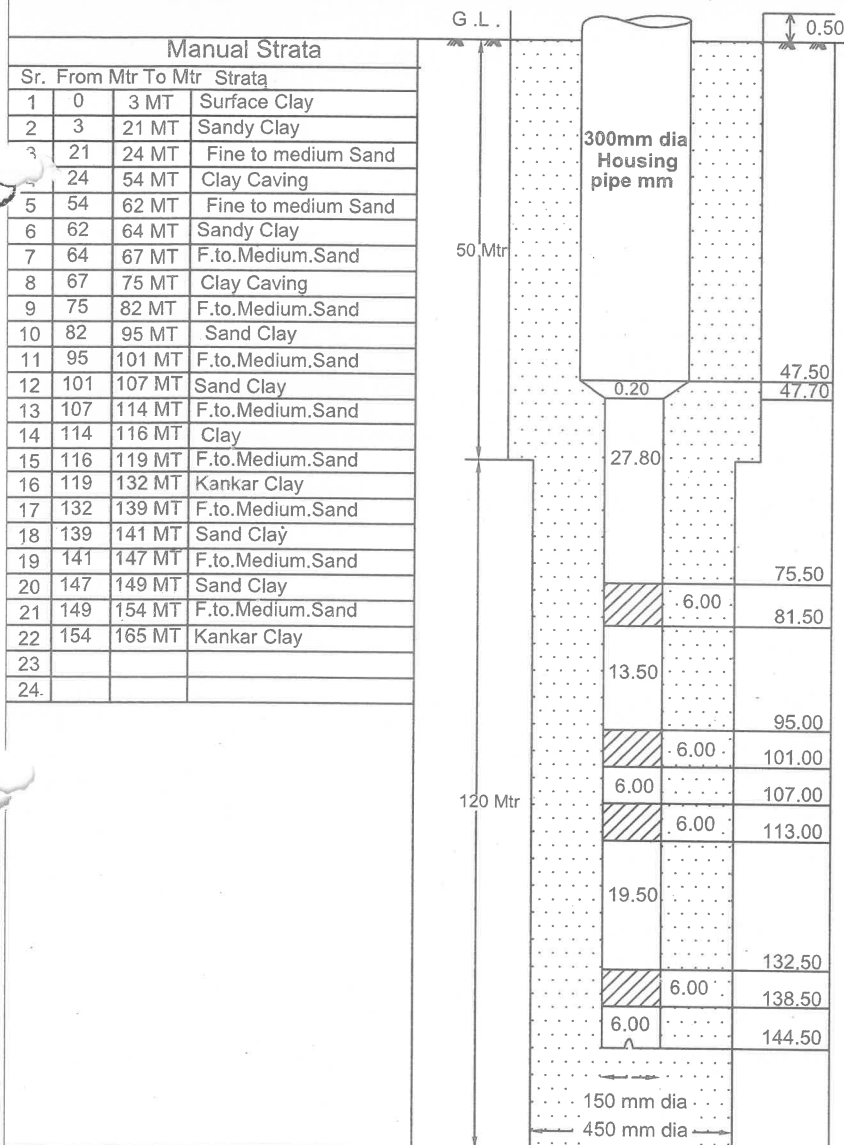


(147)

COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. KUWARPUR G.P W/S SCHEME BLOCK SIDHAULI DISTRICT SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 225 /ED/21-22/ V / DATE / 30/12/2021
 LOWERED ASSEMBLY CHART OF T.W. OF KUWARPUR G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT. 600 MM DIA BORE

**ABSTRACT**

1- Required Discharge	:- 640 LPM
2- Static Water Level	:- 10 MTR
3- Type of Rig Machine	:- R.C./D.C
4- Bore Size	:- 600x450 mm dia
5- Assembly size	:- 300x150 mm dtr
6- Total Depth of Bore	:- 165 Mtr
a- 600 mm dia o to 50	:- 50.00 m.
b- 300 mm dia 50 to 165	:- 115.00 m.
Total	:- 165.00 m.
7- Logging date	:- 13-10-2022
8- Logging Depth	:- 165.00 m.

LOGGING REPORT

Sr.	Depth Range Mbg	Thickness m.	Remarks
1	21 - 24	3.00 m	Good
2	54 - 62	08.00 m	Good
3	64 - 67	3.00 m	Good
4	75 - 82	07.00 m	-6 Good
5	95 - 101	06.00 m	-6 Good
6	107 - 114	07.00 m	-6 Good
7	116 - 119	3.00 m	Good
8	132 - 139	07.00 m	-6 Good
9	141 - 147	6.00 m	Good
10	149 - 154	5.00 m	Good
11			

11- Detail of Tubewell Assembly

(A) 300 mm dia Housing Pipe	:- 48.00 Meter
(B) 300x150 mm dia MS Reducer	:- 0.20 Meter
(C) 150 mm dia MS Plain Pipe	:- 72.80 Meter
(D) 150 mm dia Slotted Pipe	:- 24.00 Meter
Total	:- 145.00 Meter
A G L	:- 0.50 Meter
B G L	:- 144.50 Meter
12- Date of Lowering	14-10-2022

PREPARED BY

(Signature)
 (P . M .)
 LARSEN AND TOUBRO
 LIMITED SITAPUR

RECOMMENDED BY

(Signature)
 (VIKRAM JEET)
 (J E)
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW

APPROVED BY

(Signature)
 (SHRI RAM GUPTA)
 EXECUTIVE ENGINEER
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW
