

Gayatri Phase - II

Proposed Tubewell Assembly chart of **Mohana**
District - Amethi

Drilling/Lowering - 400/380m
T.W. Asse. Size - 300X150mm.
Housing (Plan Pipe) - 66m
Housing (Slotted Pipe) -

W/S Scheme Block - Bahadurpur

Bore Size - 600X500mm.
Recommended Discharge - 1050 LPM
Plan Pipe - 272m
Slotted Pipe - 42m

Logging Report - 05/01/24
1- 15 - 21 $\Rightarrow$ 06 Good

2- 26 - 30 $\Rightarrow$ 04 n

3- 32 - 36 $\Rightarrow$ 04 n

4- 43 - 47 $\Rightarrow$ 04 n

5- 56 - 59 $\Rightarrow$ 03 n


6- 185 - 193 $\Rightarrow$ 08 Good to Moderate

7- 200 - 209 $\Rightarrow$ 09 n n

8- 245 - 250 $\Rightarrow$ 05 n n

9- 287 - 295 $\Rightarrow$ 08 n n

10- 316 - 320 $\Rightarrow$ 04 Moderate

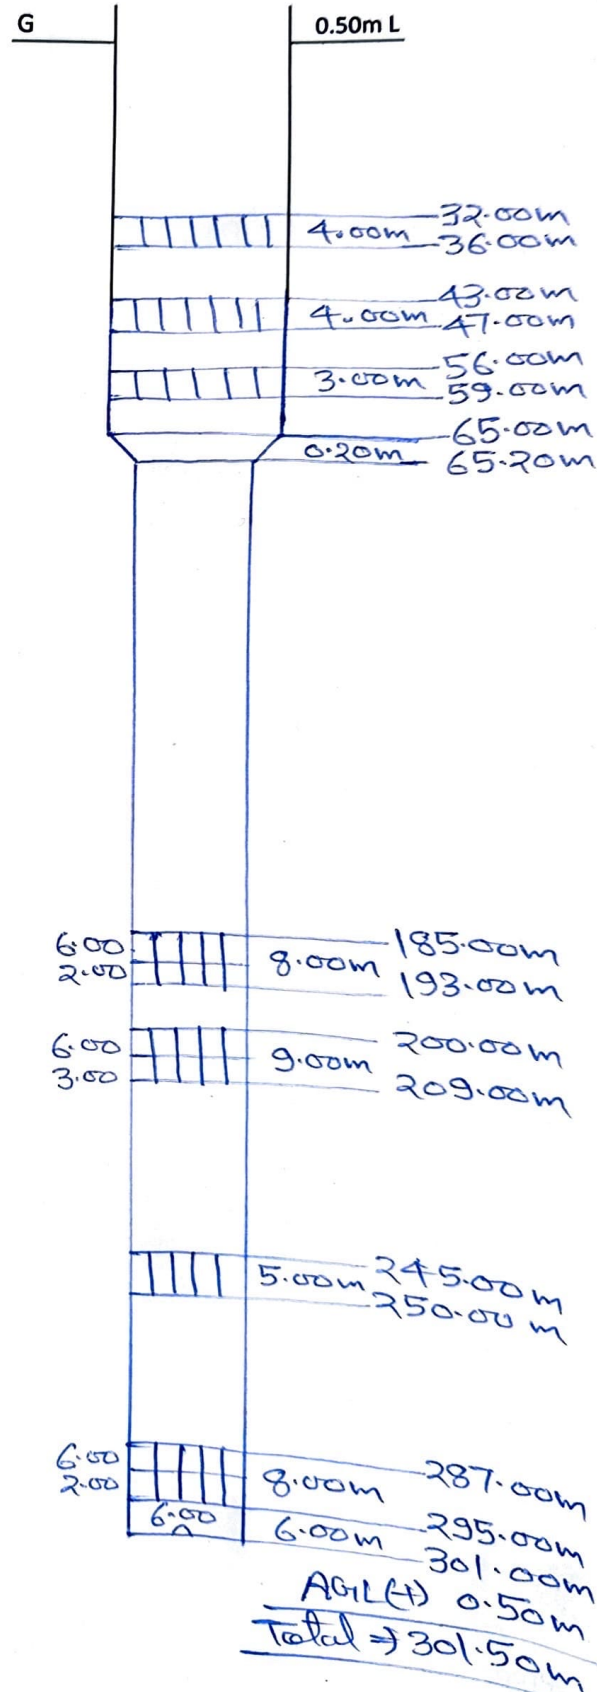

Prepared by
A.E.
(Sampuranand)
A.E.

Approved by
(Mohd. Maaz)
E.E.
