


OFFICE OF THE EXECUTIVE ENGINEER, CONSTRUCTION DIVISION(E&M), U.P. JAL NIGAM, GONDA

Completion plan of **KHANPUR T.W.** District **GONDA**
 Type of Rig M/c **R.C. RIG MACHINE** Size of Bore **600X500mm**
 Size of Assembly **250X150mm** Name of Contractor **M/S Sai Enterprises Bareilly**
 Static Water Level **3 mty**

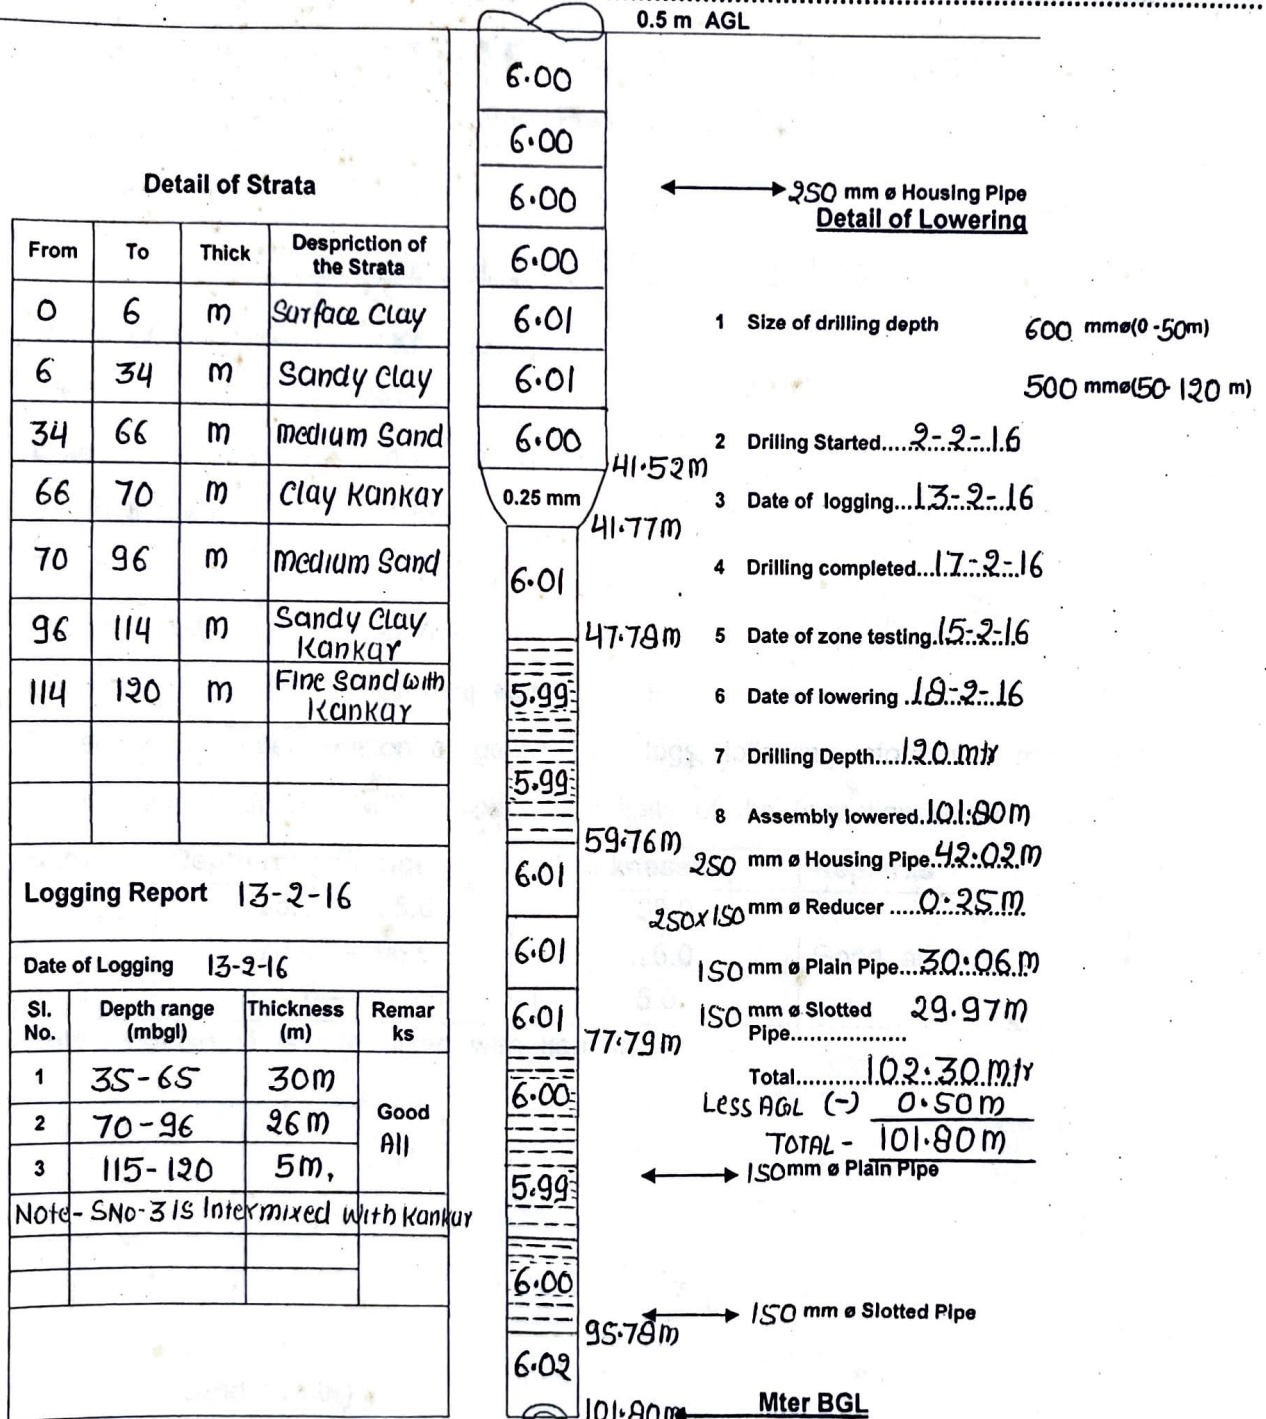

(RAJ KUMAR)
Junior Engineer

(S.K. KARNADHAR)
Assistant Engineer

(R.K. SINGH)
Executive Engineer



Telephone 0522- 2230712
FAX 0522- 2625586

UTTAR PRADESH JAL NIGAM

6, Rana Pratap Marg, Lucknow-226001

Ref.

Geophysical Borehole Logging Report

Name of the site : Khanpur
District : Gonda
Date : 13.02.2016
Depth logged : 120.0 mbgl
Depth drilled : 125.0 mbgl
Logger used : AXWS
Presence : Er. Raj Kumar , J.E.

Based on the interpretation of geophysical logs, following information may be deciphered, particularly with respect to salinity of the formation water.

Sl.No.	Depth range(mbgl)	Thickness(m)	Remarks
1	35.0-----65.0	30.0	Good all
2	70.0-----96.0	26.0	
3	115.0-----120.0	5.0	

Note. Sl.No. 3 is intermixed with kankar.

(Dr.R.A.Yadav)

Manager(Ground Water)

Copy;

1. C.E.(E/M), U.P.Jal Nigam, Lucknow.
2. E.E., C.D.(E/M), U.P.Jal Nigam, Gonda
for information and necessary action.
