


OFFICE OF THE EXECUTIVE ENGINEER, CONSTRUCTION DIVISION(E&M), U.P. JAL NIGAM, GONDA

Completion plan of **SISOOR ANDUPUR T.W.** District **GONDA**
 Type of Rig M/c **RC. RIG MACHINE** Size of Bore **600 X 500 mm**
 Size of Assembly **250 X 150 mm** Name of Contractor **M/S. Sai Enterprises Bareilly**
 Static Water Level **5 mtr**

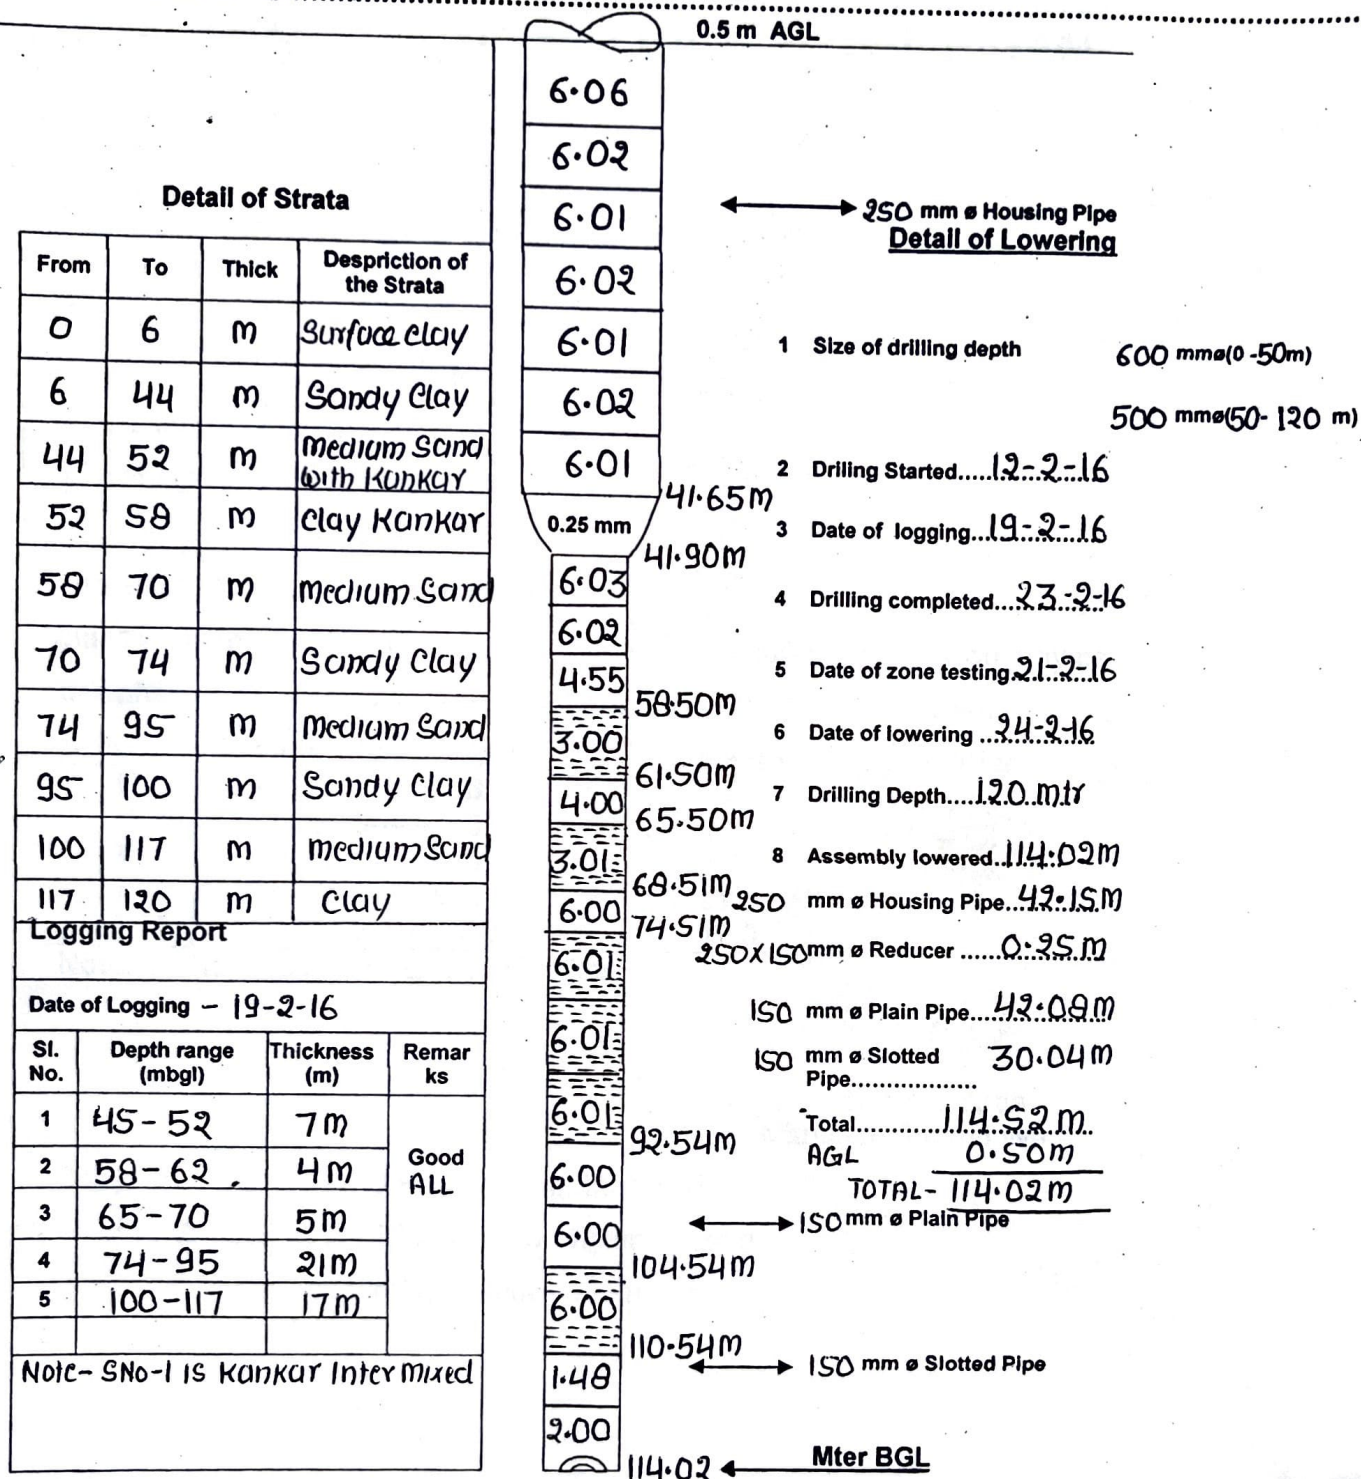

(RAJ KUMAR)
Junior Engineer

(S.K. KARNADHAR)
Assistant Engineer

(R.K. SINGH)
Executive Engineer



Telephone 0522- 2230712
FAX 0522- 2625586

UTTAR PRADESH JAL NIGAM

6, Rana Pratap Marg, Lucknow-226001

Ref.

Geophysical Borehole Logging Report

Name of the site : Sisour Andupur

District : Gonda

Date : 19.02.2016

Depth logged : 124.0 mbgl

Depth drilled : 125.0 mbgl

Logger used : AXWS

Presence : Er. Raj Kumar, J.E.

Based on the interpretation of geophysical logs, following information may be deciphered, particularly with respect to salinity of the formation water.

Sl.No.	Depth range(mbgl)	Thickness(m)	Remarks
1	45.0----52.0	7.0	Good all
2	58.0----62.0	4.0	
3	65.0----70.0	5.0	
4	74.0----95.0	21.0	
5	100.0----117.0	17.0	

Note. Sl. No. 1 is intermixed with kankar.

(Dr.R.A.Yadav)
Manager(Ground Water)

Copy; 1. C.E.(E/M), U.P.Jal Nigam, Lucknow.
2. E.E., C.D.(E/M), U.P.Jal Nigam, Gonda
for information and necessary action.
