


OFFICE OF THE EXECUTIVE ENGINEER, CONSTRUCTION DIVISION(E&M), U.P. JAL NIGAM, GONDA

Completion plan of NIGWA BODH T.W District..... GONDA
 Type of Rig M/c..... R.C. Rig m/c Size of Bore..... 600 x 500 mm
 Size of Assembly..... 250 x 150 mm Name of Contractor..... M/S. Sai Enterprises, Barcilly
 Static Water Level..... 5 mtr

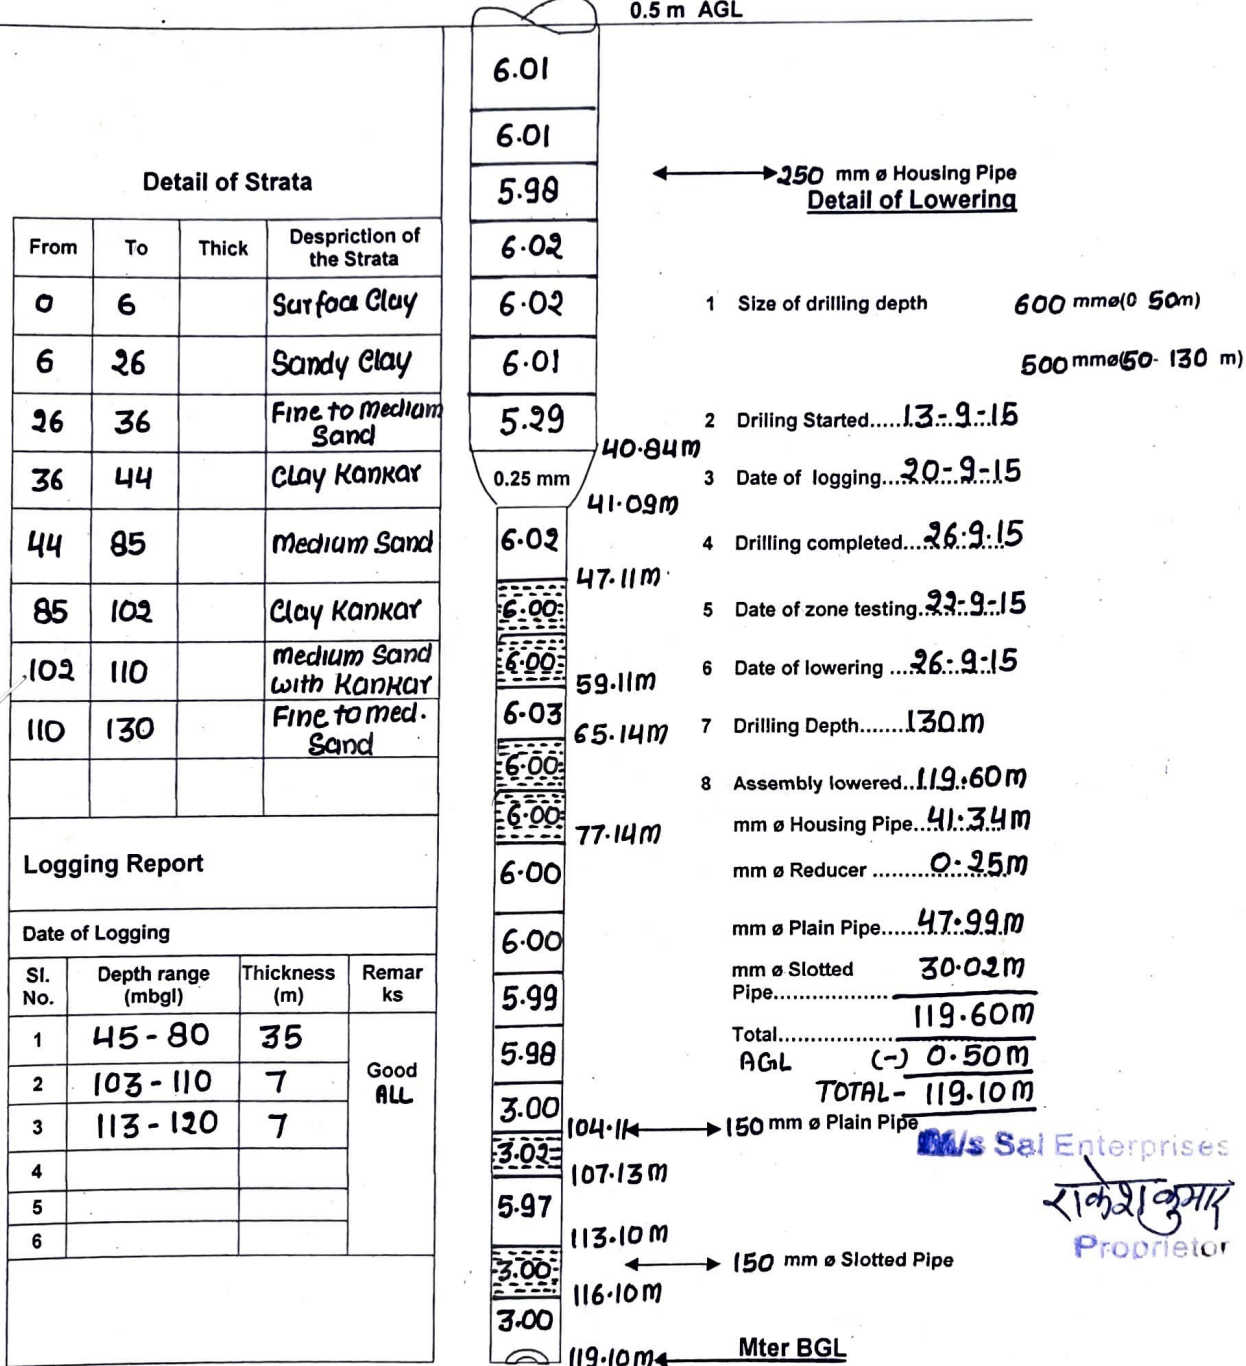

(RAJ KUMAR)
Junior Engineer

(S.K. KARNADHAR)
Assistant Engineer

(R.K. SINGH)
Executive Engineer



Telephone 0522- 2230712

FAX 0522- 2625586

UTTAR PRADESH JAL NIGAM

6, Rana Pratap Marg, Lucknow-226001

Ref.

Geophysical Borehole Logging Report

Name of the site : Nagwa Bodh

District : Gonda

Date : 20.09.2015

Depth logged : 125.0 mbgl

Depth drilled : 130.0 mbgl

Logger used : AXWS

Presence : Er. Raj Kumar, J.E.

Based on the interpretation of geophysical logs, following information may be deciphered, particularly with respect to salinity of the formation water.

Sl.No.	Depth range(mbgl)	Thickness(m)	Remarks
1	45.0-----80.0	35.0	Good all
2	103.0-----110.0	7.0	
3	113.0-----120.0	7.0	

Note.

(Dr.R.A.Yadav)
Manager(Ground Water)

Copy;

1. C.E.(E/M), U.P.Jal Nigam, Lucknow.
2. E.E., C.D.(E/M), U.P.Jal Nigam, Gonda
for information and necessary action.
