


OFFICE OF THE EXECUTIVE ENGINEER, CONSTRUCTION DIVISION(E&M), U.P. JAL NIGAM, GONDA

Completion plan of NAGWA T. W. District GONDA
 Type of Rig M/c R.G. RIG MACHINE Size of Bore 600x500mm
 Size of Assembly 250x150mm Name of Contractor M/S Sai Enterprises Bareilly
 Static Water Level 3 mtr

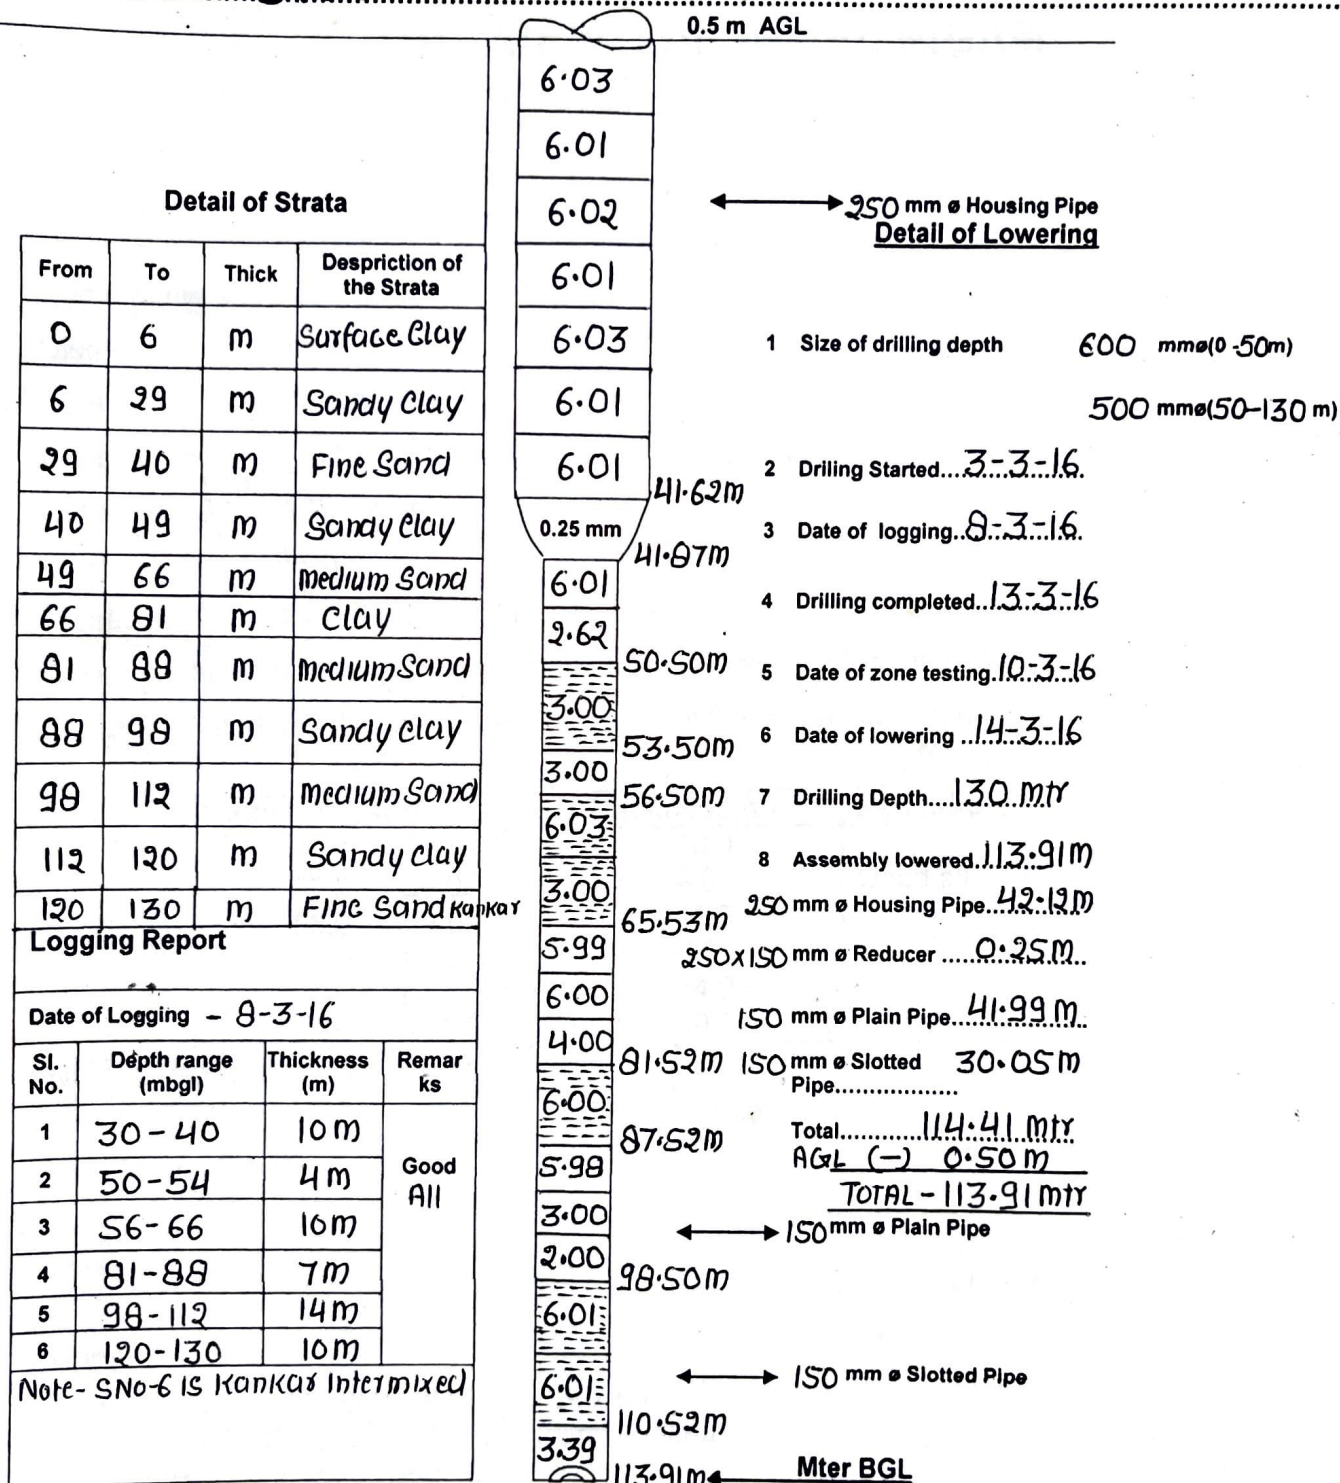

(RAJ KUMAR)
Junior Engineer

(S.K. KARNADHAR)
Assistant Engineer

(R.K. SINGH)
Executive Engineer



Telephone 0522- 2230712
FAX 0522- 2625586

UTTAR PRADESH JAL NIGAM

6, Rana Pratap Marg, Lucknow-226001

Ref.

Geophysical Borehole Logging Report

Name of the site : Nagwa - Nawabganj

District : Gonda

Date : 08.03.2016

Depth logged : 130.0 mbgl

Depth drilled : 135.0 mbgl

Logger used : AXWS

Presence : Er. Raj kumar, J.E.

Based on the interpretation of geophysical logs, following information may be deciphered, particularly with respect to salinity of the formation water.

Sl.No.	Depth range(mbgl)	Thickness(m)	Remarks
1	30.0-----40.0	10.0	Good all
2	50.0-----54.0	4.0	
3	56.0-----66.0	10.0	
4	81.0-----88.0	7.0	
5	98.0-----112.0	14.0	
6	120.0-----130.0	10.0	

Note. Sl.No. 6 is kankar intermixed.

(Dr.R.A.Yadav)
Manager(Ground Water)

Copy;

1. C.E.(E/M), U.P.Jal Nigam, Lucknow.
2. E.E., C.D.(E/M), U.P.Jal Nigam, Gonda
for information and necessary action.
