


OFFICE OF THE EXECUTIVE ENGINEER, CONSTRUCTION DIVISION(E&M), U.P. JAL NIGAM, GONDA

Completion plan of **BHITARA T.W.** District **GONDA**
 Type of Rig M/c **R.C. RIG MACHINE** Size of Bore **625x550 mm**
 Size of Assembly **300x200 mm** Name of Contractor **M/S. Sai Enterprises Bareilly**
 Static Water Level **3.5 mtr**

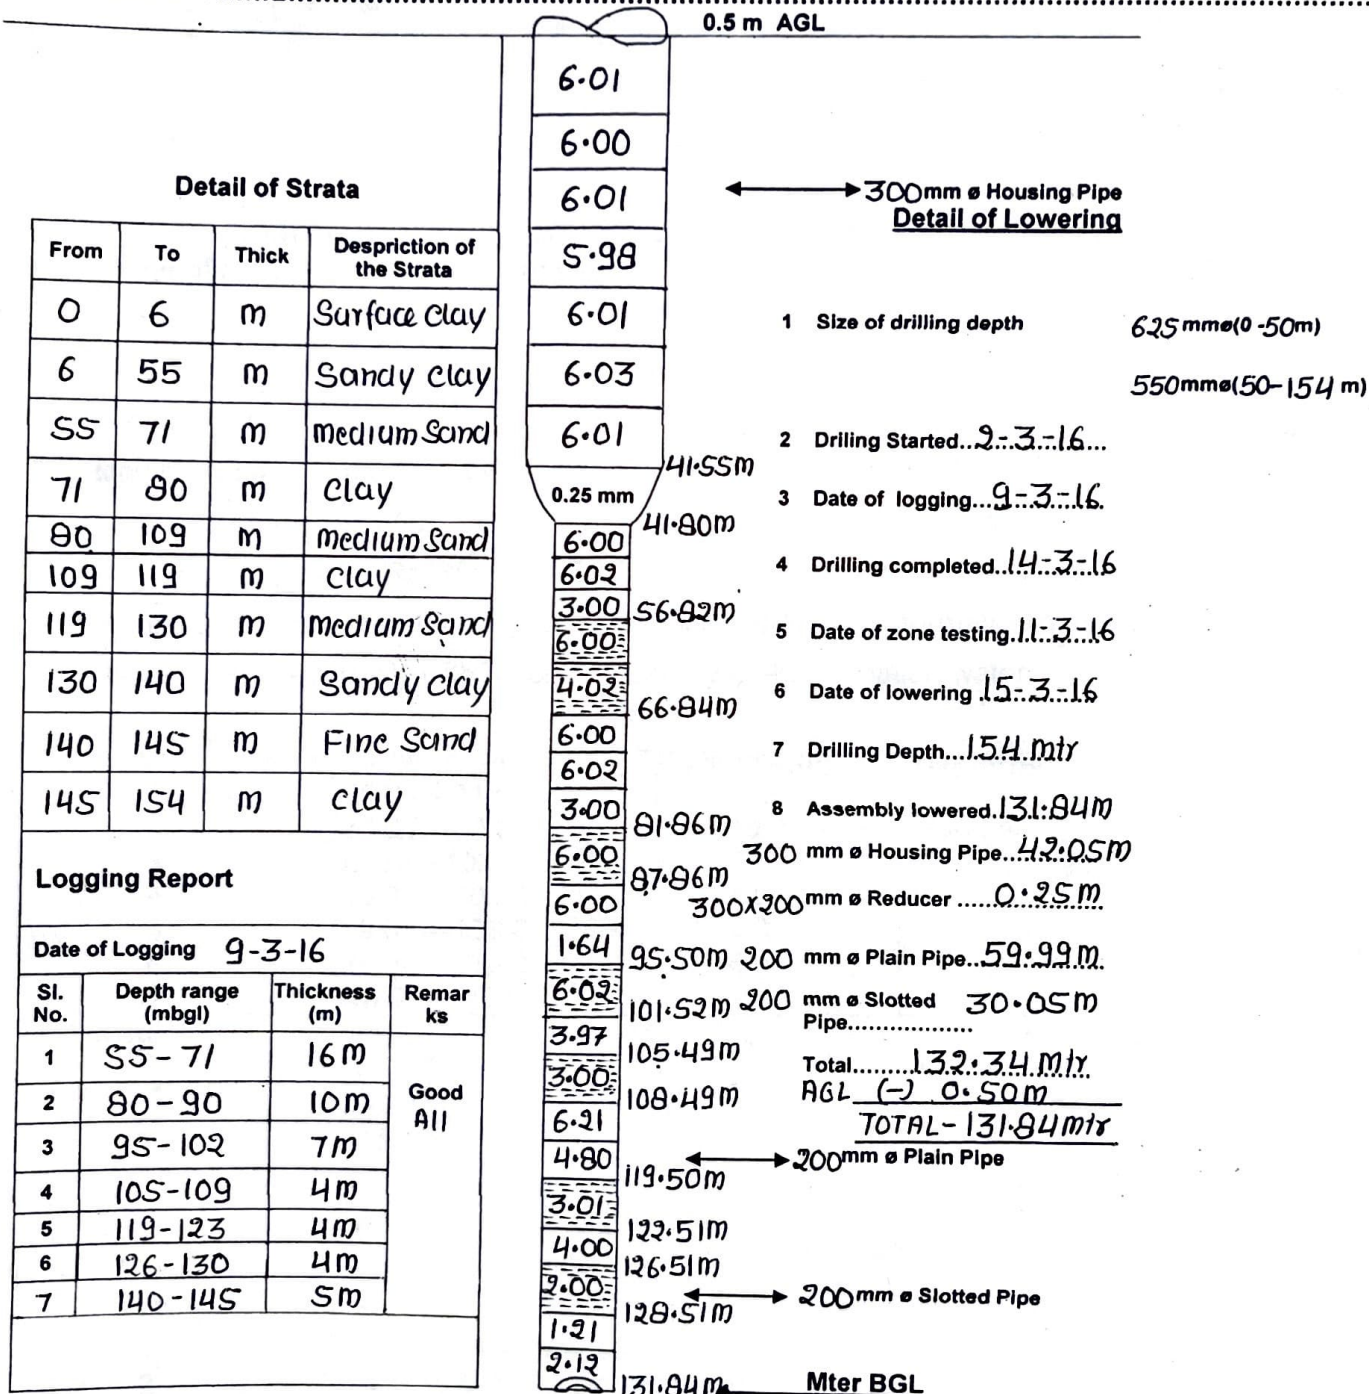

Raj Kumar
 (RAJ KUMAR)
 Junior Engineer

S.K. Karnadhar
 (S.K. KARNADHAR)
 Assistant Engineer

R.K. Singh
 (R.K. SINGH)
 Executive Engineer



Telephone 0522- 2230712
FAX 0522- 2625586

UTTAR PRADESH JAL NIGAM

6, Rana Pratap Marg, Lucknow-226001

Ref.

Geophysical Borehole Logging Report

Name of the site : Bhitaura - Mankapur

District : Gonda

Date : 09.03.2016

Depth logged : 153.0 mbgl

Depth drilled : 155.0 mbgl

Logger used : AXWS

Presence : Er. Raj kumar, J.E.

Based on the interpretation of geophysical logs, following information may be deciphered, particularly with respect to salinity of the formation water.

Sl.No.	Depth range(mbgl)	Thickness(m)	Remarks
1	55.0-----71.0	16.0	Good all
2	80.0-----90.0	10.0	
3	95.0-----102.0	7.0	
4	105.0-----109.0	4.0	
5	119.0-----123.0	4.0	
6	126.0-----130.0	4.0	
7	140.0-----145.0	5.0	

Note.

(Dr.R.A.Yadav)
Manager(Ground Water)

Copy;

1. C.E.(E/M), U.P.Jal Nigam, Lucknow.
2. E.E., C.D.(E/M), U.P.Jal Nigam, Gonda
for information and necessary action.
