


OFFICE OF THE EXECUTIVE ENGINEER, CONSTRUCTION DIVISION(E&M), U.P. JAL NIGAM, GONDA

Completion plan of **MADHAV PUR CHAKATTA T.W.** District **GONDA**
 Type of Rig M/c **R.C. RIG MACHINE** Size of Bore **600x500mm**
 Size of Assembly **250x150mm** Name of Contractor **M/s Sai Enterprises Bareilly**
 Static Water Level **3 Mtr.**

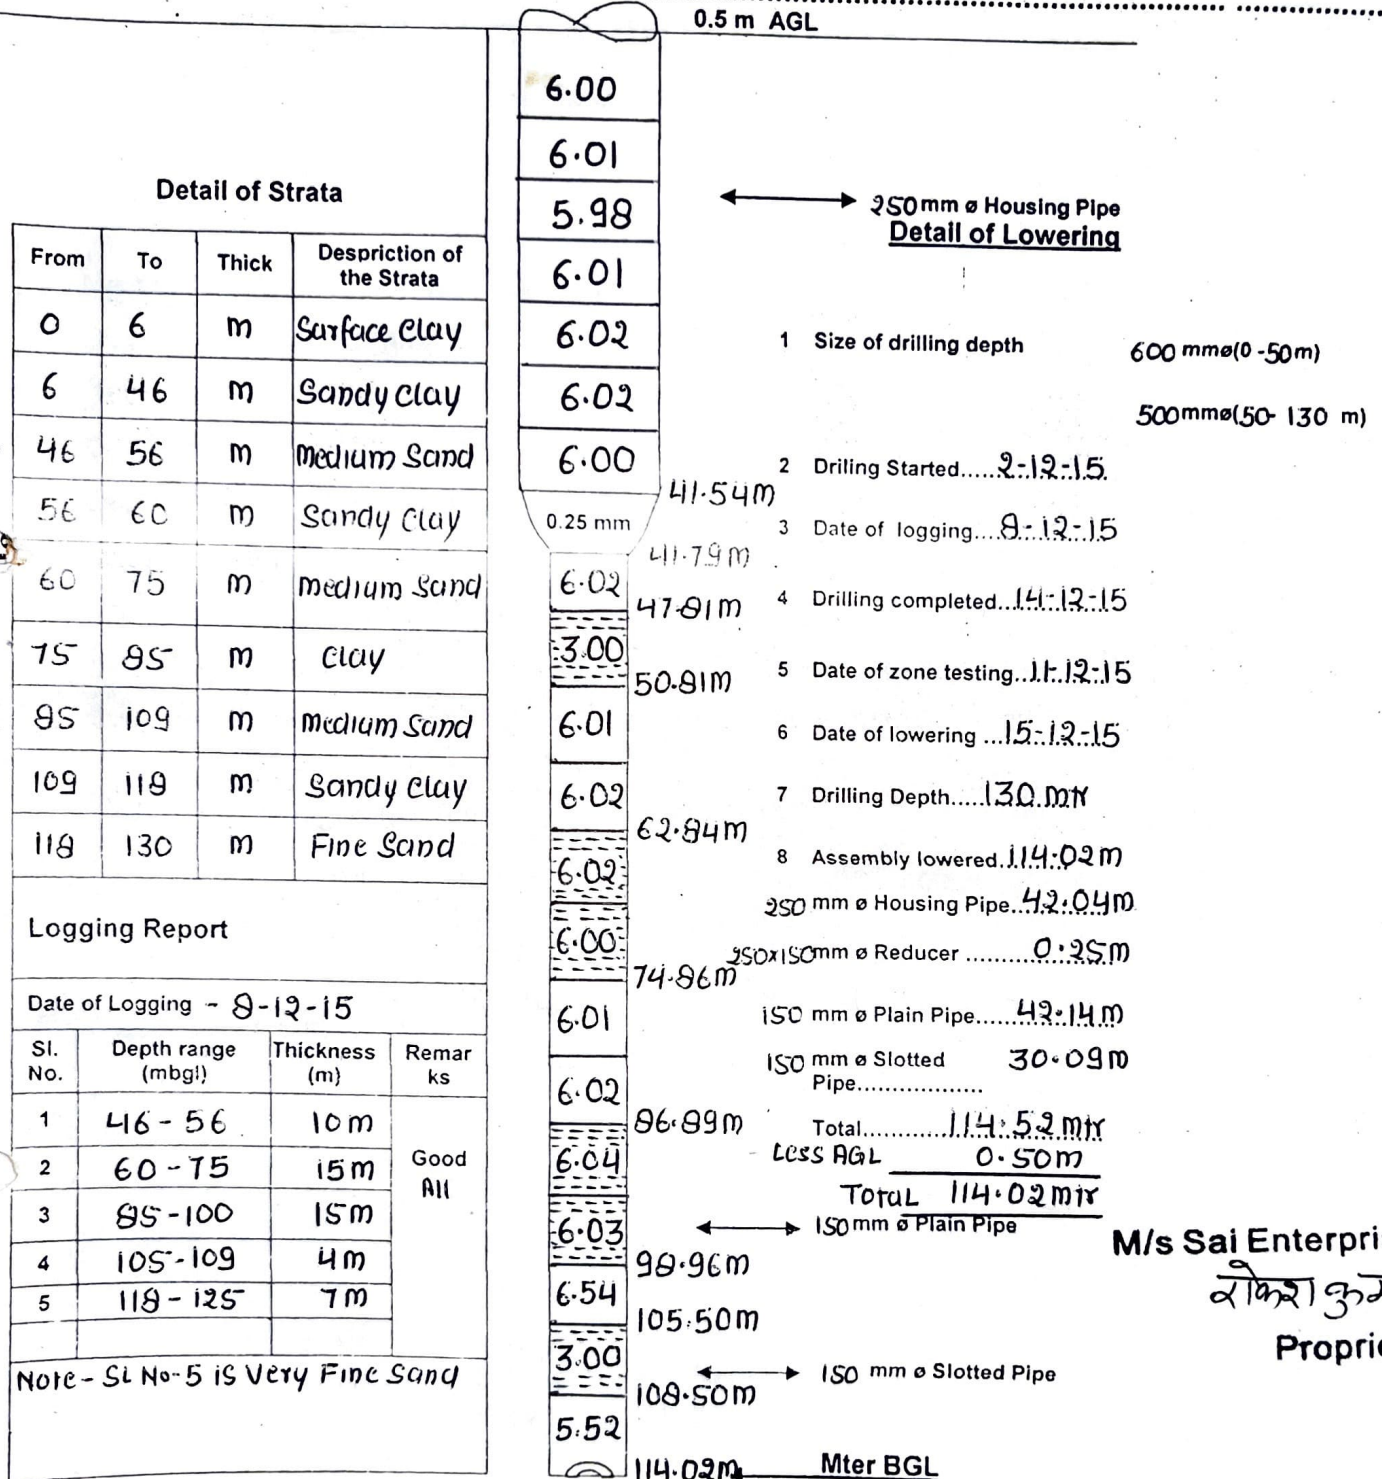

(RAJ KUMAR)
Junior Engineer

(S.K. KARNADHAR)
Assistant Engineer

(R.K. SINGH)
Executive Engineer



Telephone 0522- 2230712
FAX 0522- 2625586

UTTAR PRADESH JAL NIGAM

6, Rana Pratap Marg, Lucknow-226001

Ref.

Geophysical Borehole Logging Report

Name of the site : Madhavpur Chakatta

District : Gonda

Date : 08.12.2015

Depth logged : 125.0 mbgl

Depth drilled : 130.0 mbgl

Logger used : AXWS

Presence : Er. Raj Kumar, J.E.

Based on the interpretation of geophysical logs, following information may be deciphered, particularly with respect to salinity of the formation water.

Sl.No.	Depth range(mbgl)	Thickness(m)	Remarks
1	46.0----56.0	10.0	Good all
2	60.0----75.0	15.0	
3	85.0----100.0	15.0	
4	105.0----109.0	4.0	
5	118.0----125.0	7.0	

Note. Sl.No.5 is very fine sand.

(Dr.R.A.Yadav)
Manager(Ground Water)

Copy;

1. C.E.(E/M), U.P.Jal Nigam, Lucknow.
2. E.E., C.D.(E/M), U.P.Jal Nigam, Gonda
for information and necessary action.
