


Completion plan of **MUSAULI T.W.** District **GONDA**
 Type of Rig M/c **R.C. RIG MACHINE** Size of Bore **600x500mm**
 Size of Assembly **250x150mm** Name of Contractor **M/S. SAI ENTERPRISES BAREILLY**
 Static Water Level **4 MTR**

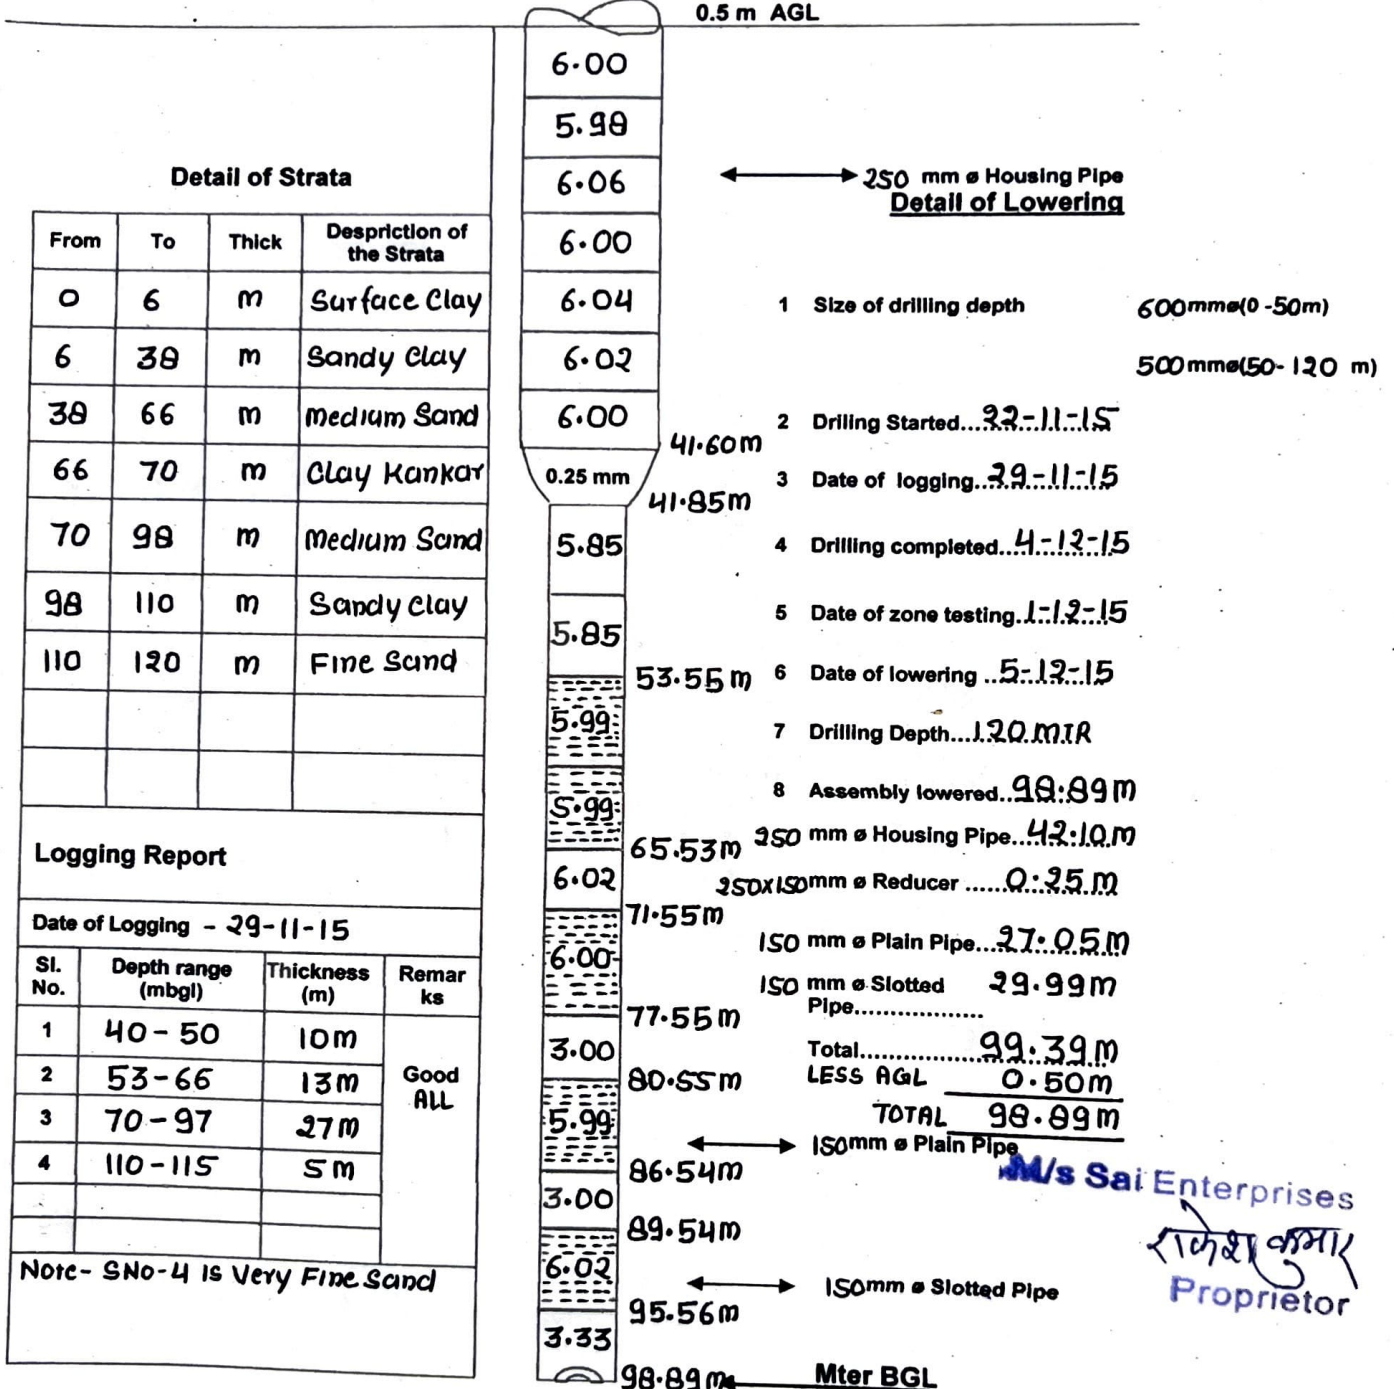

(RAJ KUMAR)
 Junior Engineer

(S.K. BARNADHAR)
 Assistant Engineer

(R.K. SINGH)
 Executive Engineer



Telephone 0522- 2230712
FAX 0522- 2625586

UTTAR PRADESH JAL NIGAM

6, Rana Pratap Marg, Lucknow-226001

Ref.

Geophysical Borehole Logging Report

Name of the site : Musauli

District : Gonda

Date : 29.11.2015

Depth logged : 119.0 mbgl

Depth drilled : 120.0 mbgl

Logger used : AXWS

Presence : Er. Raj Kumar, J.E.

Based on the interpretation of geophysical logs, following information may be deciphered, particularly with respect to salinity of the formation water ;

Sl.No.	Depth range(mbgl)	Thickness(m)	Remarks
1	40.0----50.0	10.0	Good all
2	53.0----66.0	13.0	
3	70.0----97.0	27.0	
4	110.0----115.0	5.0	

Note. Sl.No. 4 is very fine sand.

(Dr.R.A.Yadav)
Manager(Ground Water)

Copy;

1. C.E.(E/M), U.P.Jal Nigam, Lucknow.
2. E.E., C.D.(E/M), U.P.Jal Nigam, Gonda
for information and necessary action.
