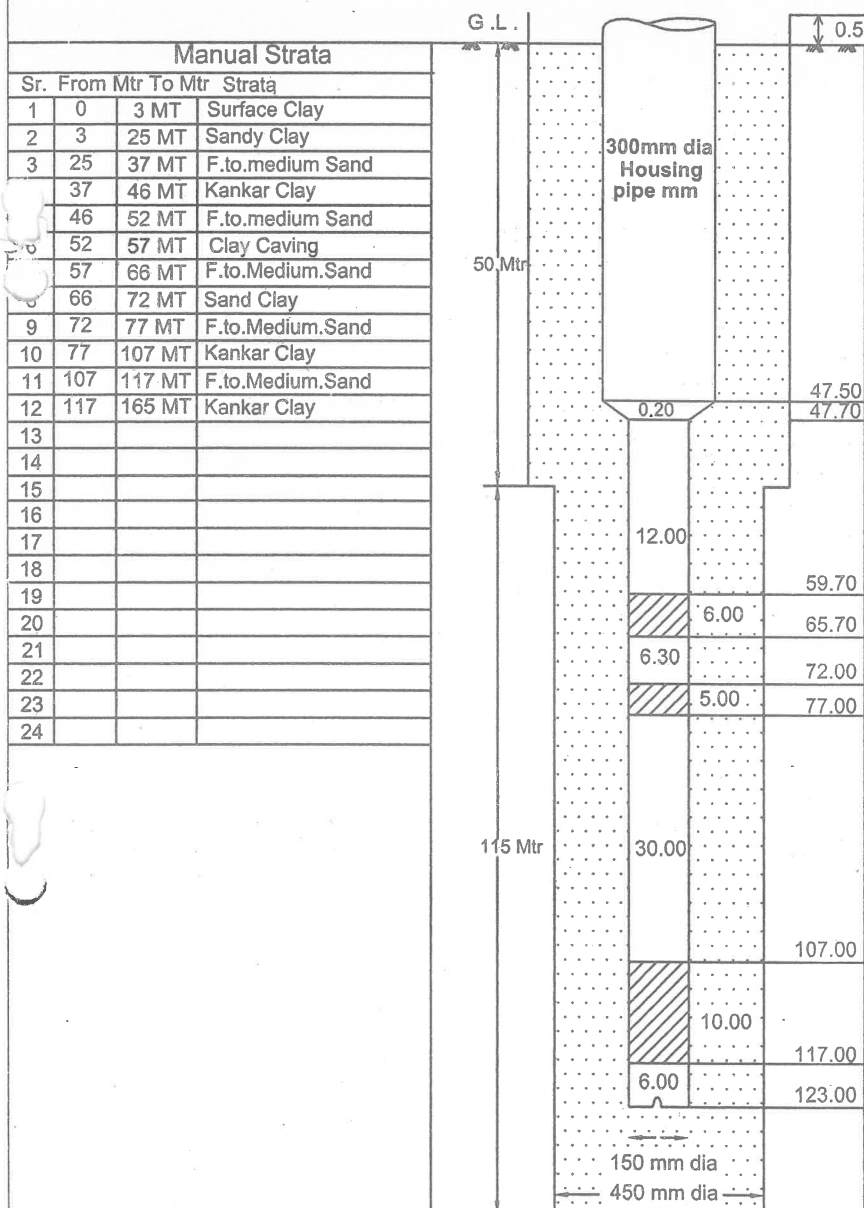


(174)

COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. LODHAURA G.P W/S SCHEME BLOCK MISHRIKH DISTRICT SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 115 / ED / PHASE - 2 / 22-23/ VIII...DATED 21 - 09 - 2022
 LOWERED ASSEMBLY CHART OF T.W. OF LODHAURA G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT. 600 MM DIA BORE

**ABSTRACT**

1- Required Discharge :- 630 LPM
 2- Static Water Level :- 10 MTR
 3- Type of Rig Machine :- R.C./D.C
 4- Bore Size :- 600x450 mm dia
 5- Assembly size :- 300x150 mm dtr
 6- Total Depth of Bore :- 165 Mtr
 a- 600 mm dia o to 50 :- 50.00 m.
 b- 300 mm dia 50 to 165 :- 115.00 m.
 Total :- 165.00 m.
 7- Logging date :- 29-11-2022
 8- Logging Depth :- 165.00 m.

LOGGING REPORT

Sr.	Depth Range Mbgl	Thickness m.	Remarks
1	25 - 37	12.00 m	Good
2	46 - 52	6.00 m	Good
3	57 - 66	9.00 m	Good
4	72 - 77	5.00 m	Good
5	107 - 117	10.00 m	Good
6			
7			
8			
9			
10			
11			

11- Detail of Tubewell Assembly

(A) 300 mm dia Housing Pipe :- 48.00 Meter
 (B) 300x150 mm dia MS Reducer :- 0.20 Meter
 (C) 150 mm dia MS Plain Pipe :- 54.30 Meter
 (D) 150 mm dia Slotted Pipe :- 21.00 Meter
 Total :- 123.50 Meter
 A G L :- 0.50 Meter
 B G L :- 123.00 Meter
 12- Date of Lowering :- 01-12-2022

PREPARED BY

(P.M.)

LARSEN AND TOUBRO
LIMITED SITAPUR

RECOMMENDED BY

(VIKRAM JEET)
(J.E)

DIVISION OFFICE (E/M)
U.P JAL NIGAM (R) LUCKNOW

APPROVED BY

(RAJENDRA KUMAR)
(A.E)

DIVISION OFFICE (E/M)
U.P JAL NIGAM (R) LUCKNOW

(SHRI RAM GUPTA)
EXECUTIVE ENGINEER

DIVISION OFFICE (E/M)
U.P JAL NIGAM (R) LUCKNOW
